





BOTSWANA - BOTASH REFURBISHMENT PROJECT 2023 - UTILITY PLANT

Update:- 16 May 2023



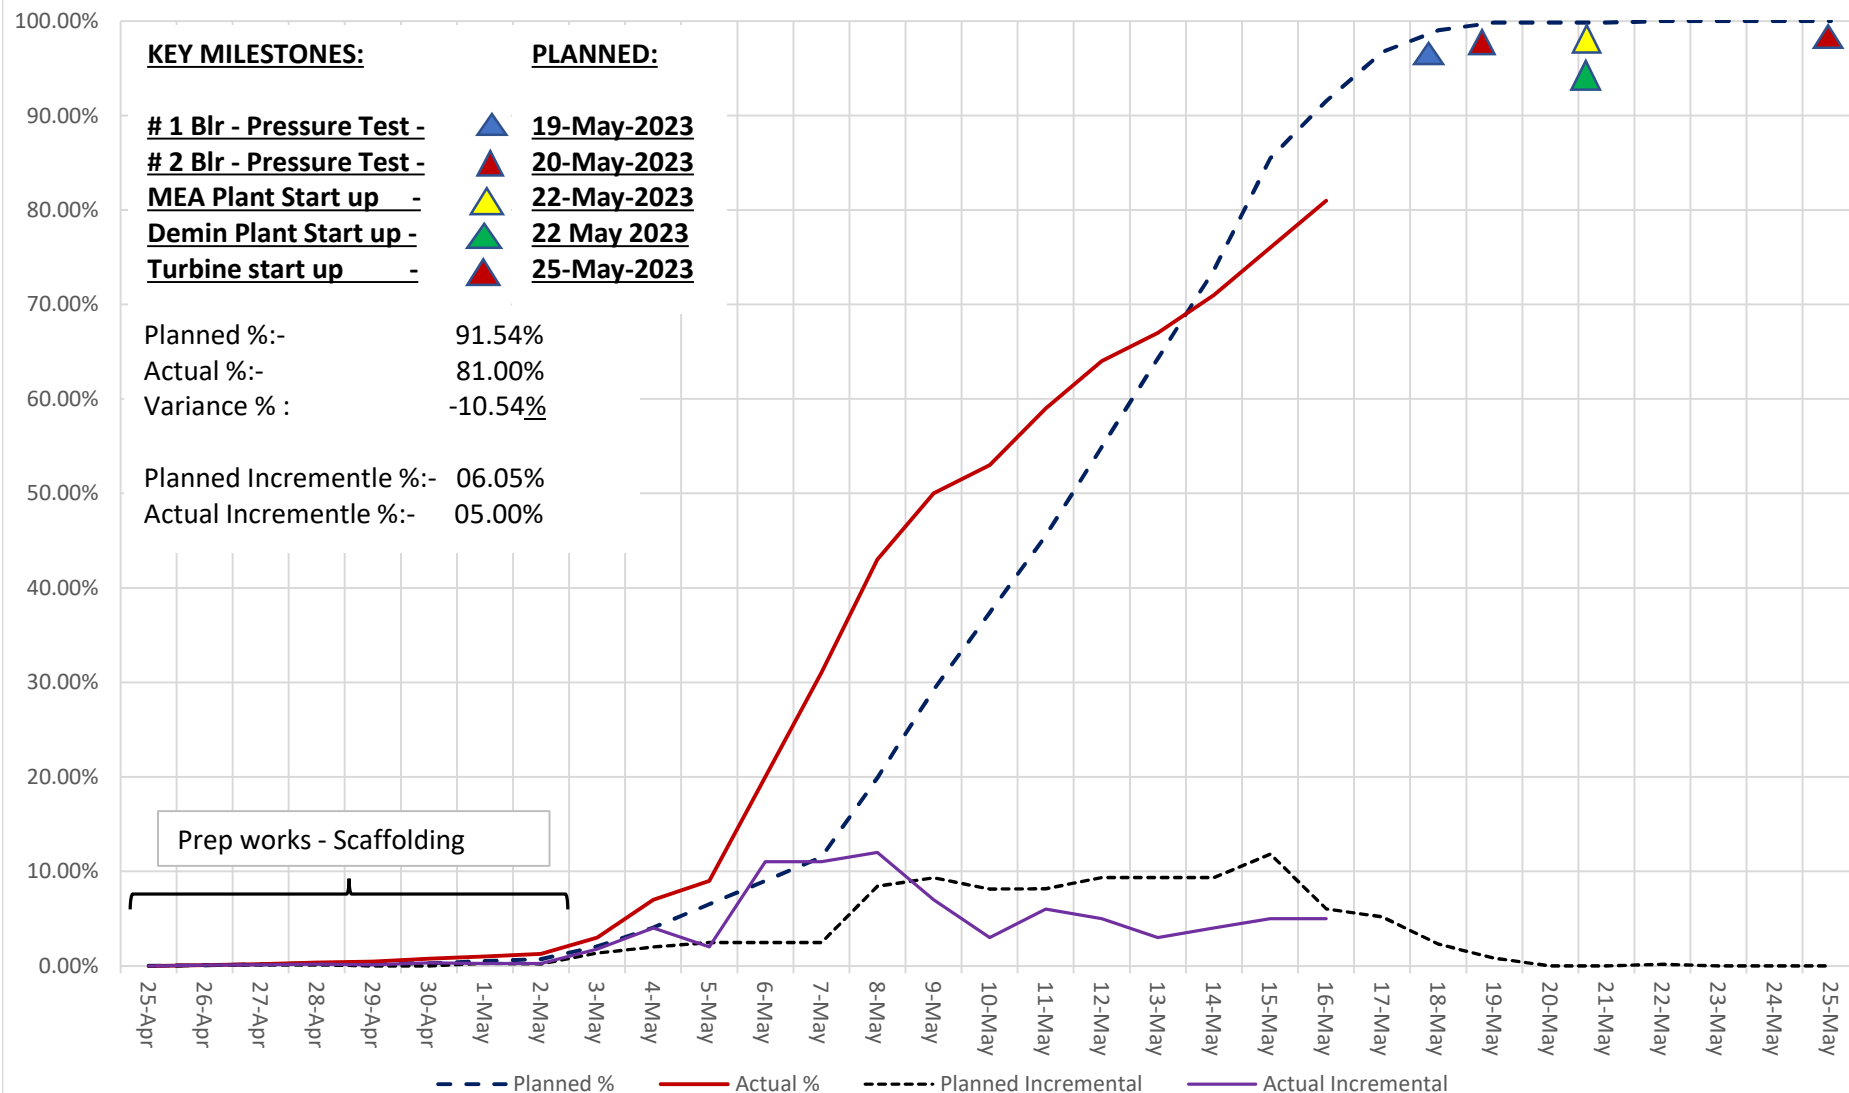


FLUE GAS DESULPHURISATION - Update:- 16 May 2023

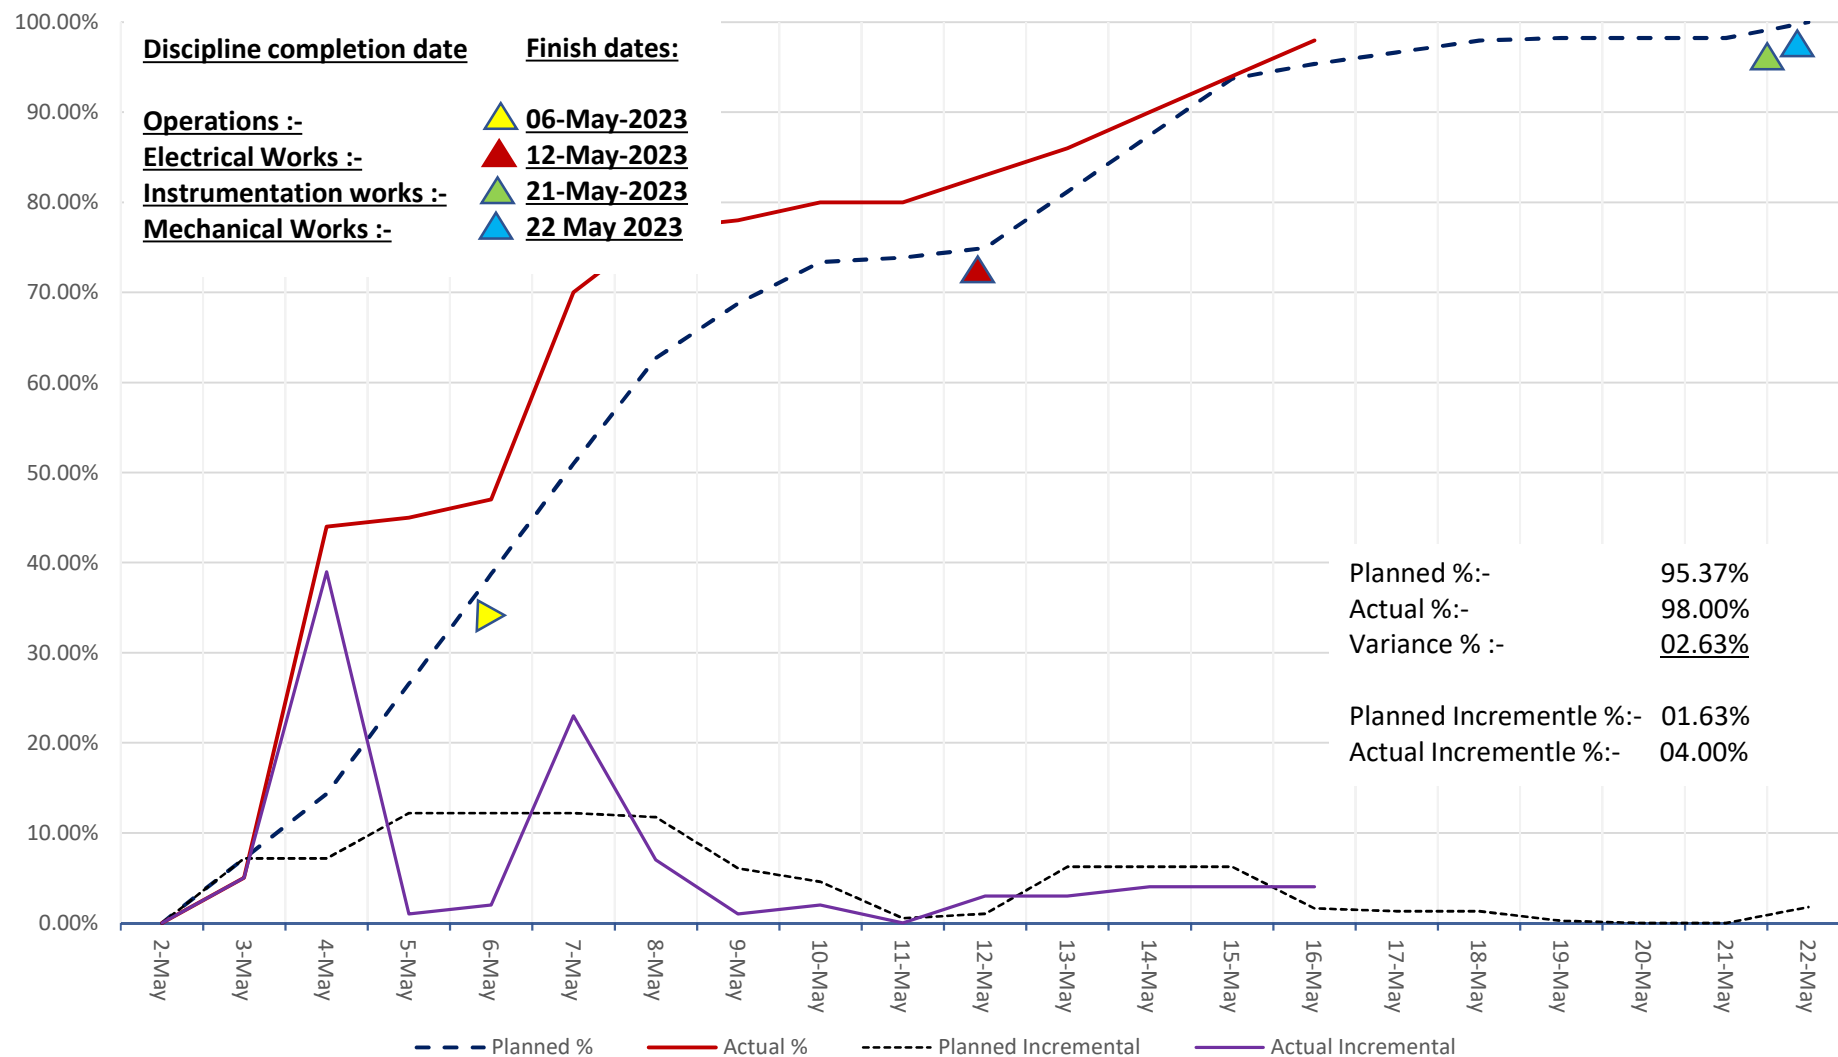




MEA SYSTEM ABSORPTION - Update 16 May 2023

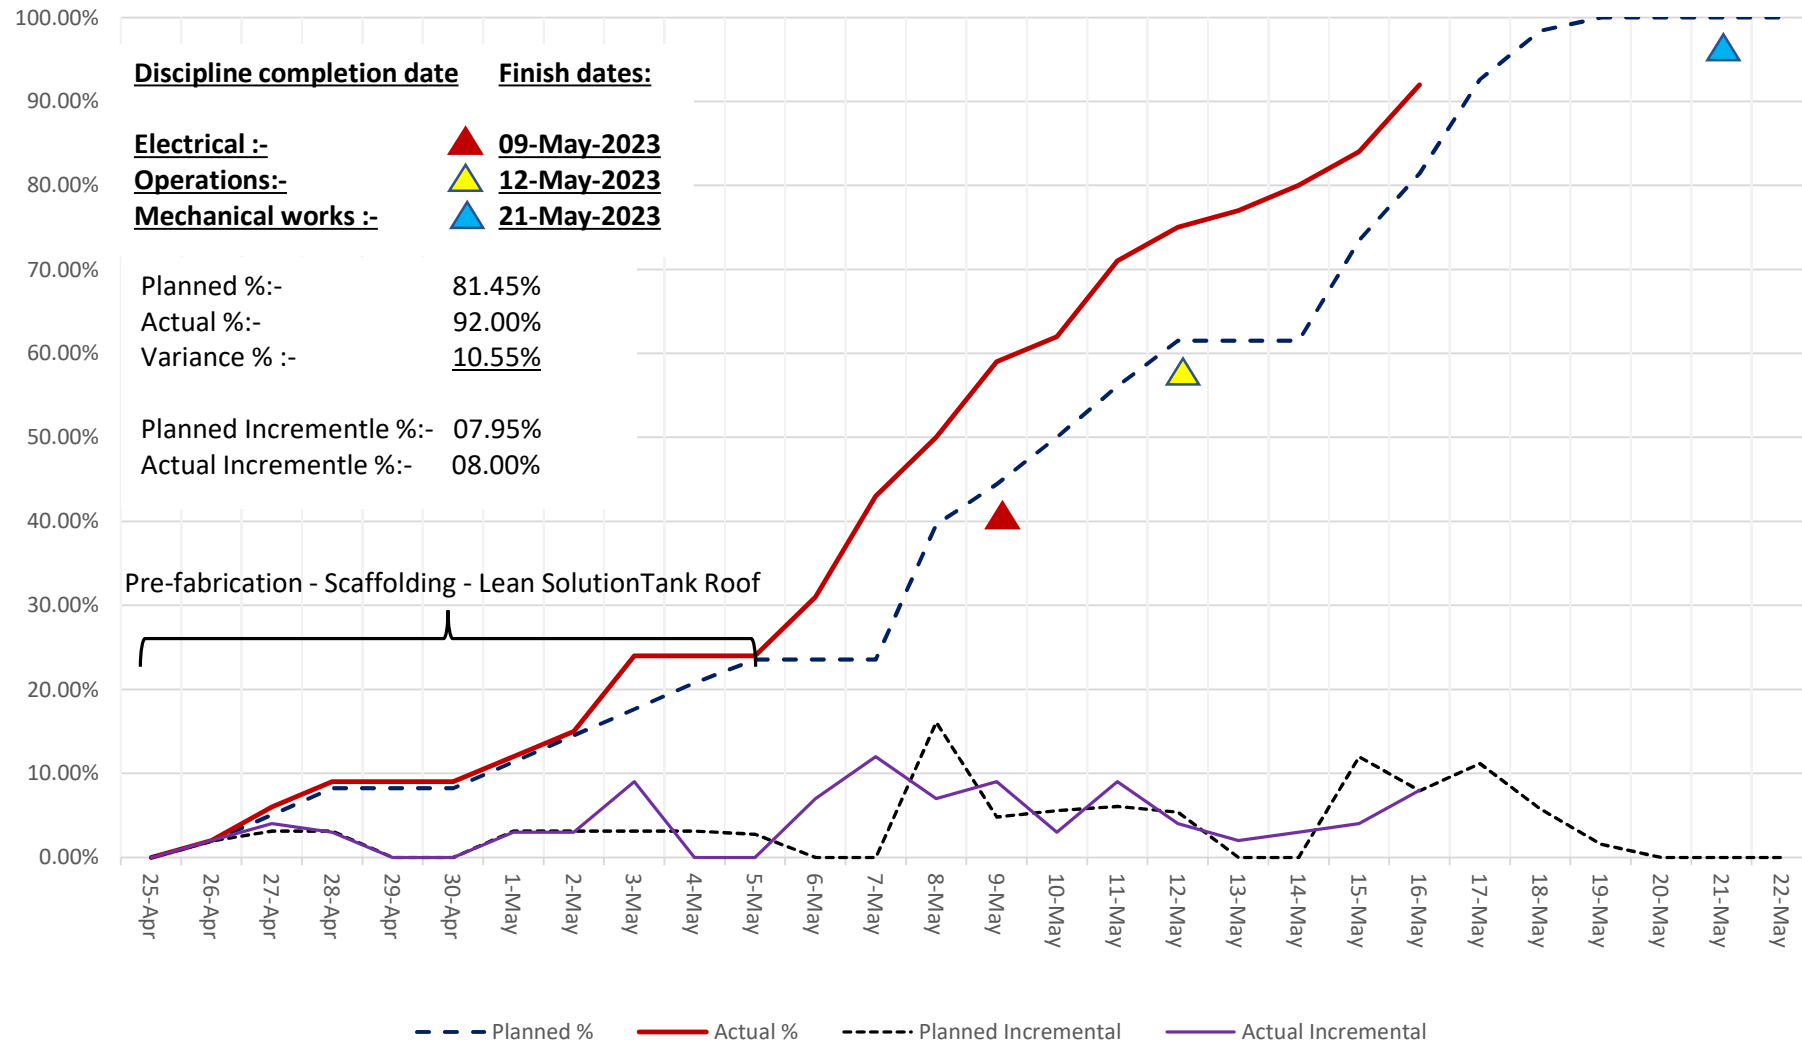




MEA SYSTEM STRIPPING - Update 16 May 2023

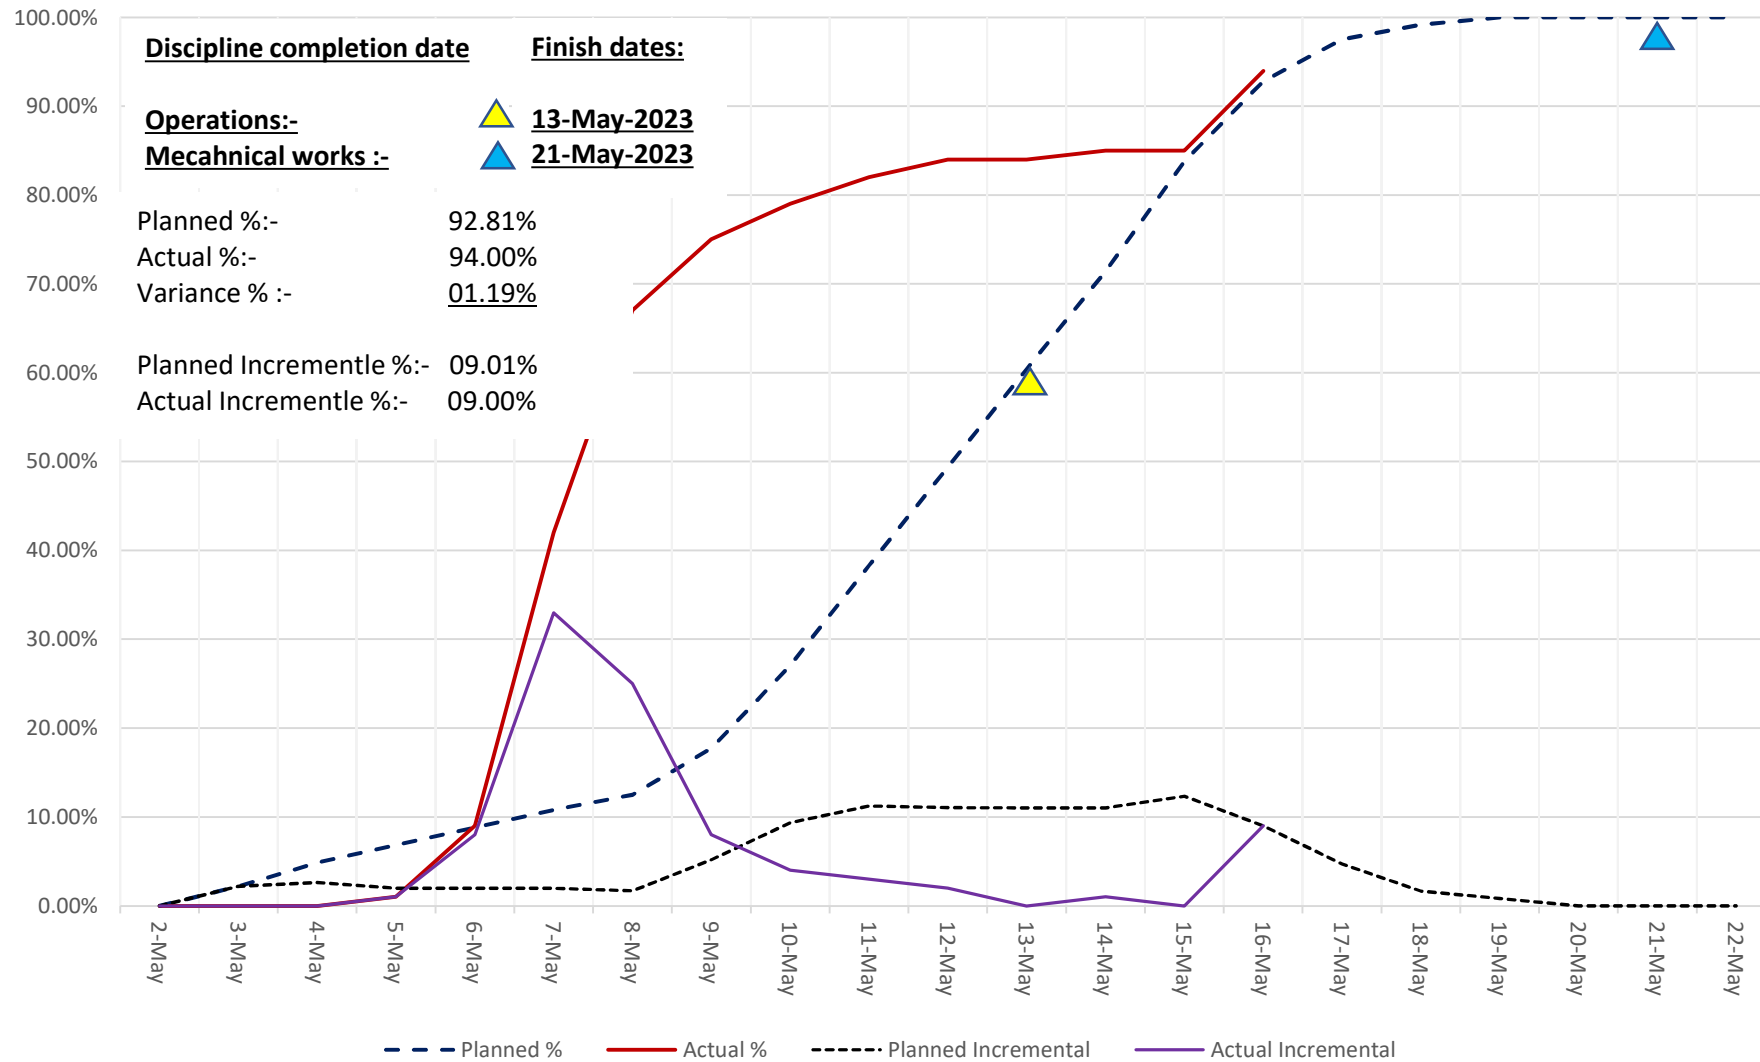




MEA SYSTEM RECLAIMER - Update 16 May 2023

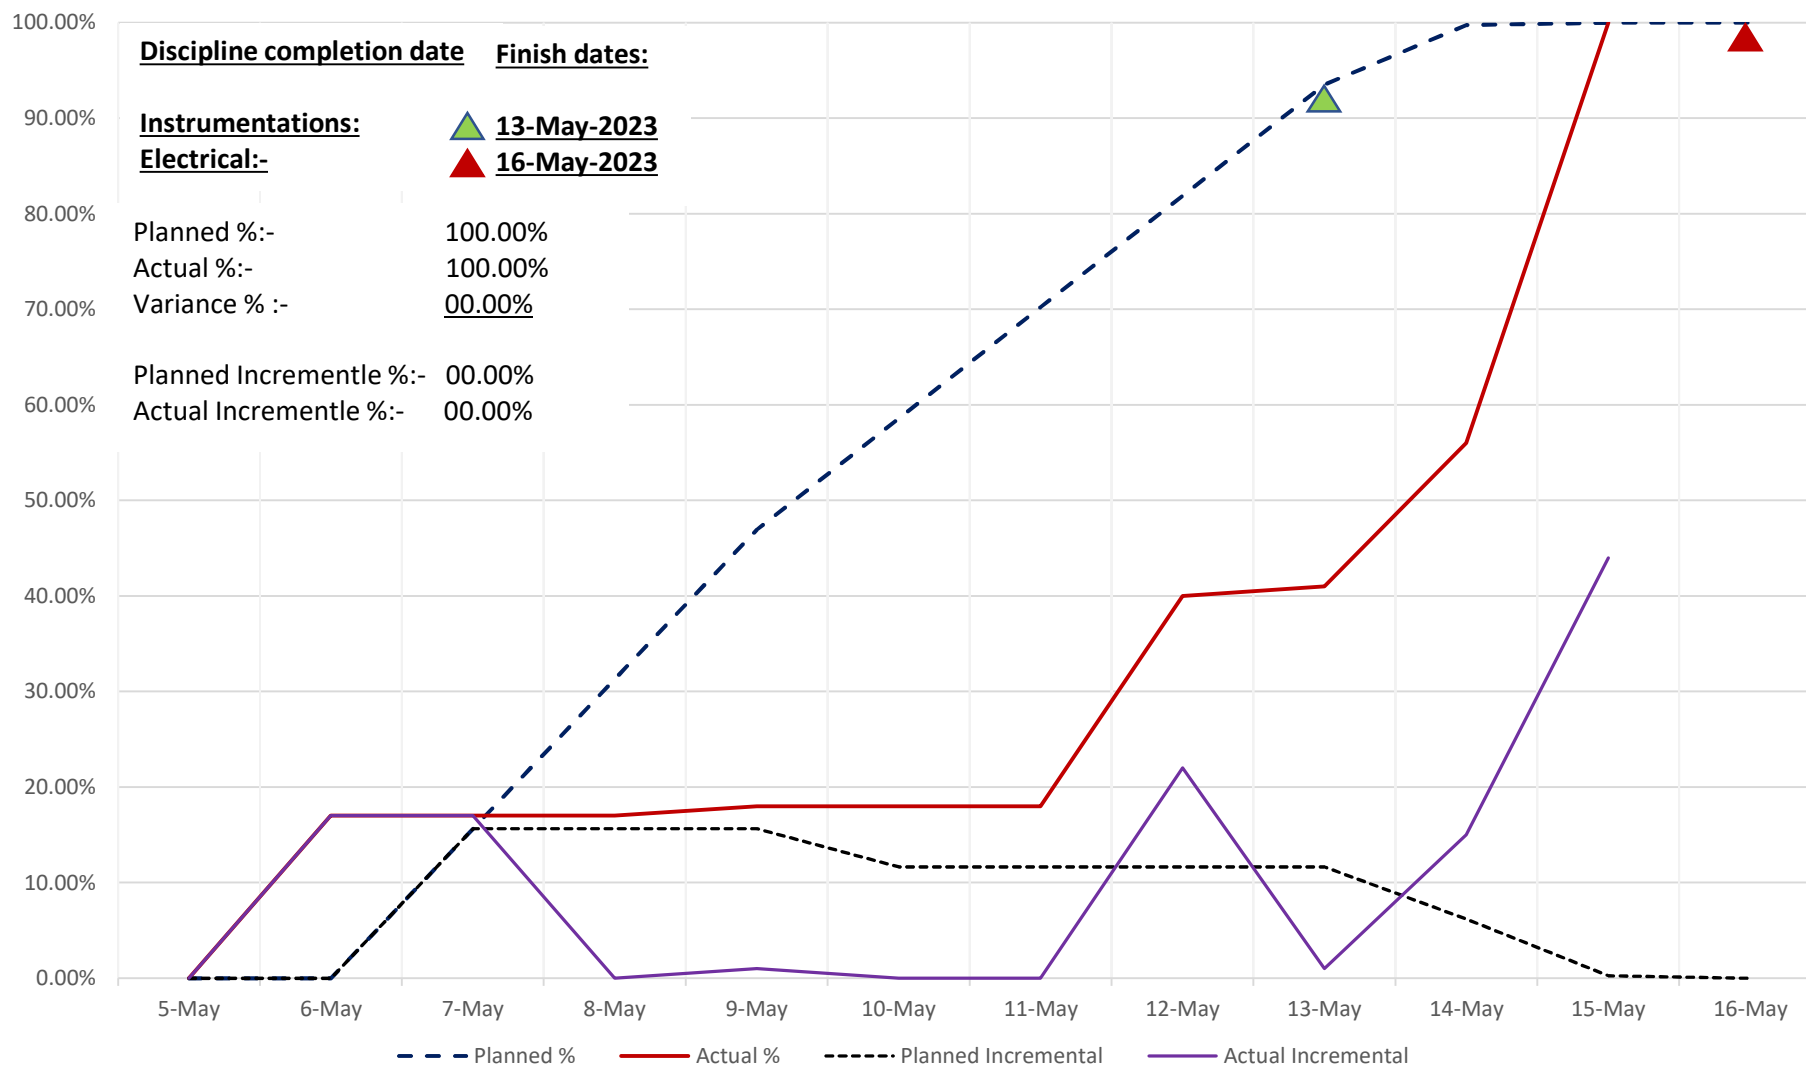




BOILER # 1 - Update 16 May 2023

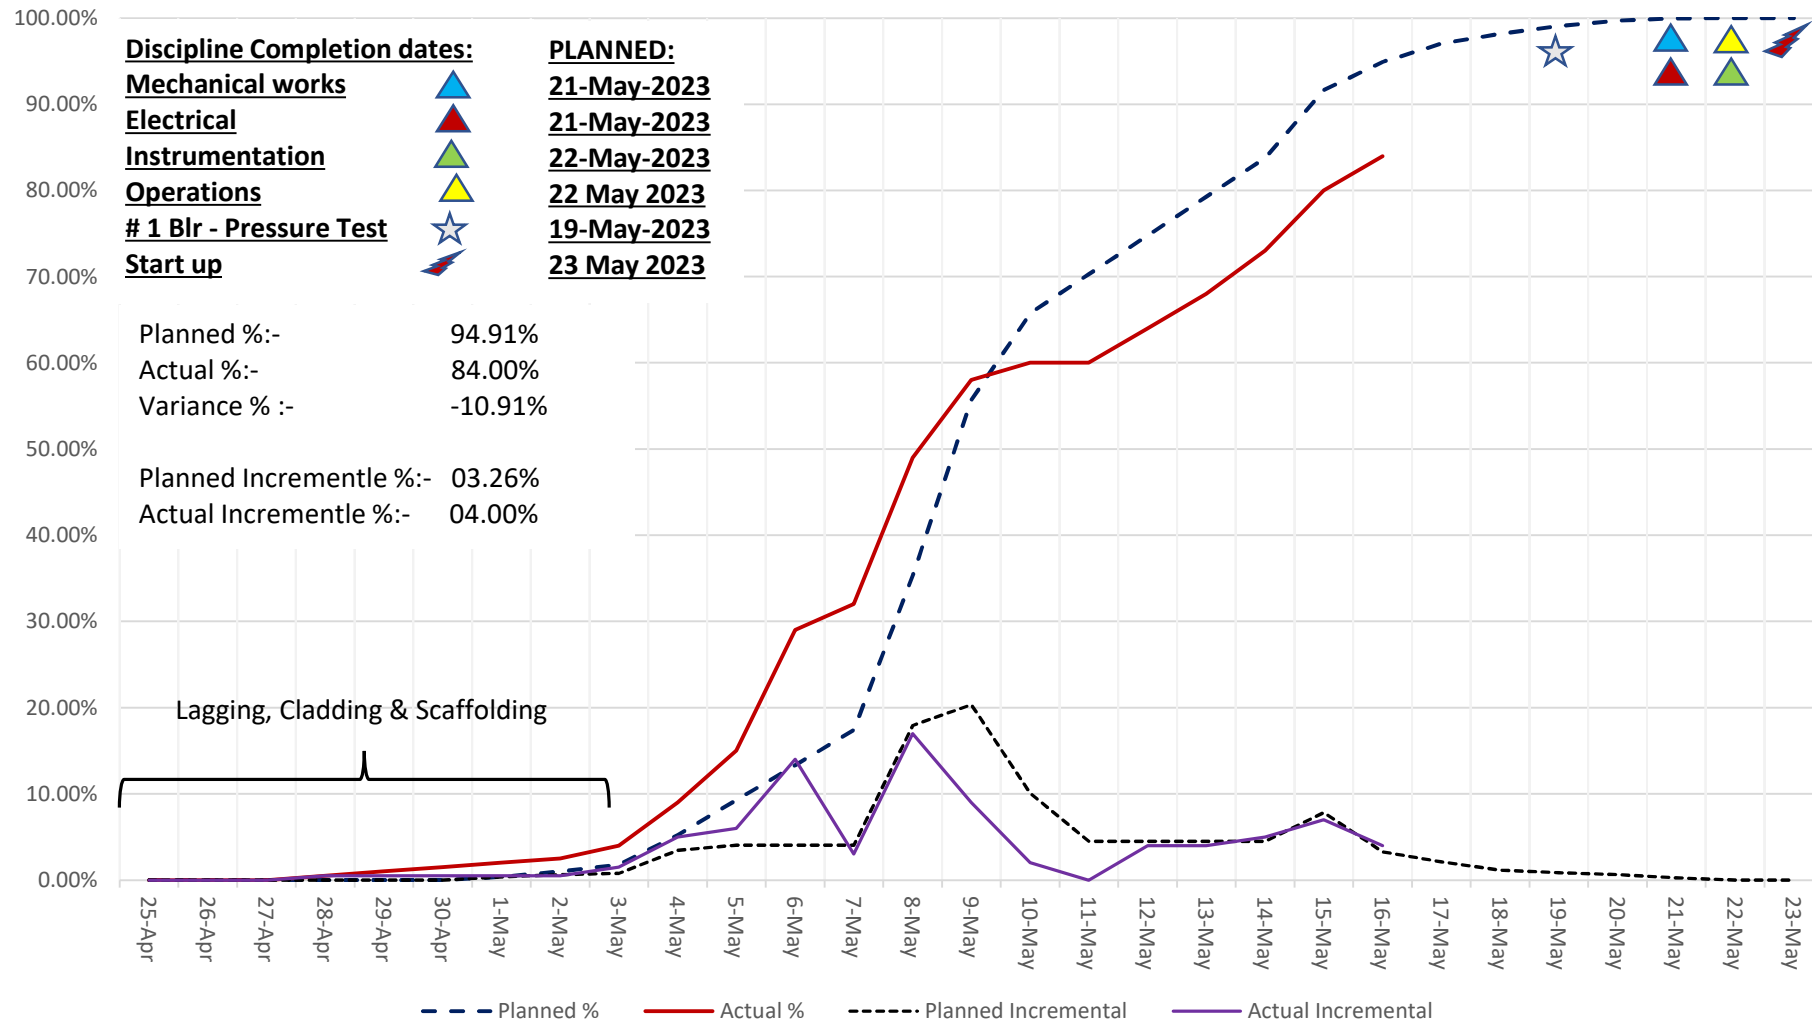





Botswana Ash (Pty) Ltd

BOILER # 2 - Update 16 May 2023

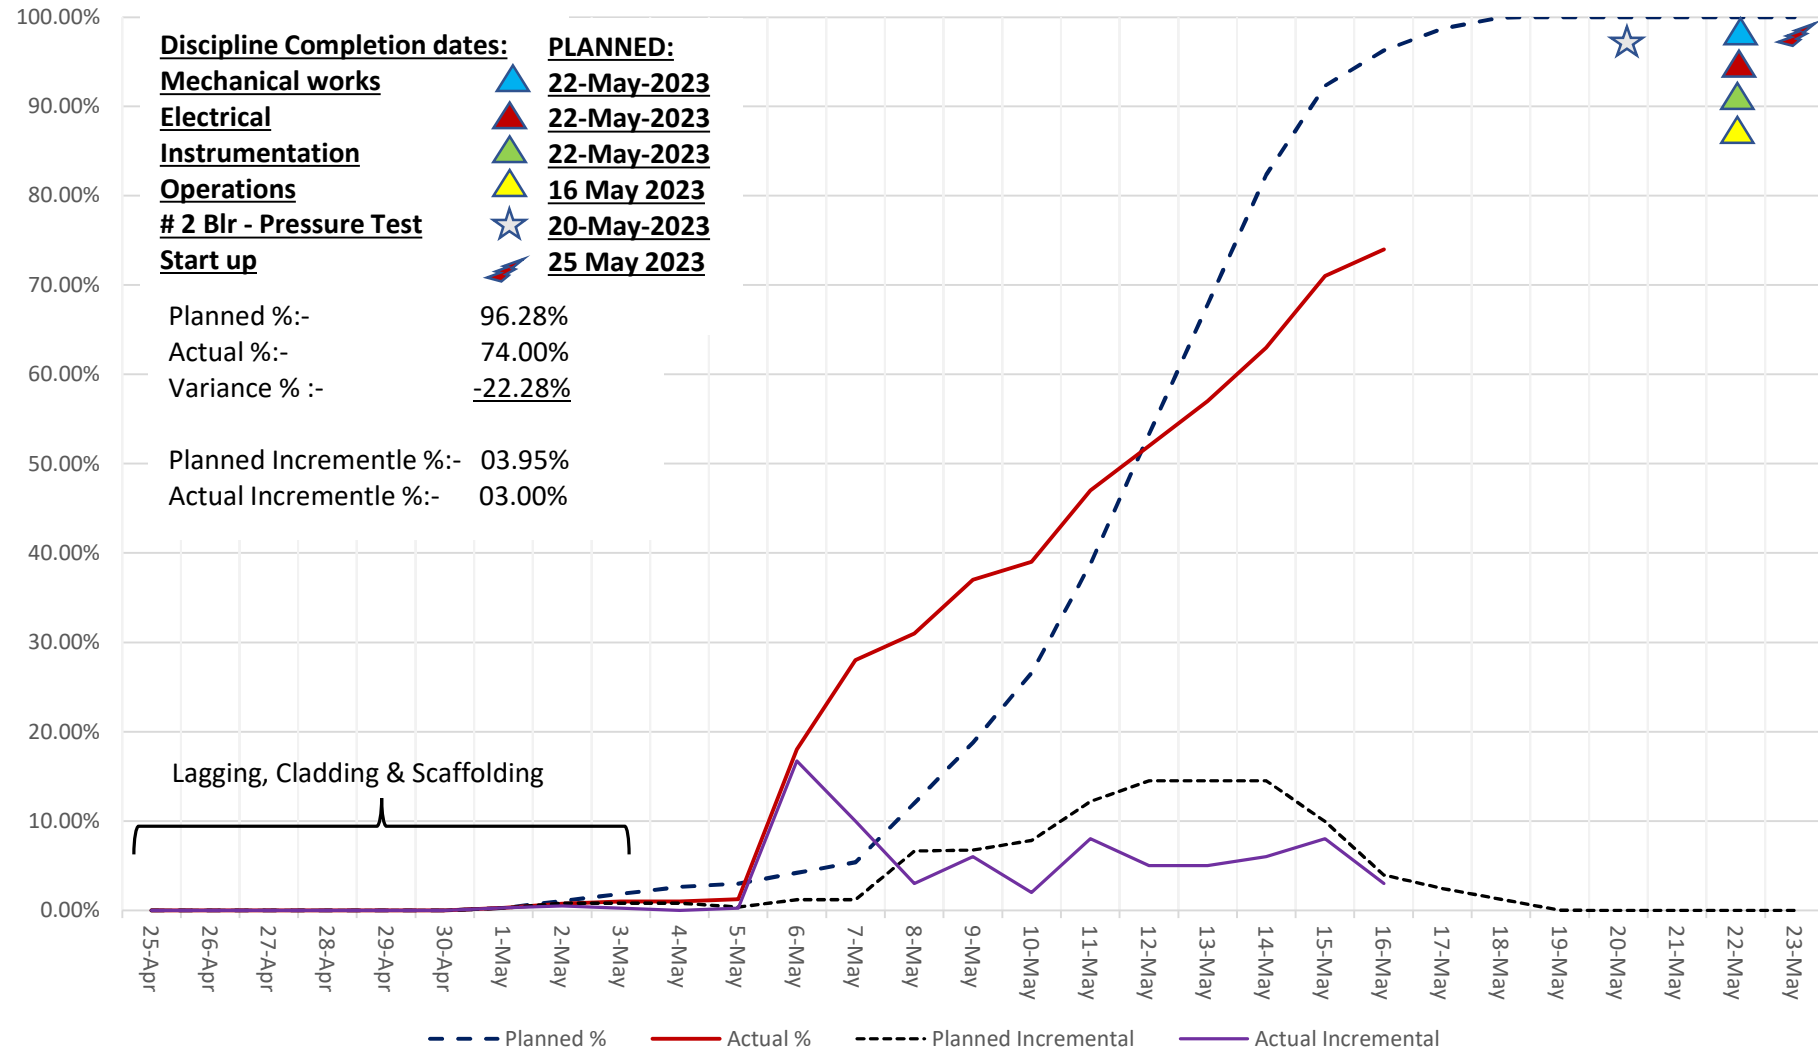




COAL HANDLING PLANT- Update 16 May 2023

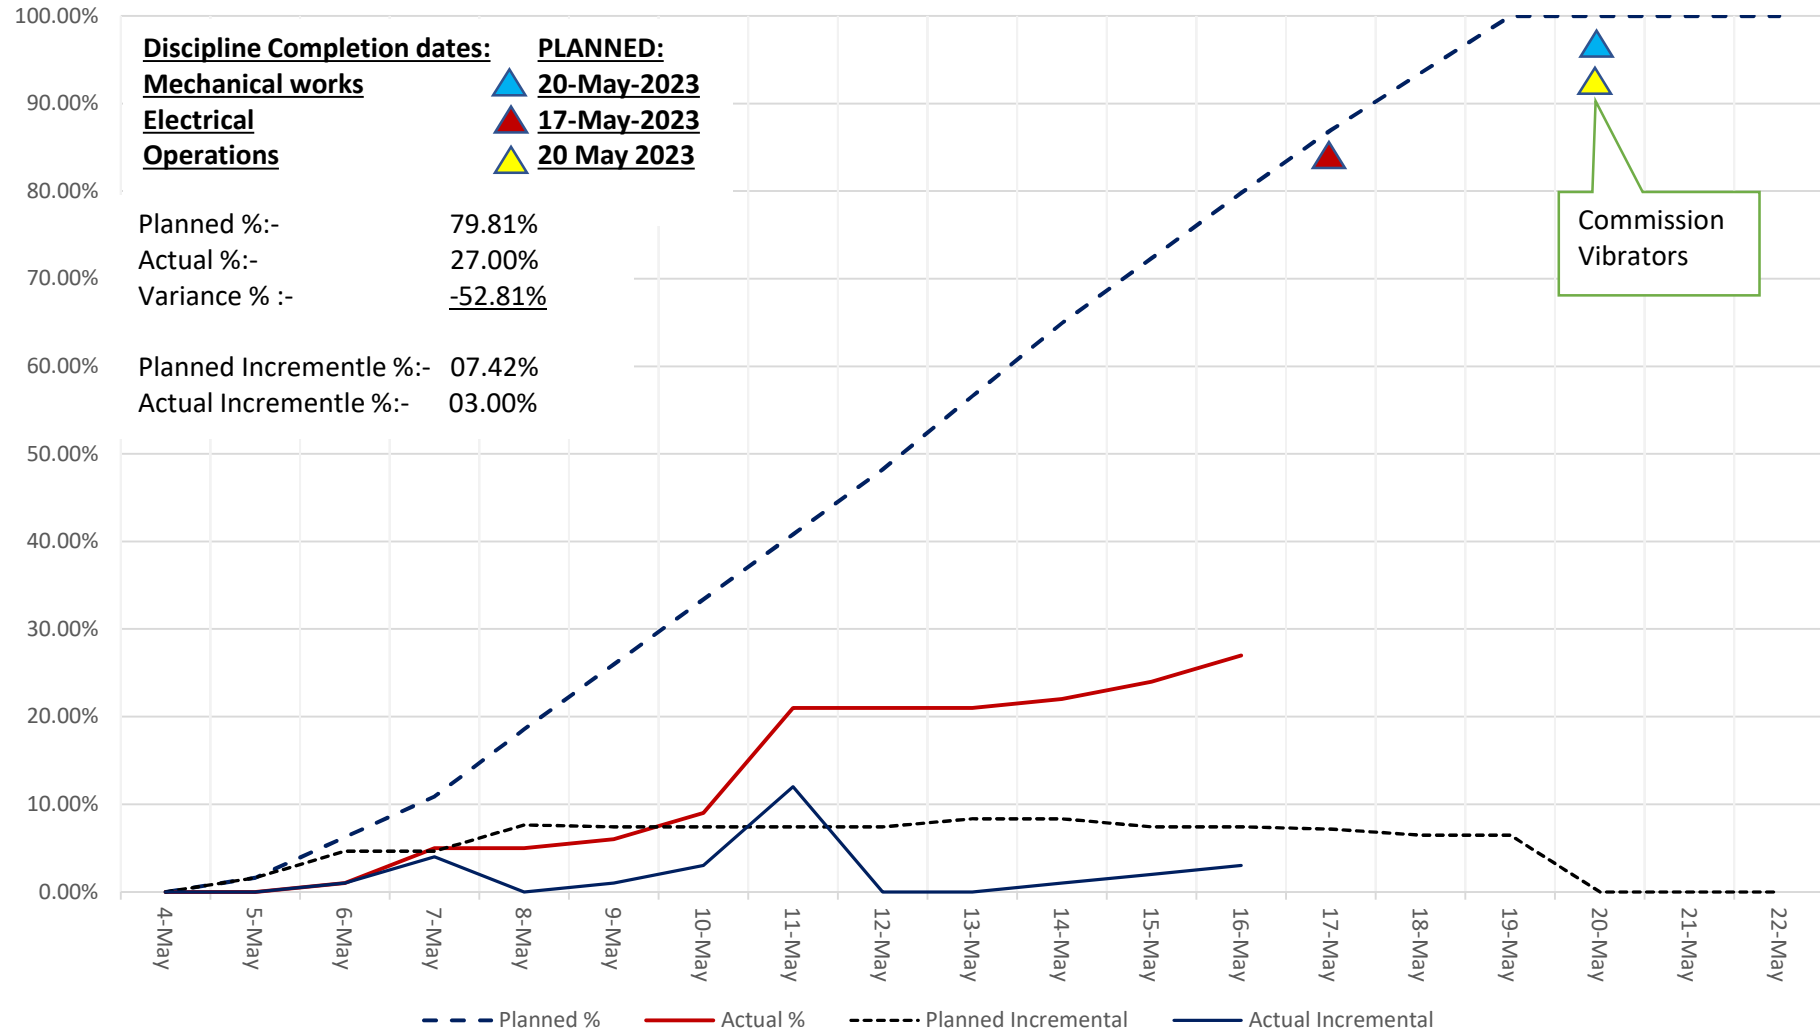



BOILER PLANT COMMON - Update 16 May 2023

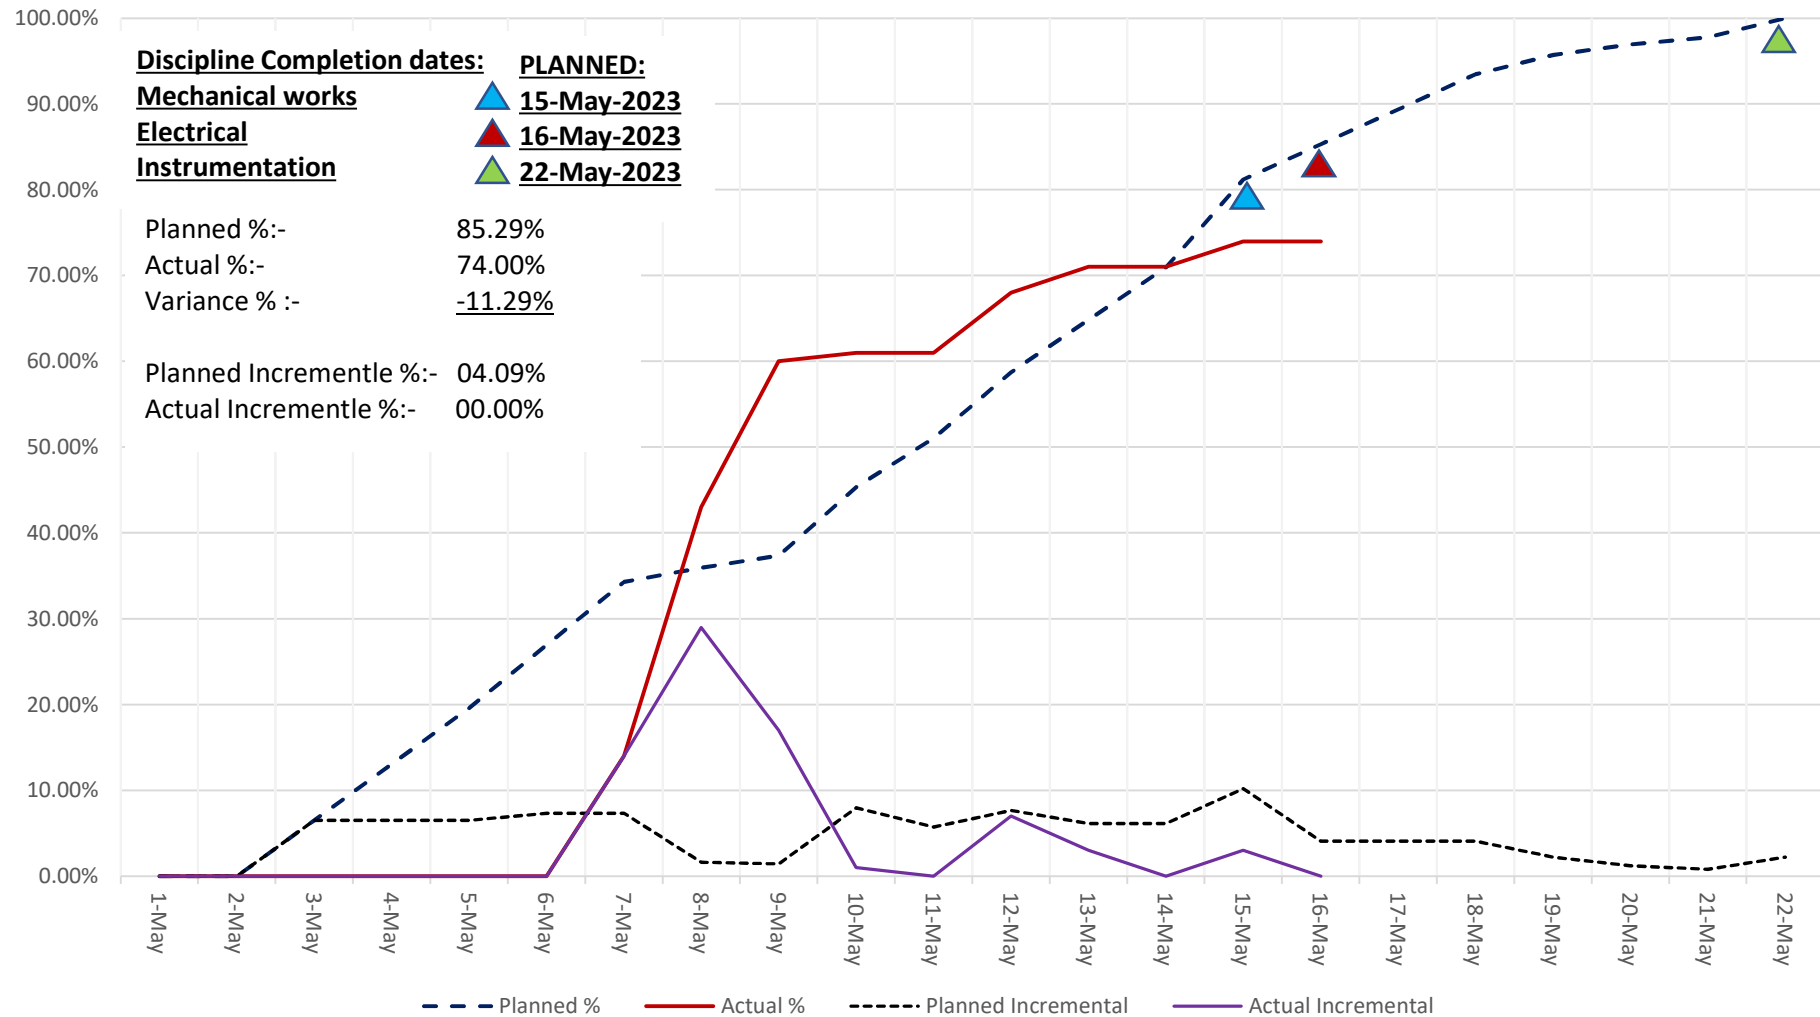



Botswana Ash (Pty) Ltd


WATER TREATMENT PLANT - Update 16 May 2023

Discipline Completion dates:

Operations	 16-May-2023
Electrical	 15-May-2023
Civils	 19-May-2023
Mechanical works	 22 May 2023


Planned %:- 86.16%
Actual %:- 79.00%
Variance % :- -07.16%

Planned Incrementle %:- 08.48%
Actual Incrementle %:- 02.00%

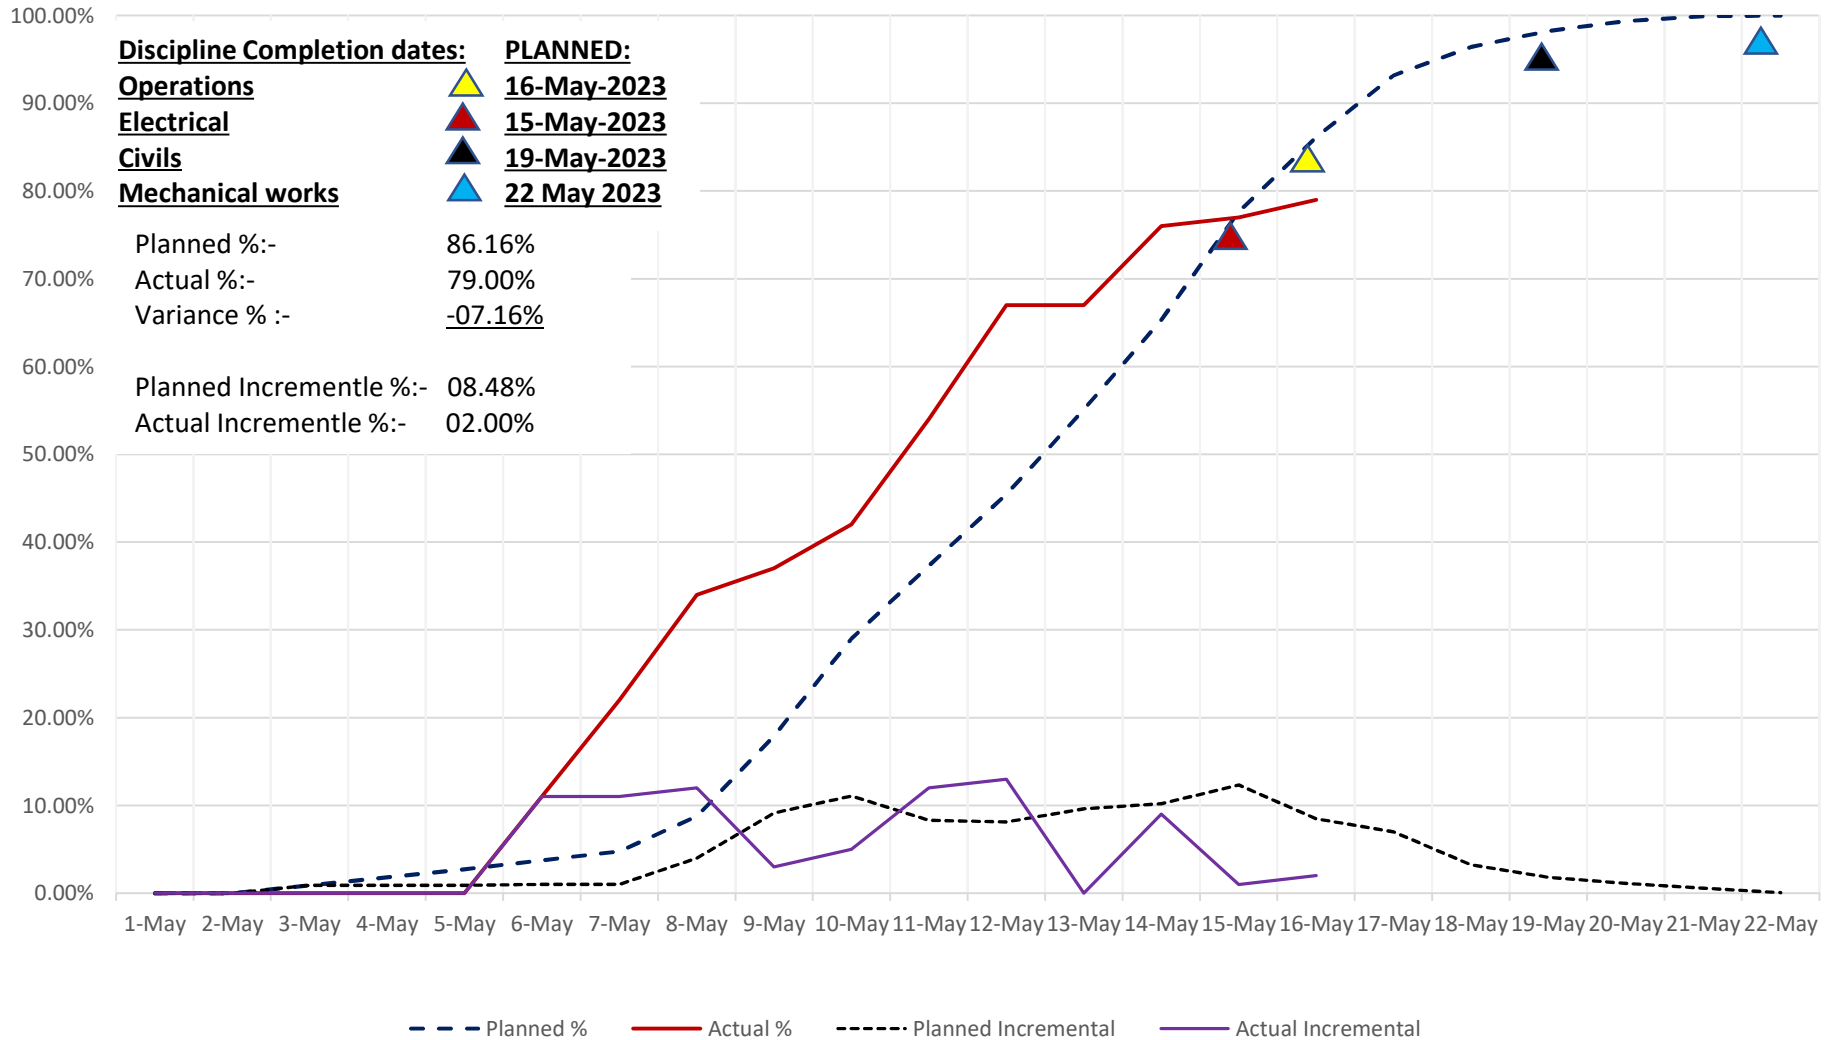




INSTRUMENT & COMPRESSED AIR - Update 16 May 2023

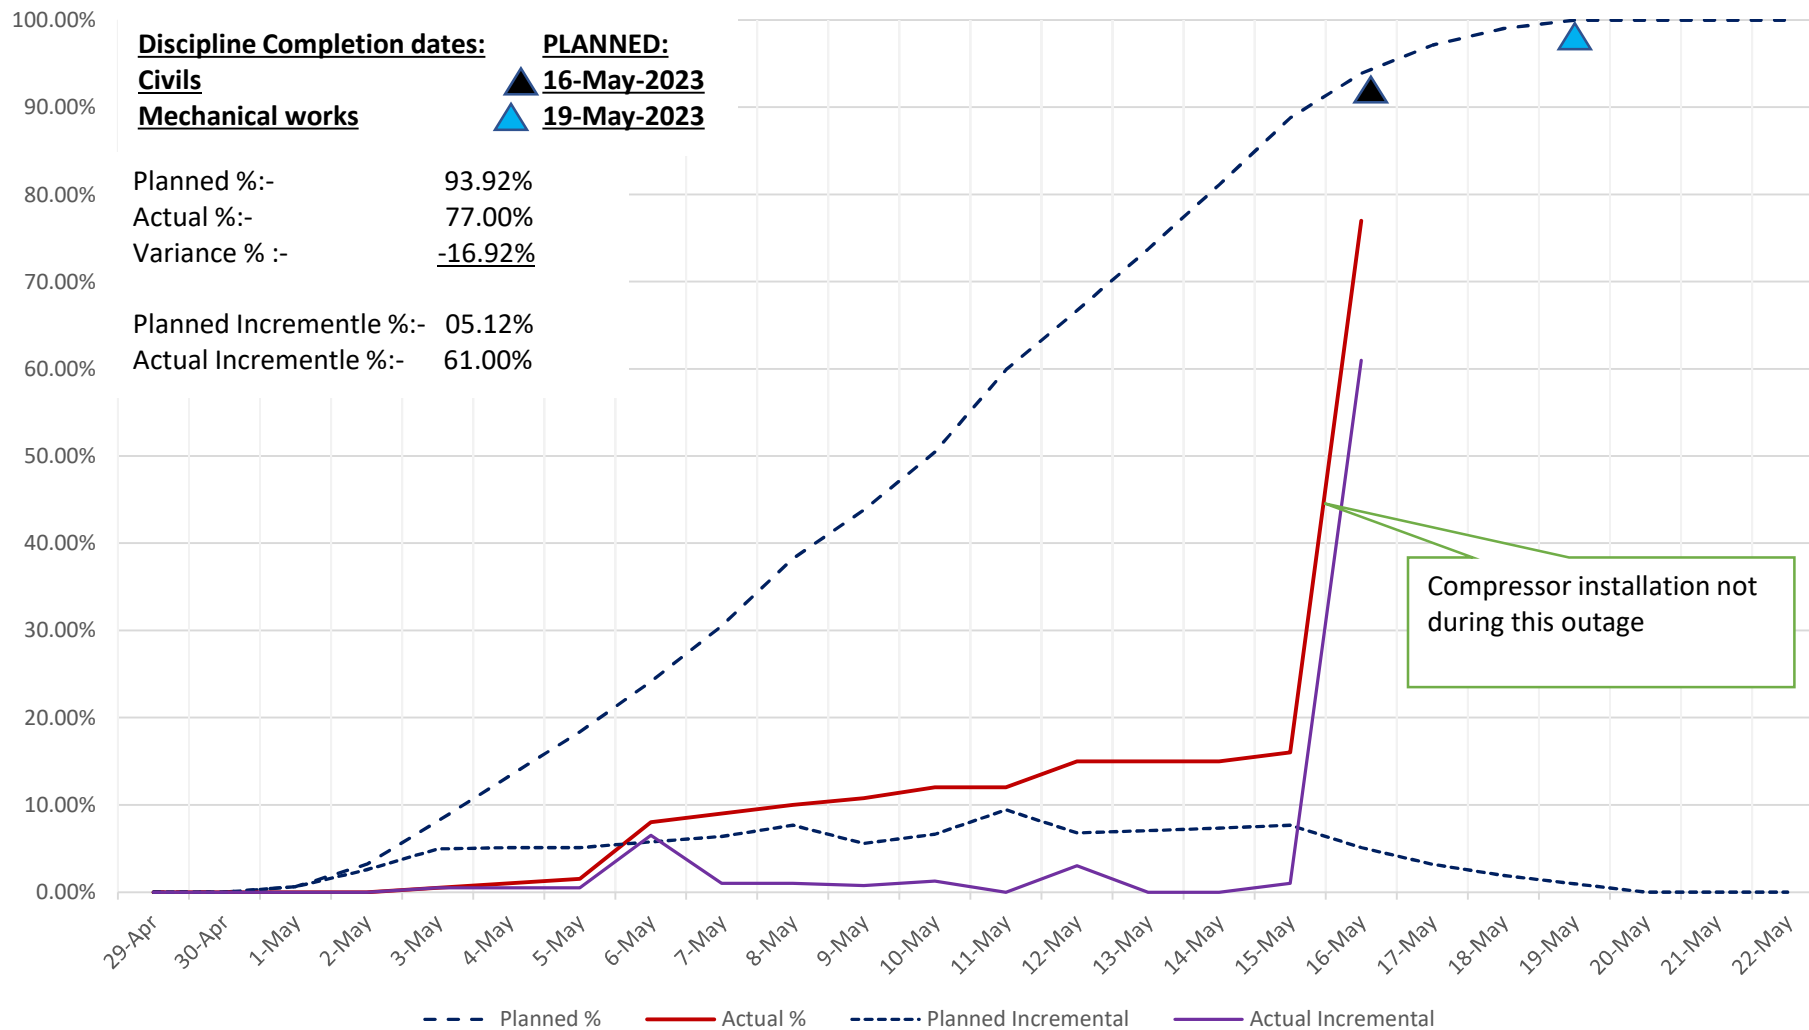




Botswana Ash (Pty) Ltd

STEAM AND CONDENSATE- Update 16 May 2023

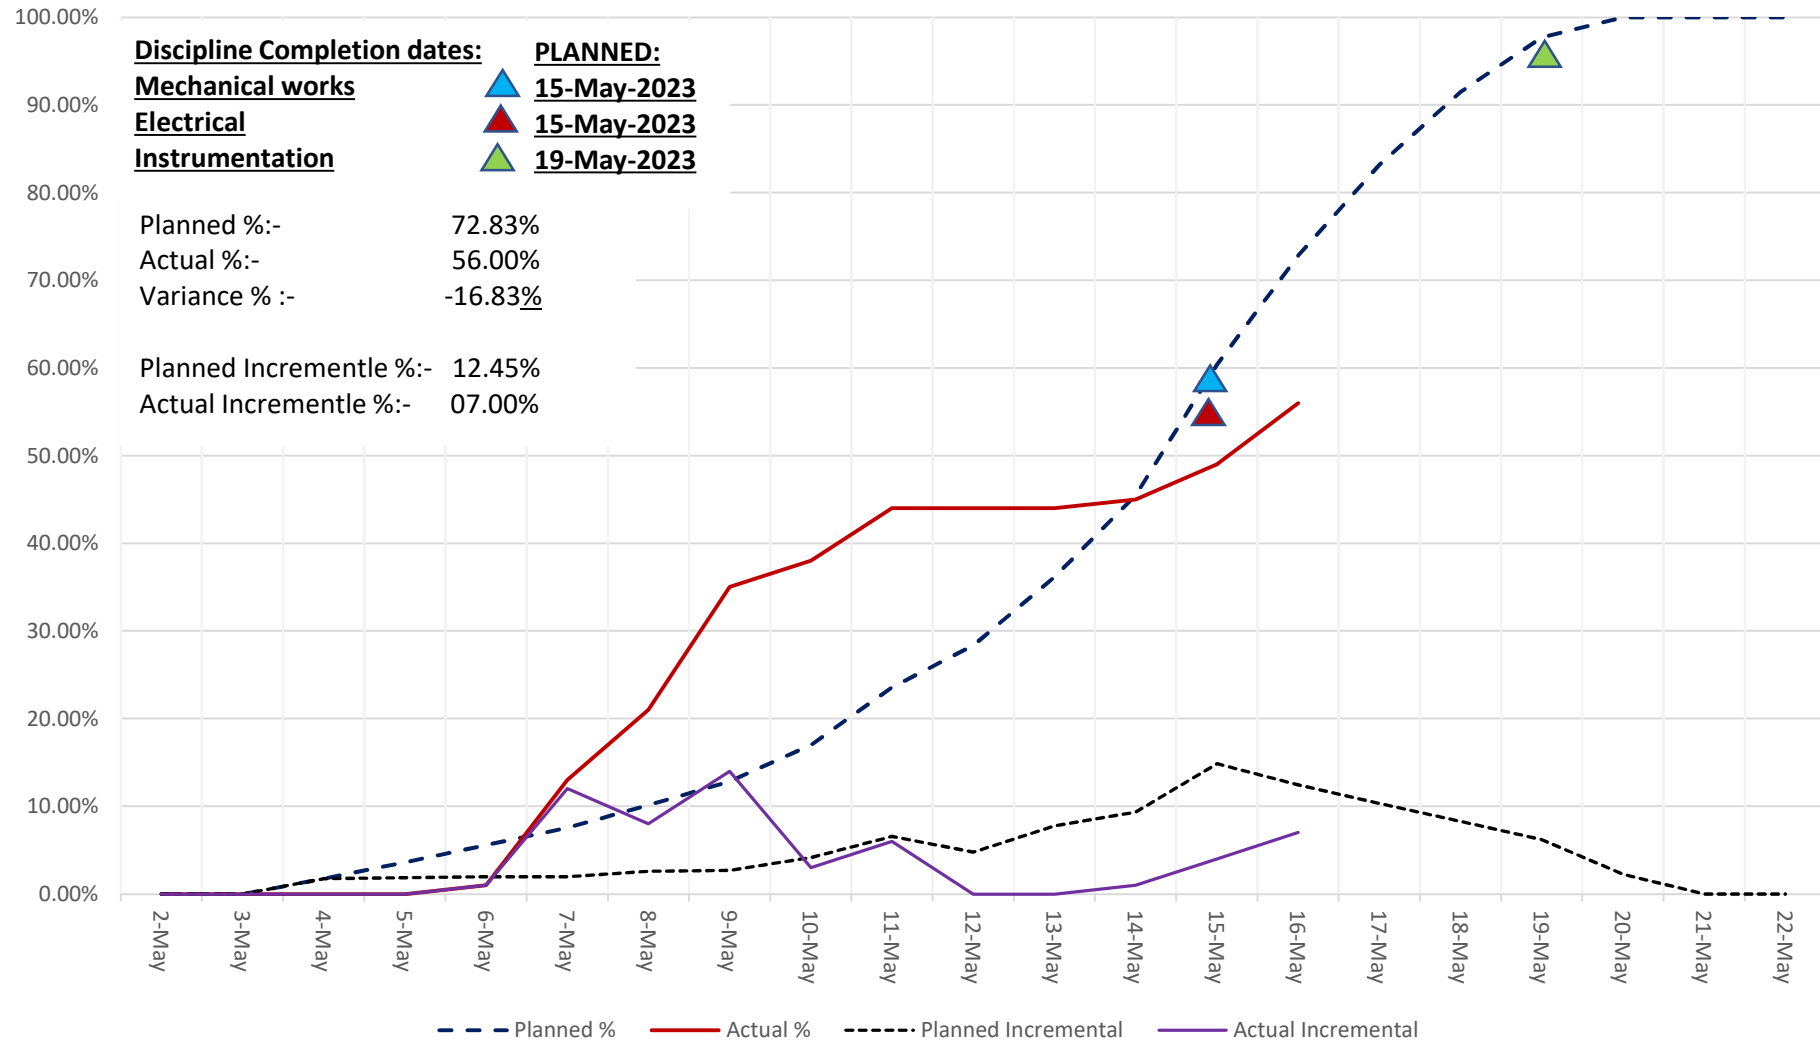




TURBINE - Update 16 May 2023

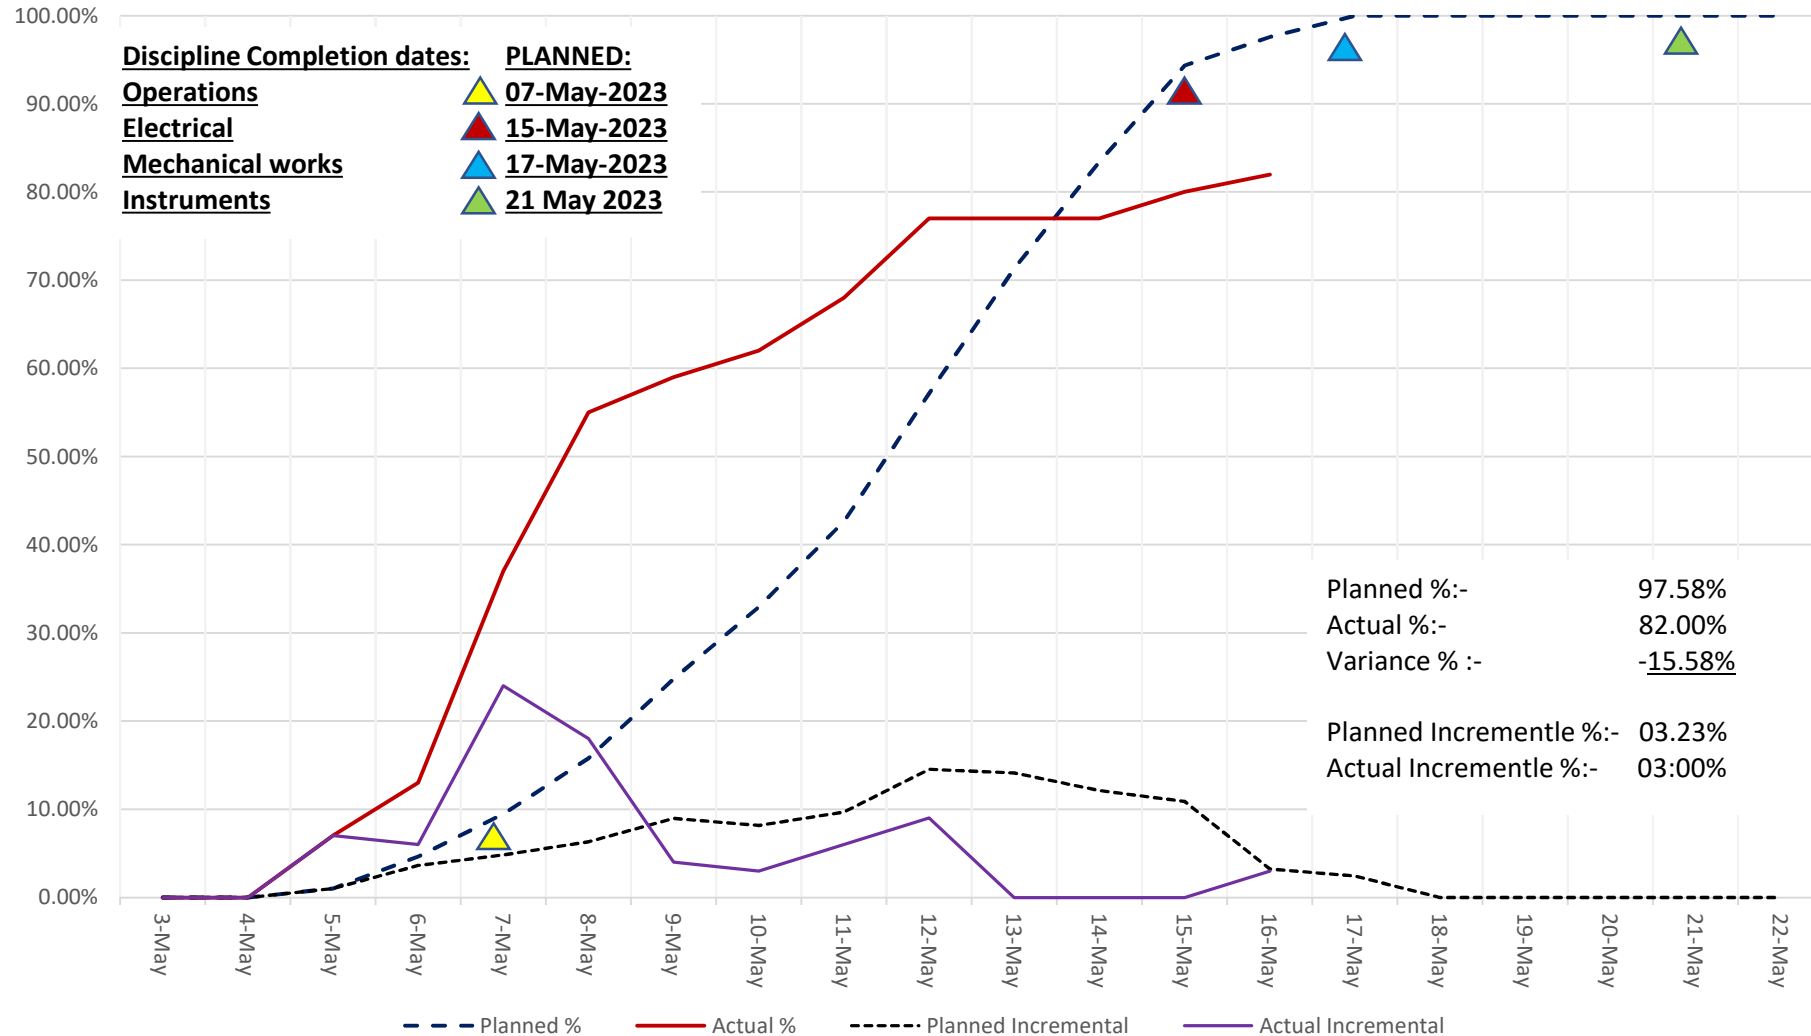



MV RETICULATION - Update 16 May 2023

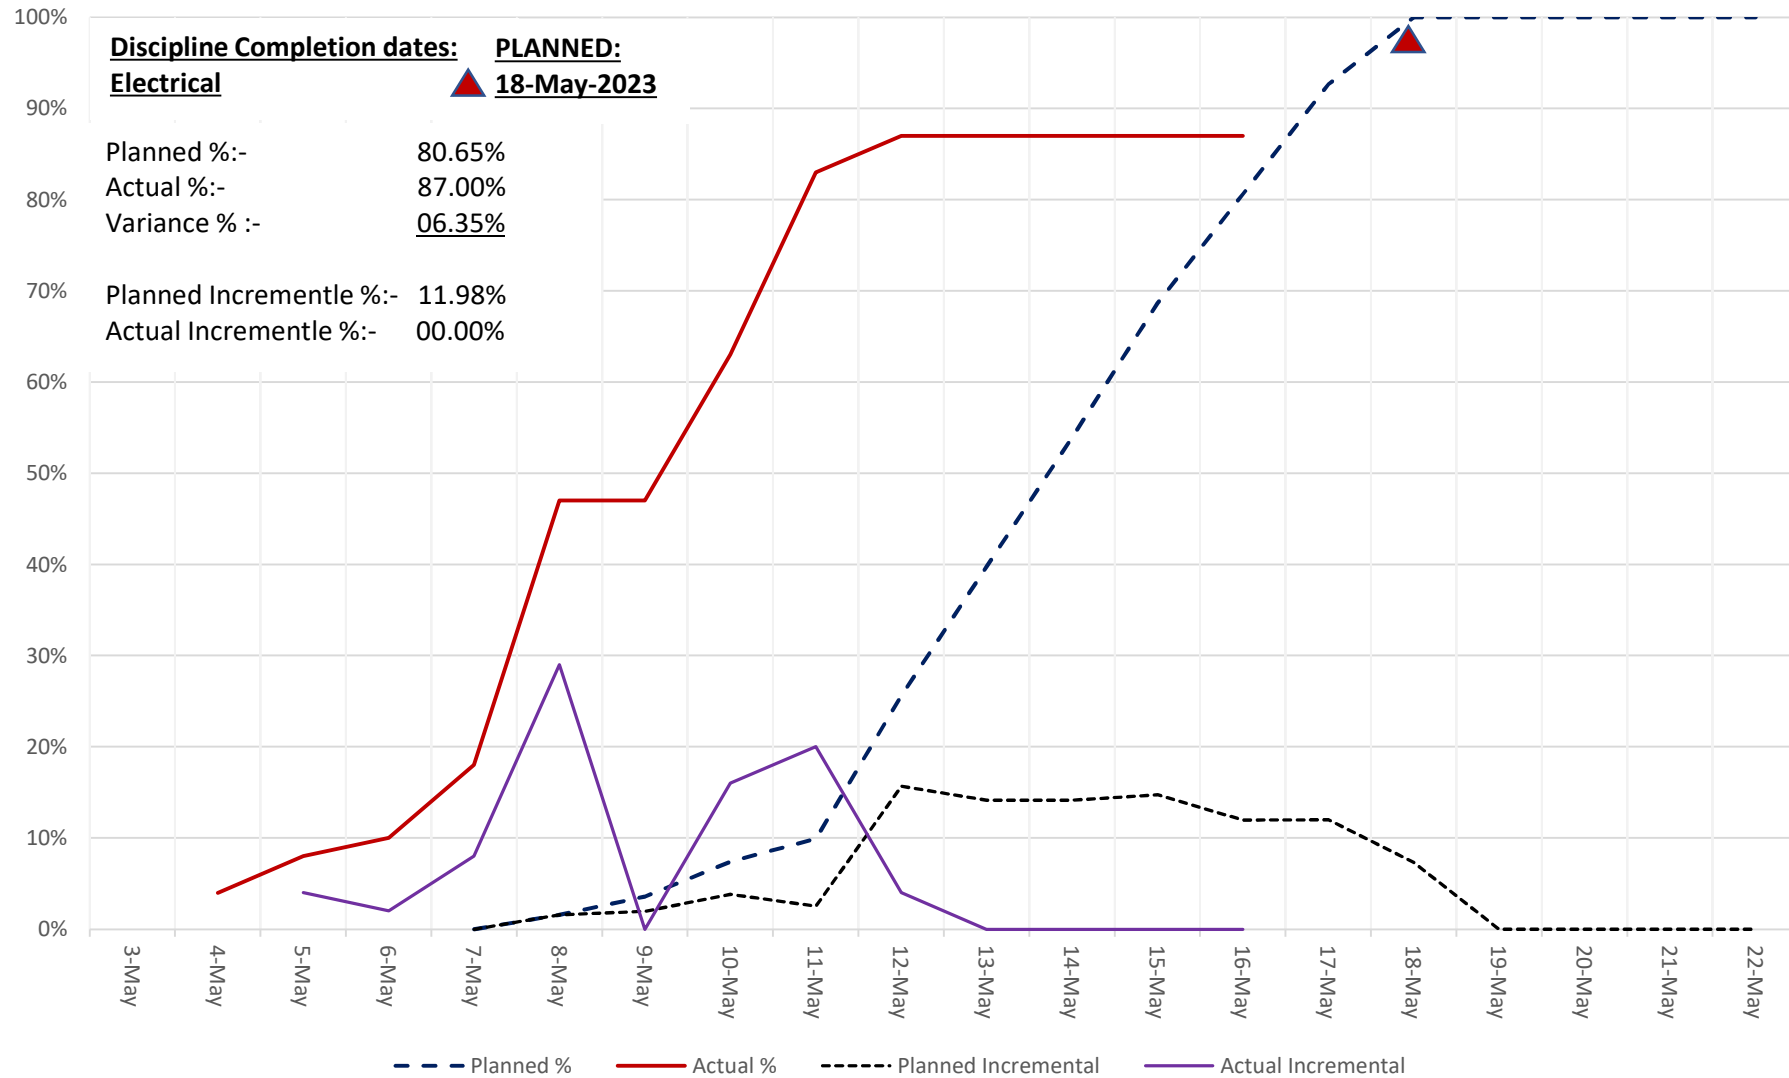



LV RETICULATION - Update 16 May 2023

Discipline Completion dates: **PLANNED:**
Electrical ▲ **18-May-2023**

Planned %:- 77.58%
Actual %:- 61.00%
Variance % :- -16.58%

Planned Incrementle %:- 19.17%
Actual Incrementle %:- 00.00%

