





BOTSWANA - BOTASH REFURBISHMENT PROJECT 2023 - UTILITY PLANT

Update:- 17 May 2023



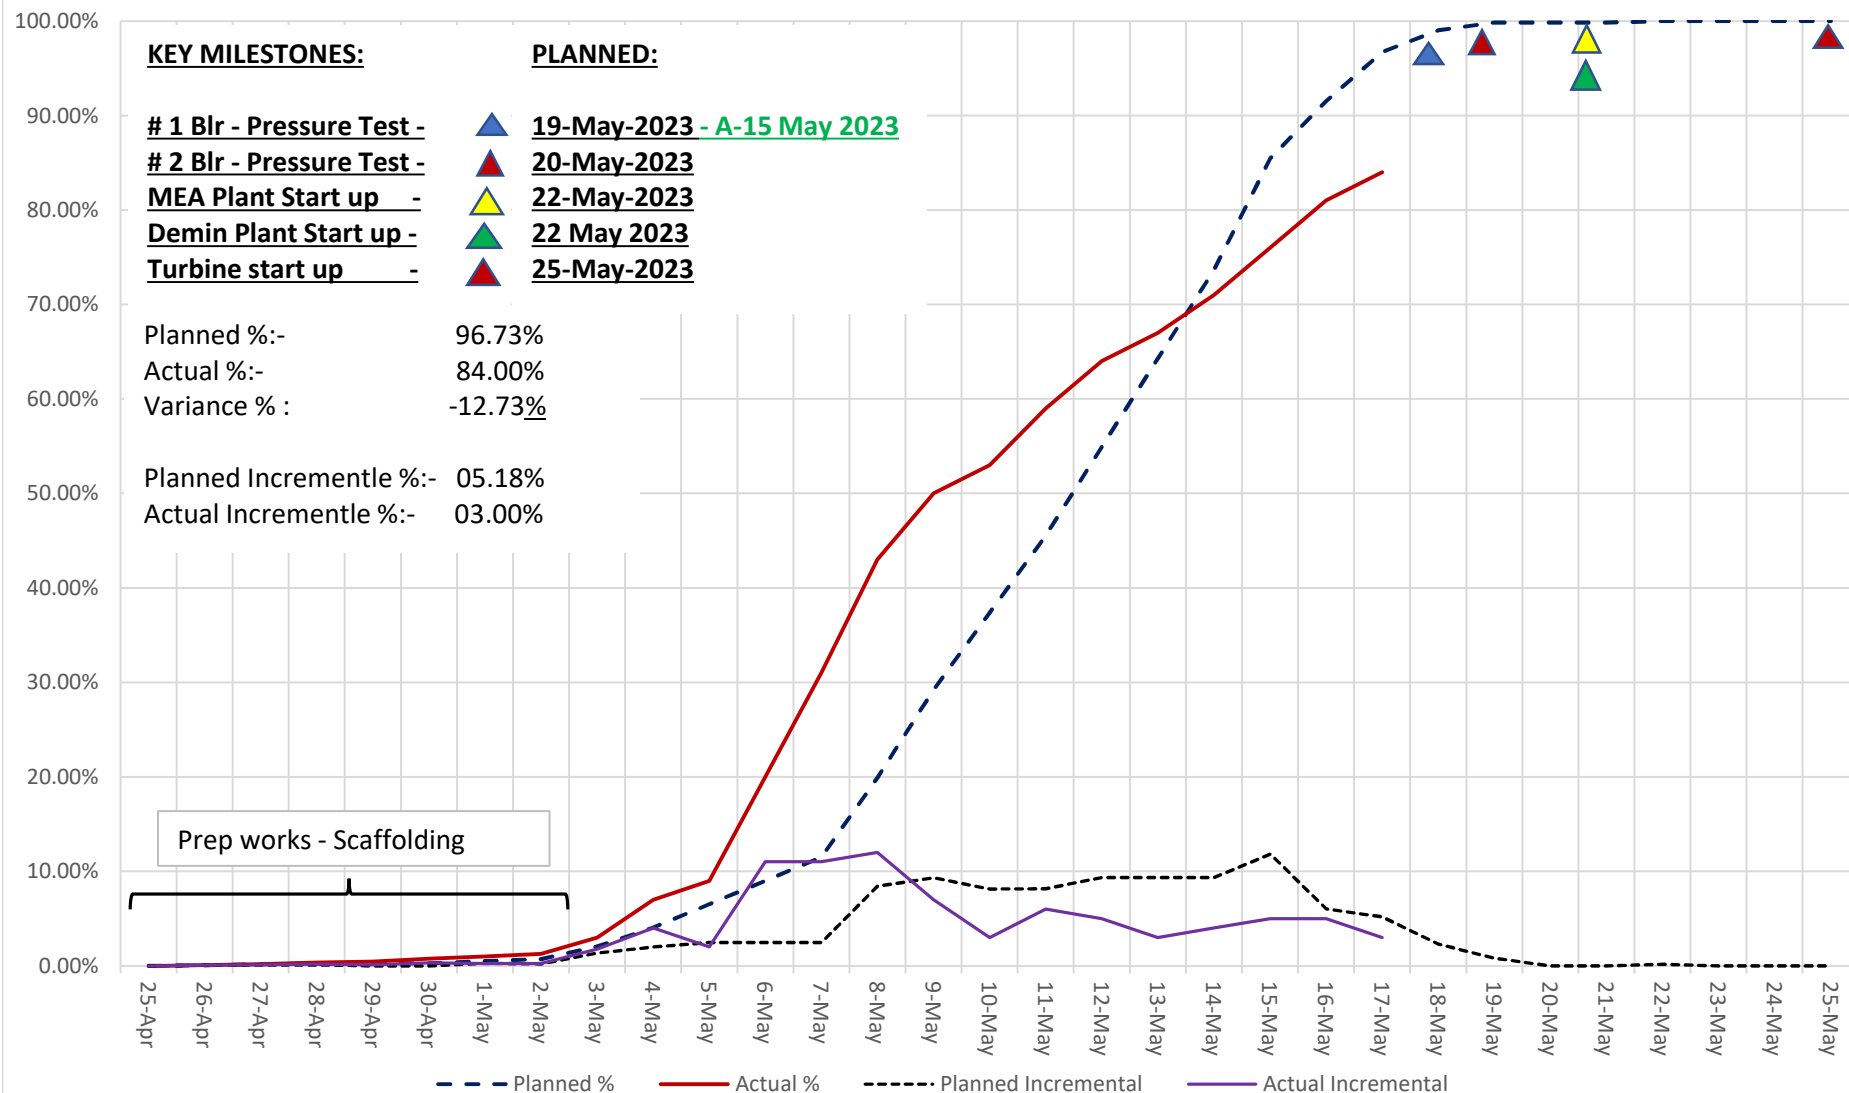


FLUE GAS DESULPHURISATION - Update:- 17 May 2023

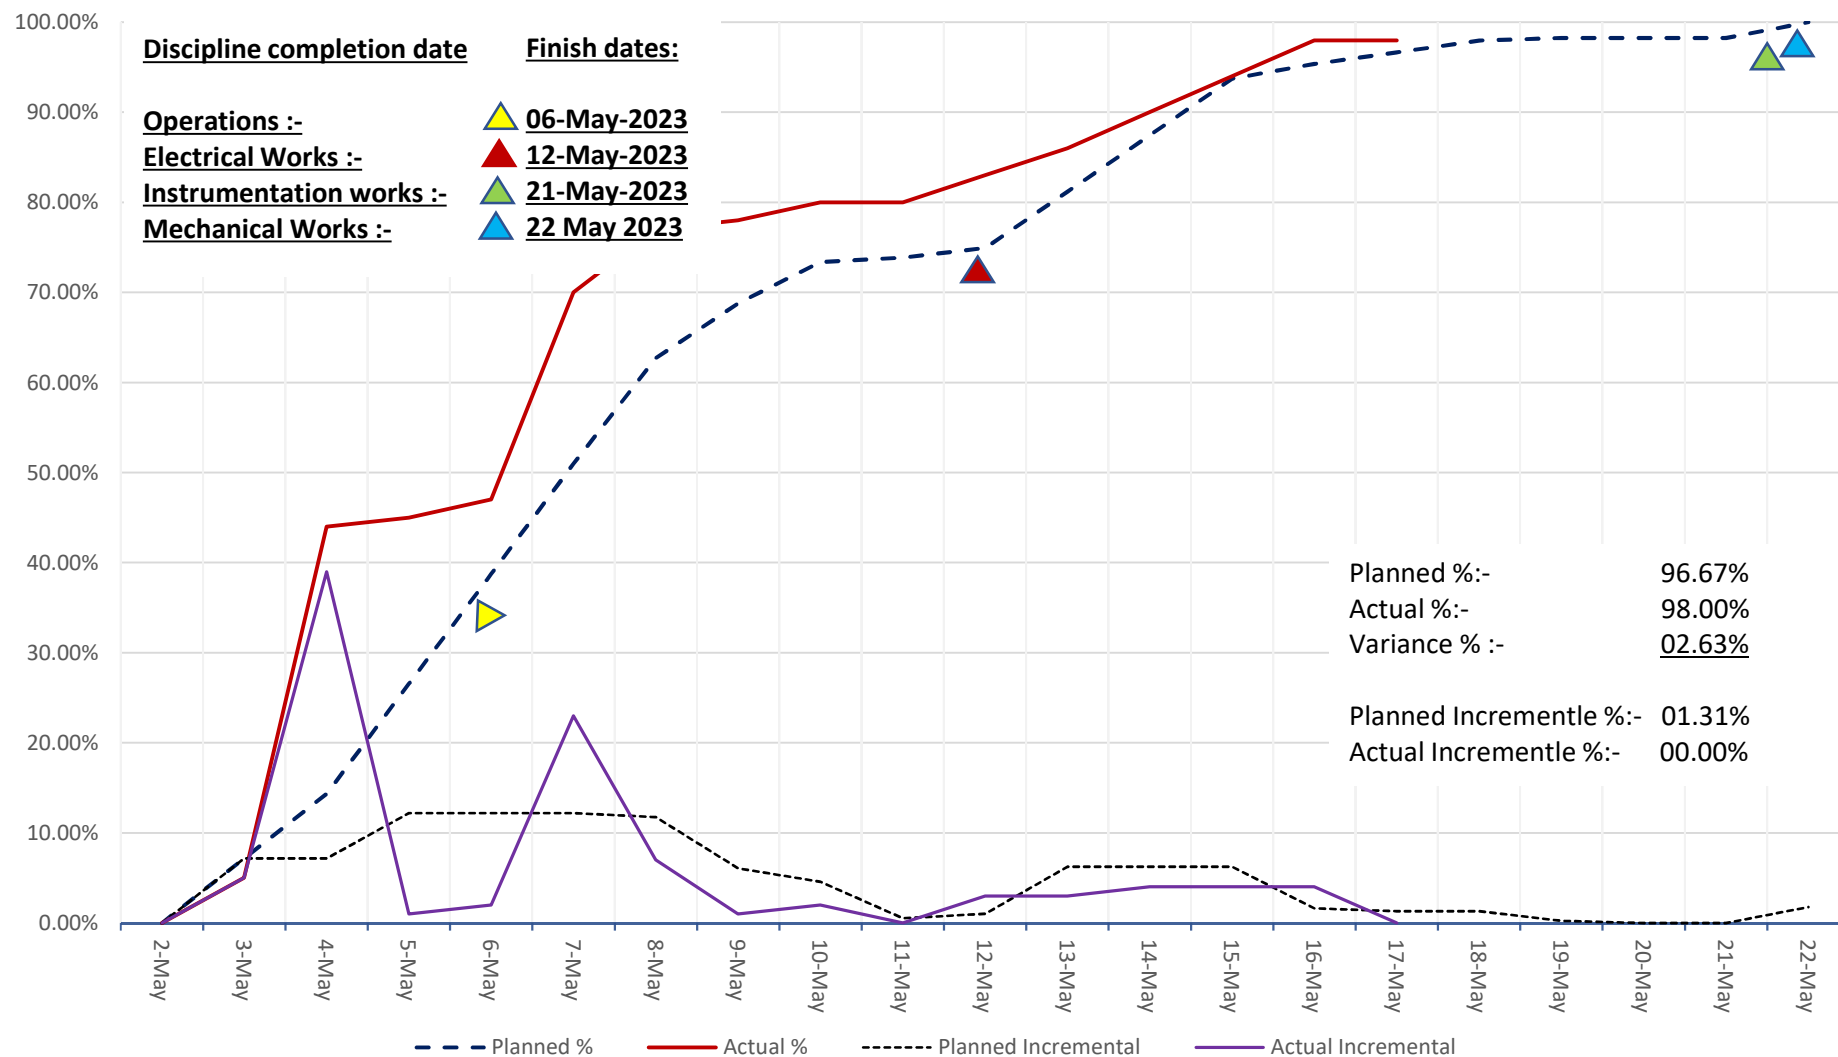




Botswana Ash (Pty) Ltd

MEA SYSTEM ABSORPTION - Update 17 May 2023

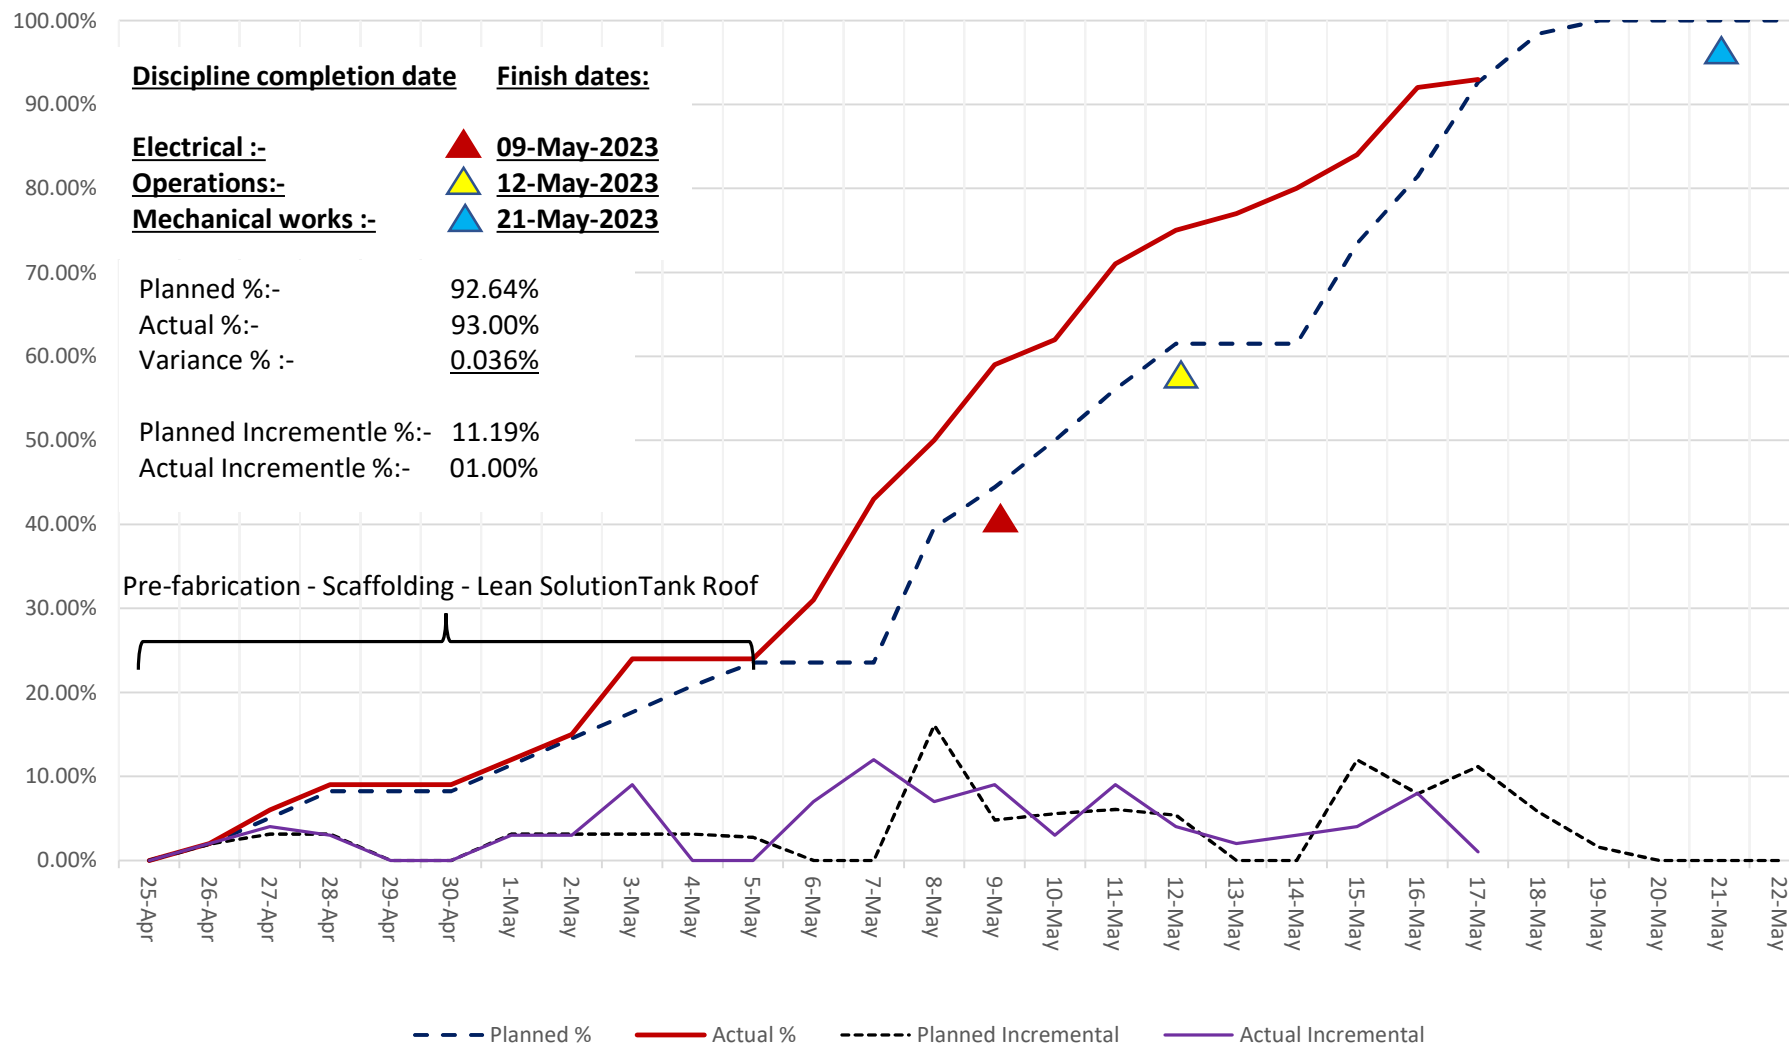




MEA SYSTEM STRIPPING - Update 17 May 2023

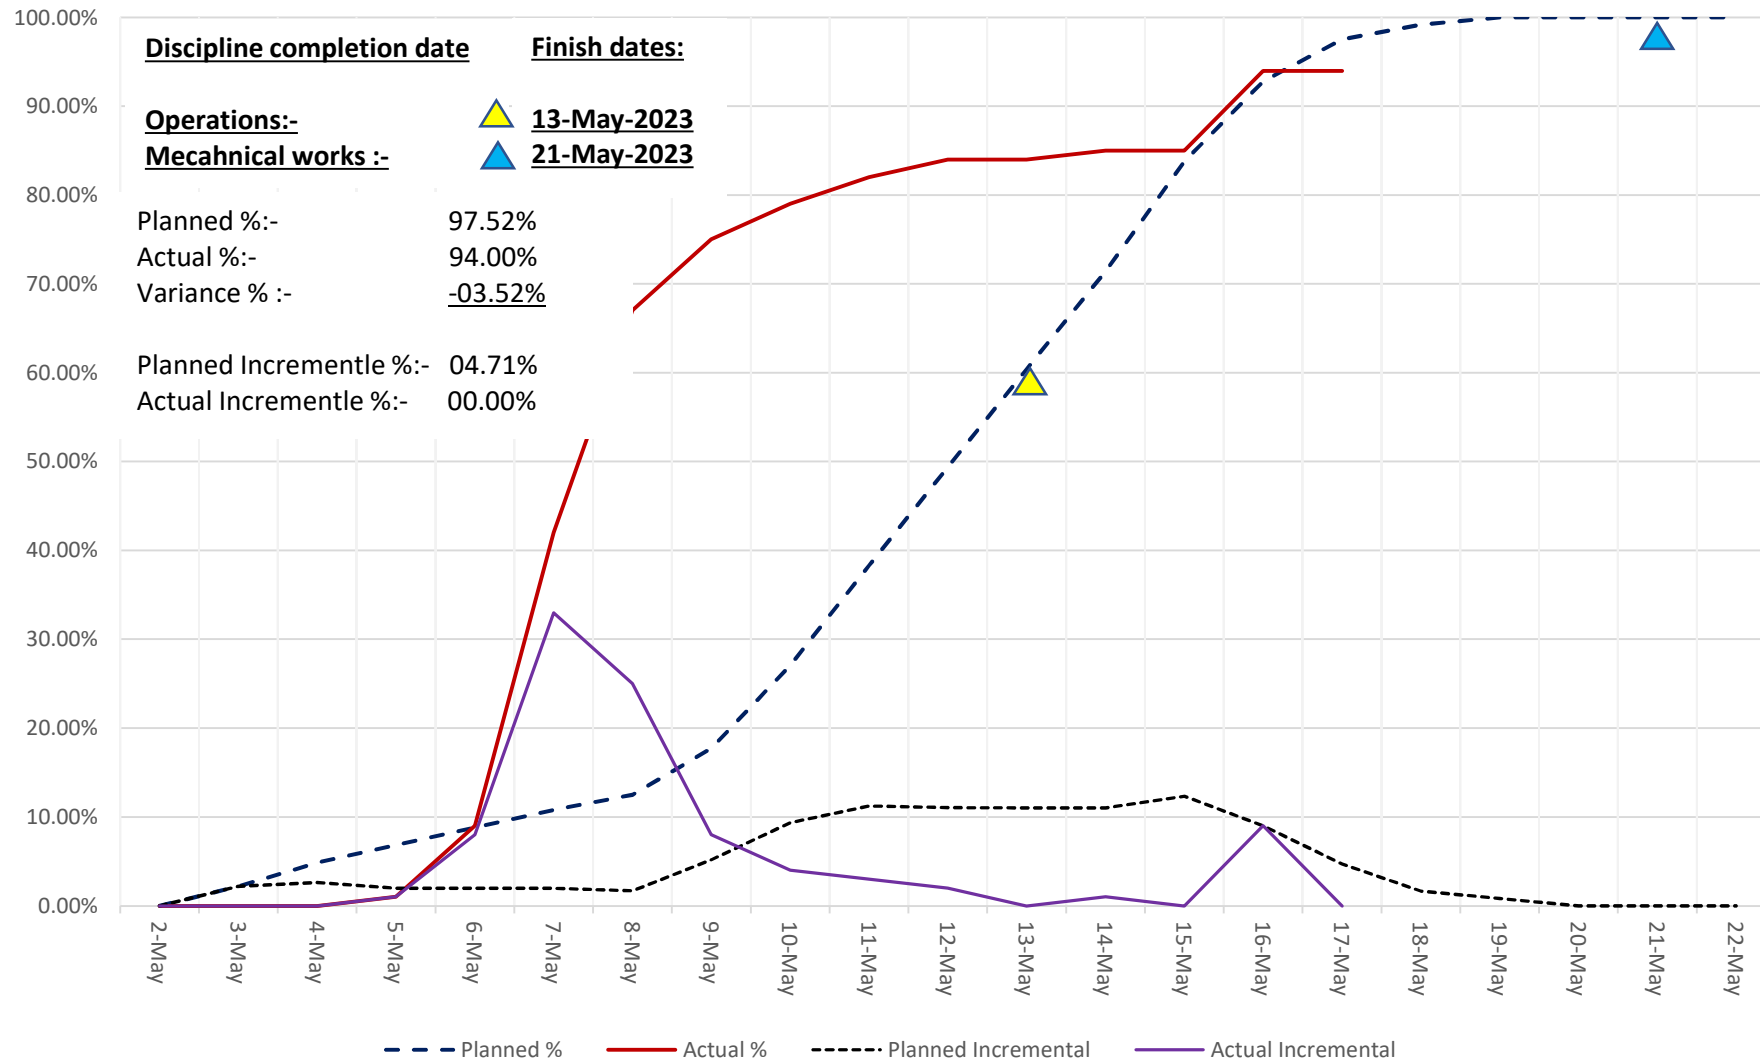




MEA SYSTEM RECLAIMER - Update 17 May 2023

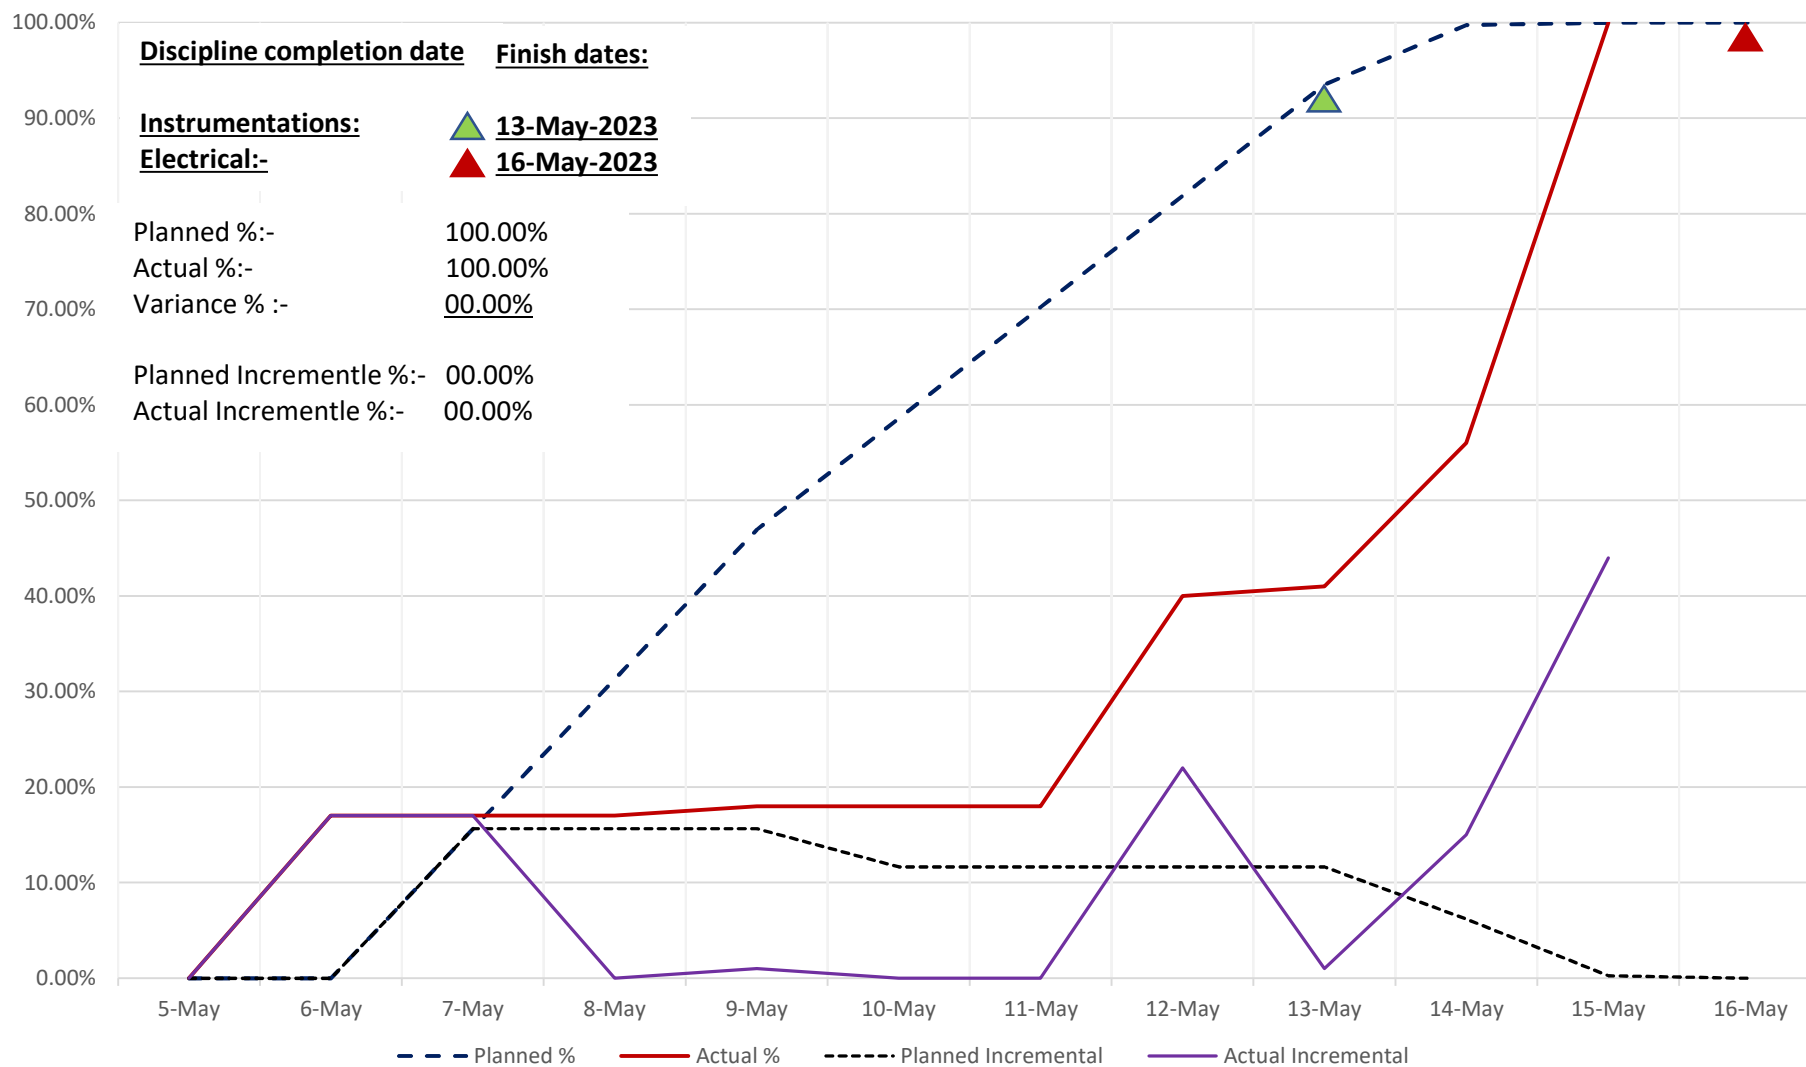




BOILER # 1 - Update 17 May 2023

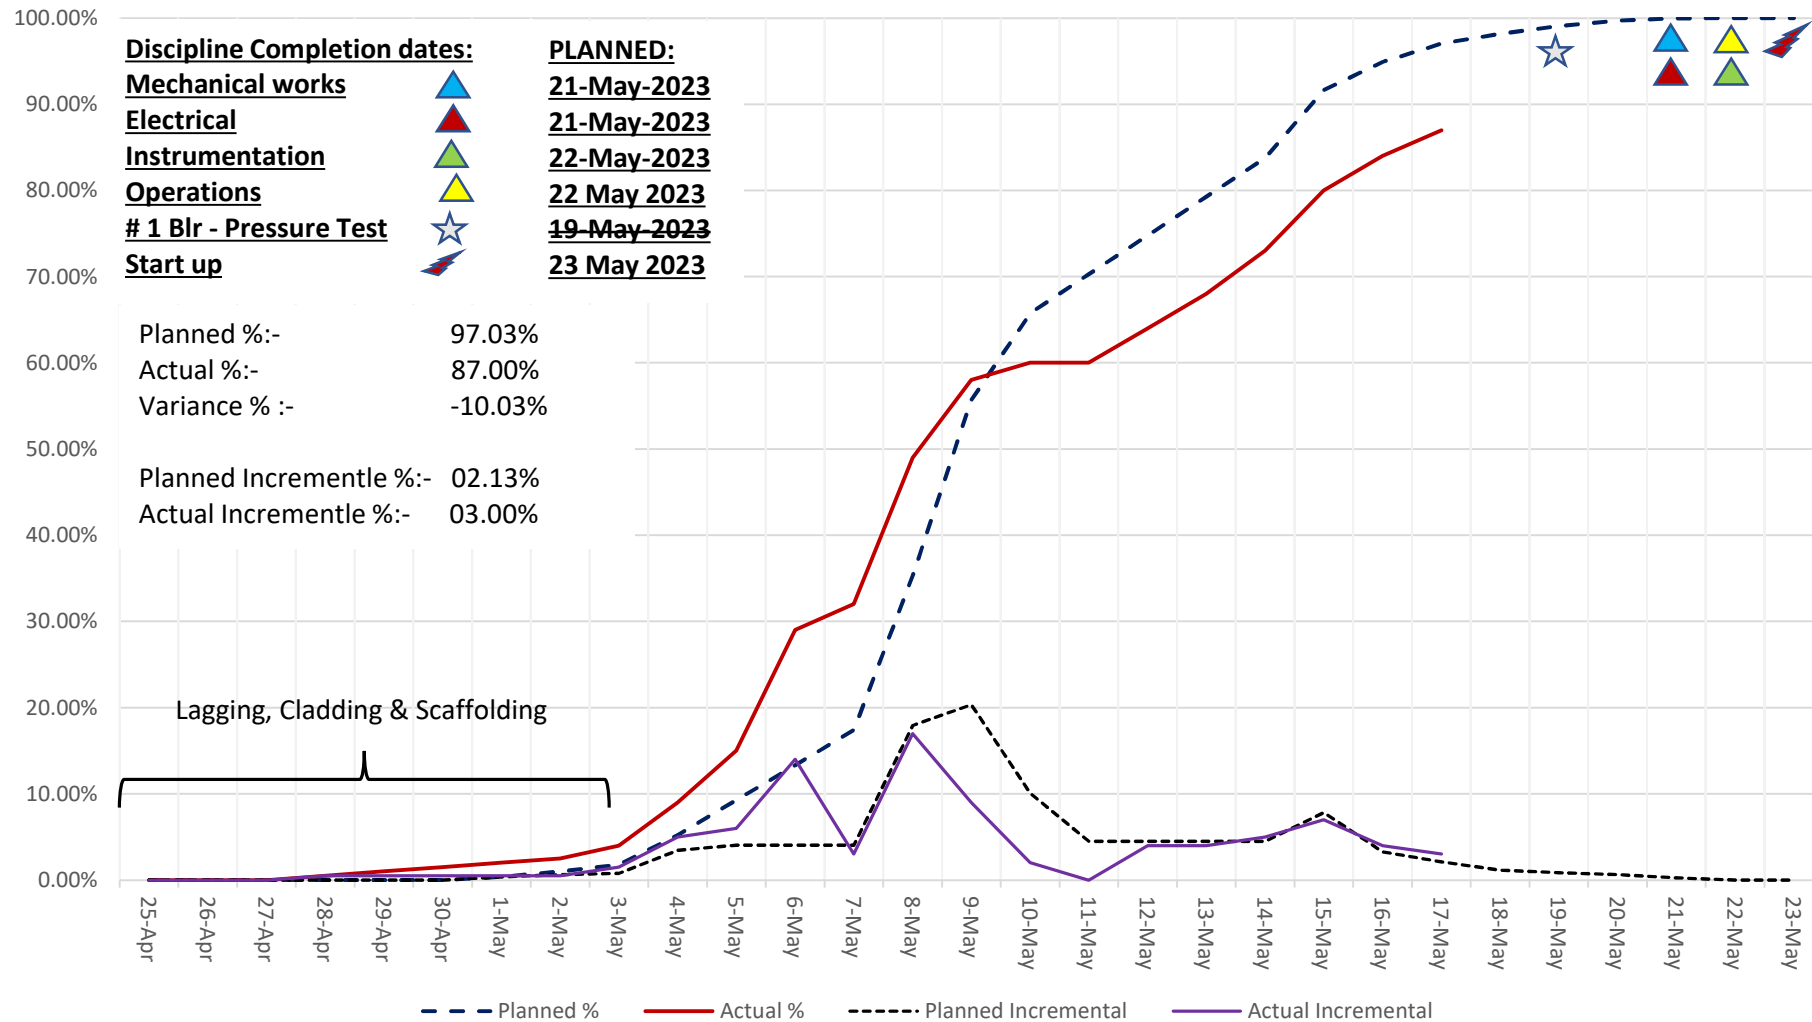





Botswana Ash (Pty) Ltd

BOILER # 2 - Update 17 May 2023

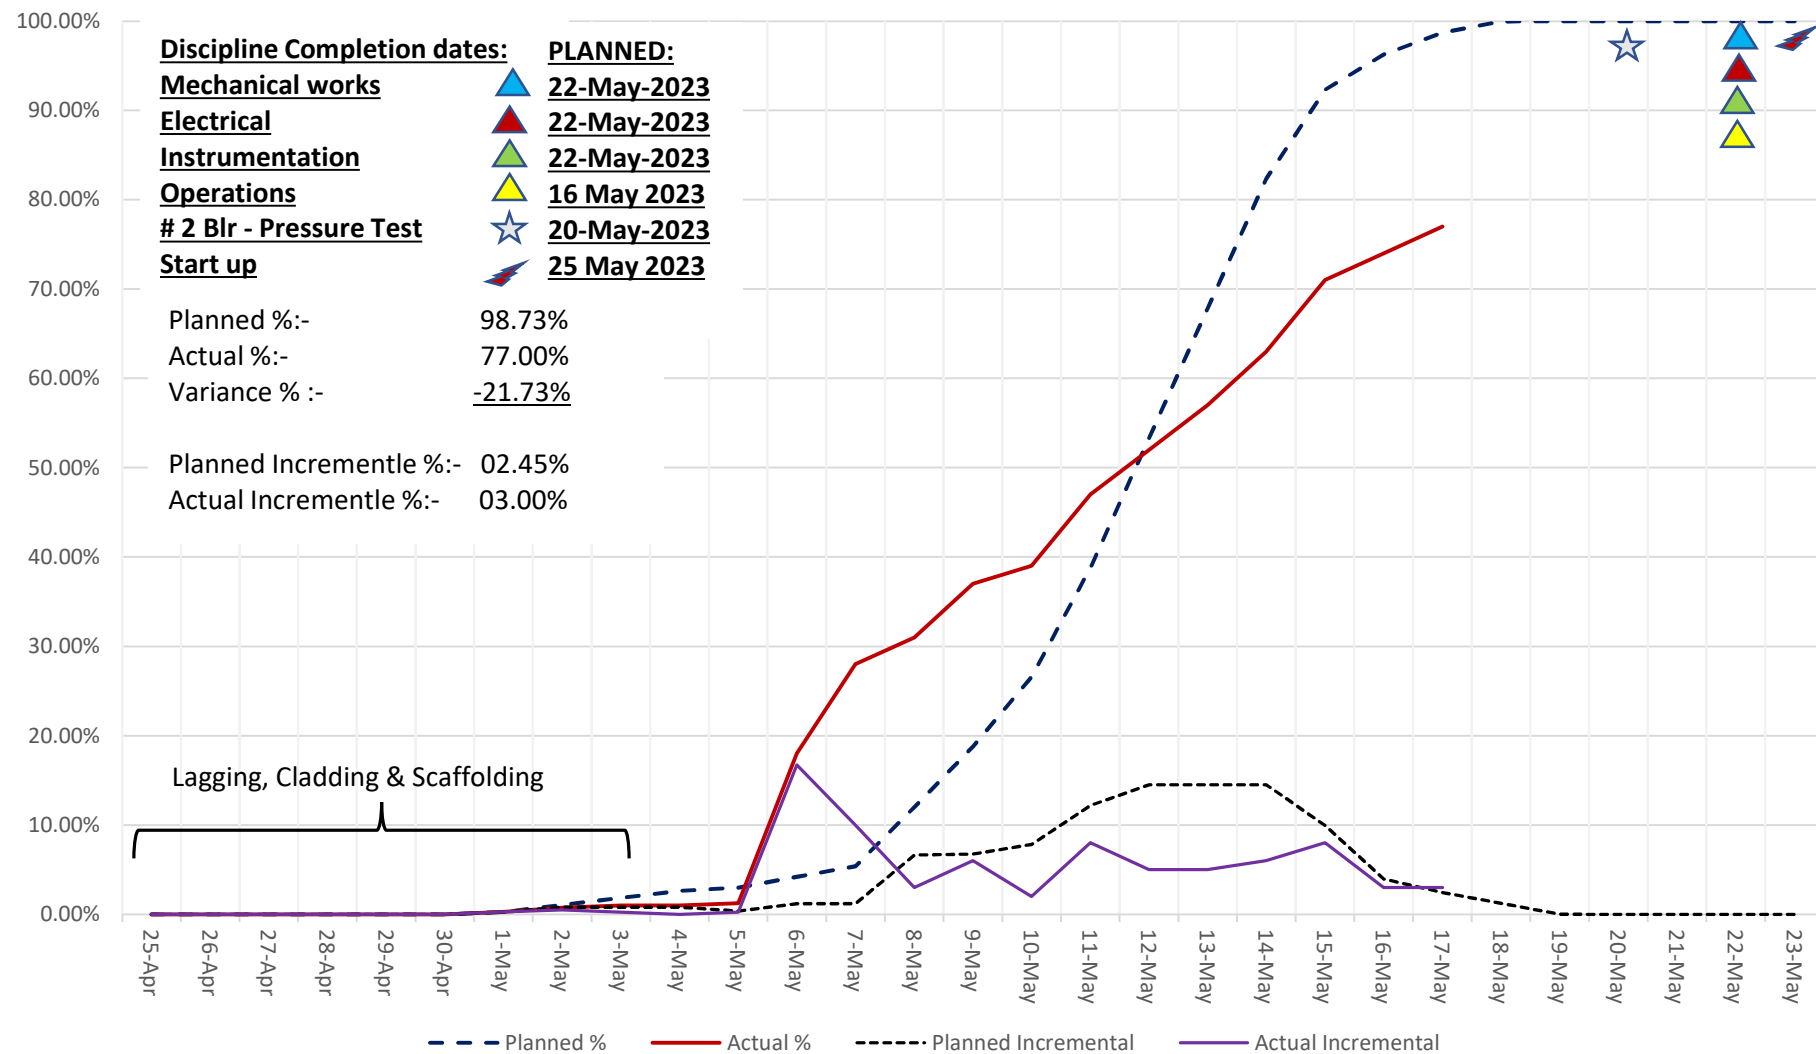




COAL HANDLING PLANT- Update 17 May 2023

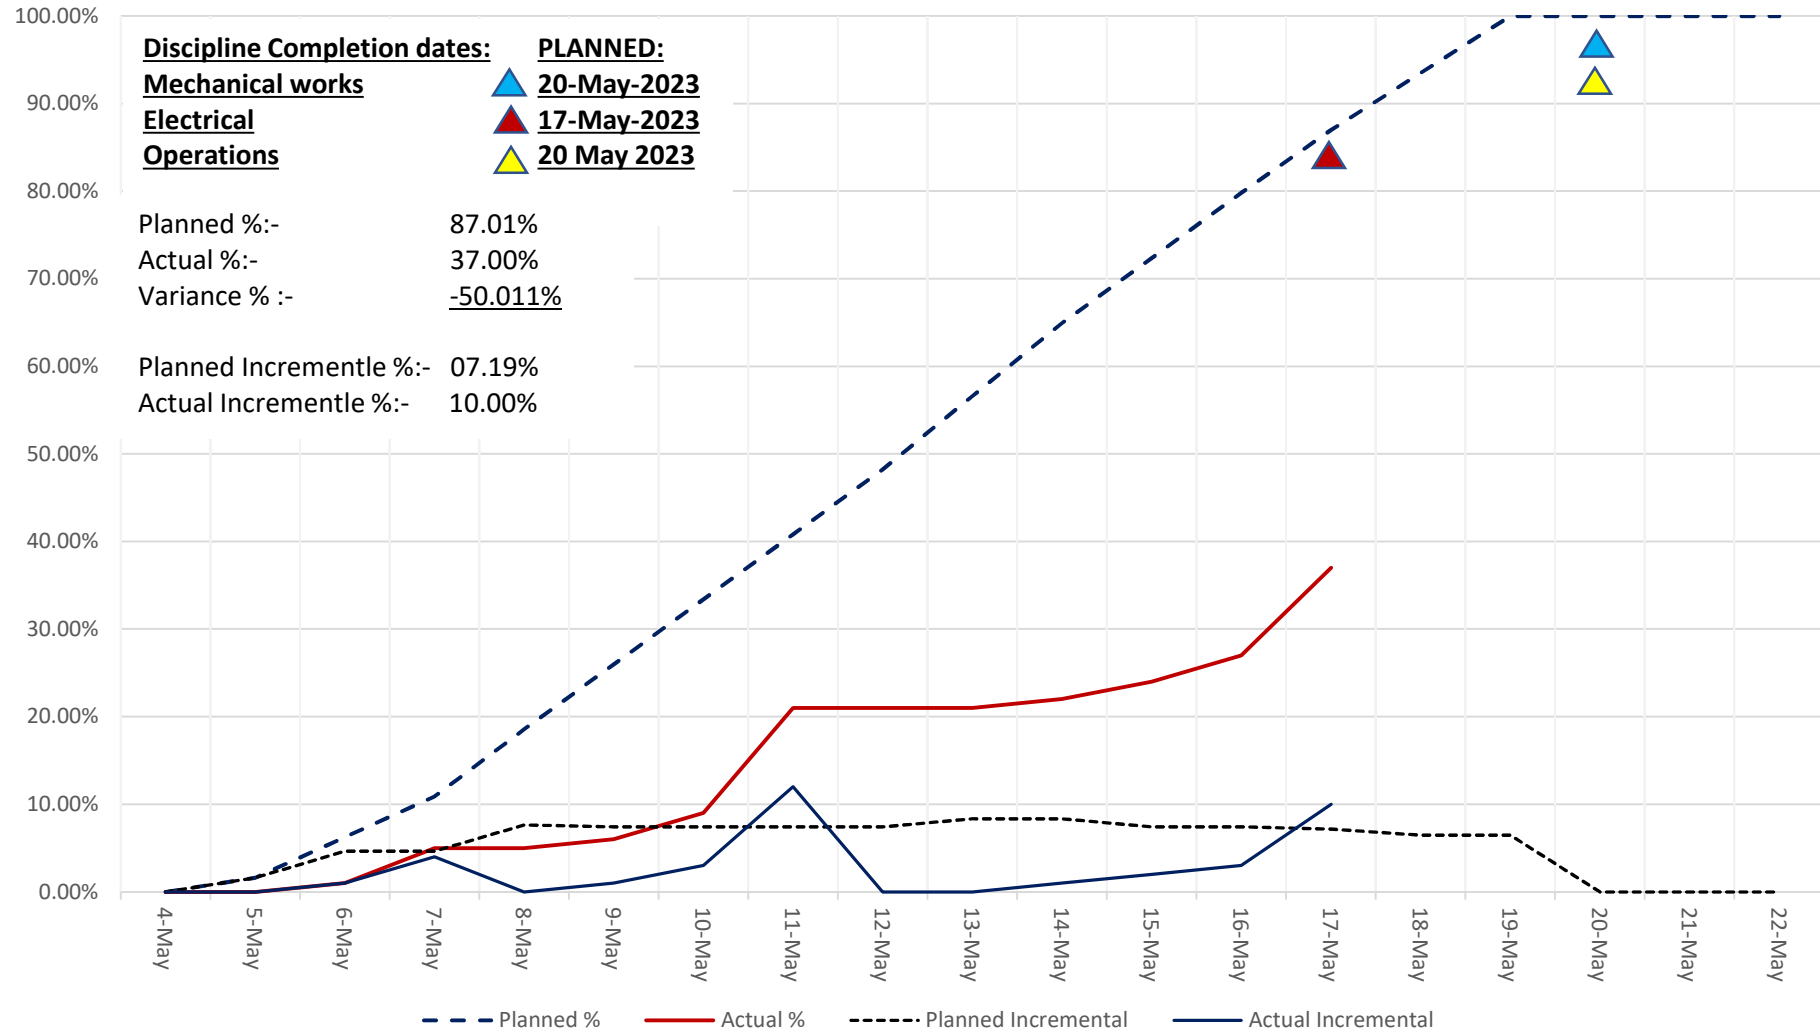



BOILER PLANT COMMON - Update 17 May 2023

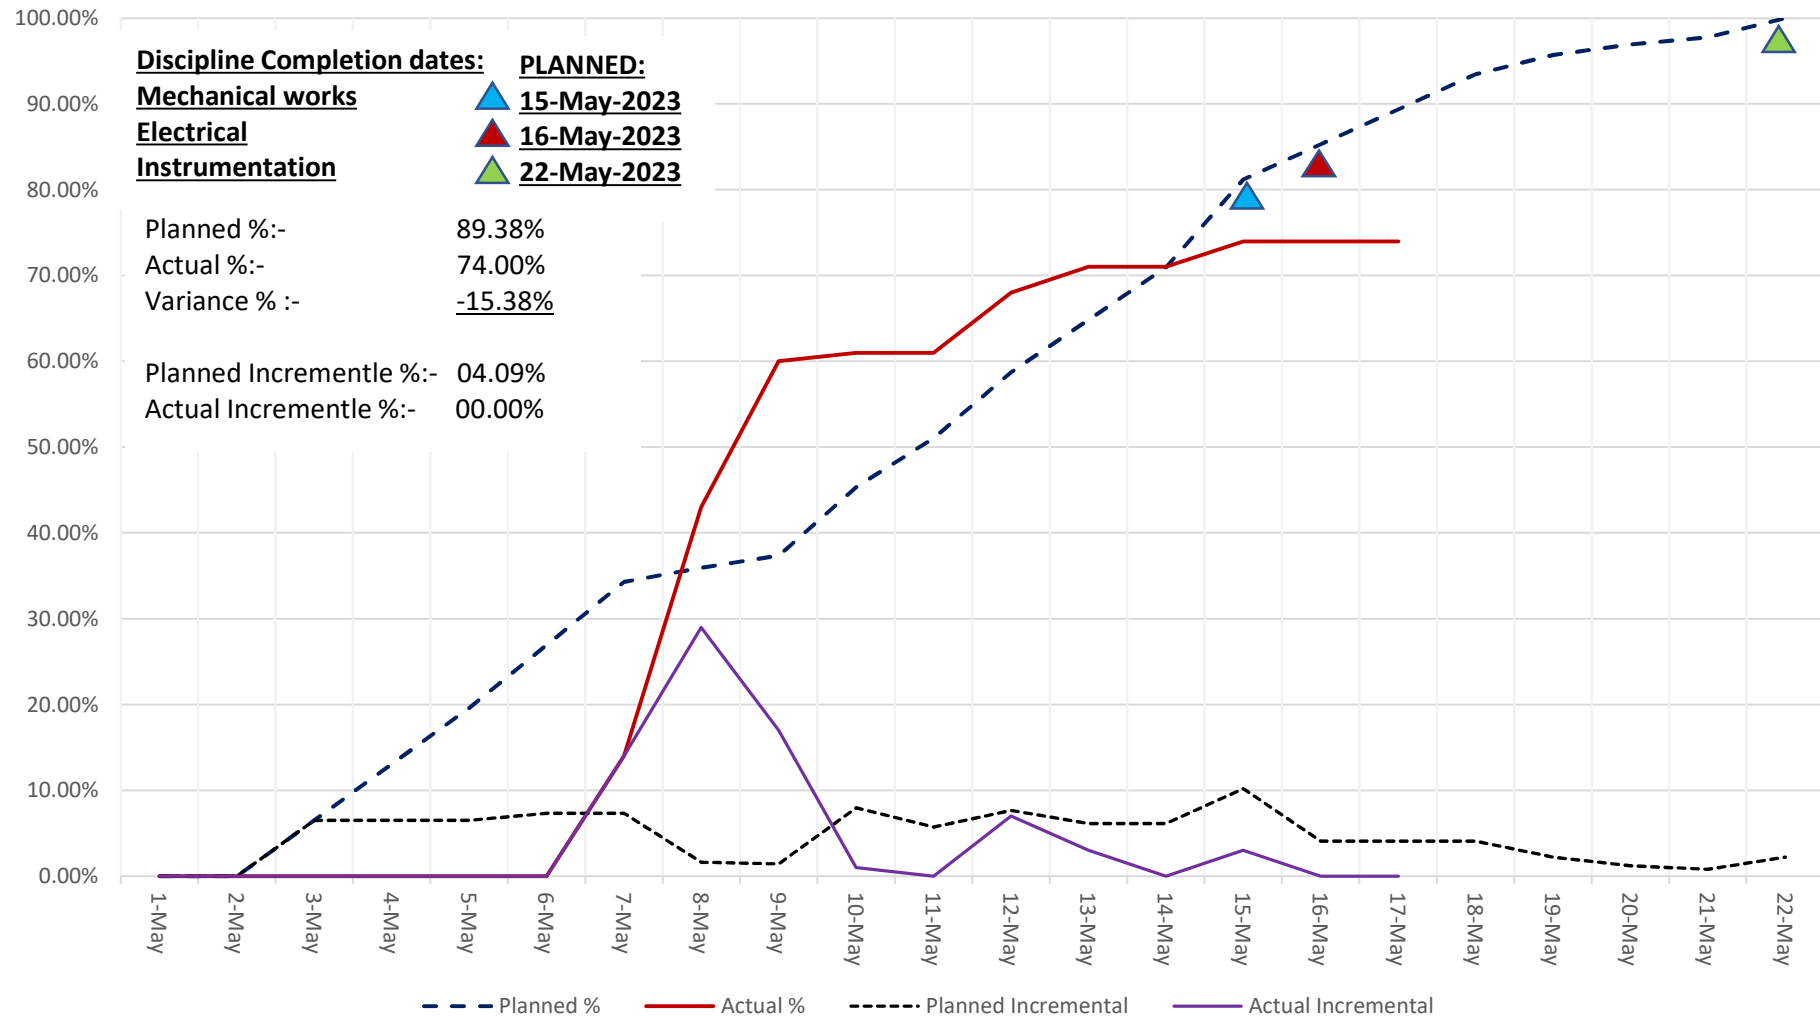



Botswana Ash (Pty) Ltd


WATER TREATMENT PLANT - Update 17 May 2023

Discipline Completion dates:

Operations	16-May-2023
Electrical	15-May-2023
Civils	19-May-2023
Mechanical works	22 May 2023


Planned %:- 93.17%
Actual %:- 79.00%
Variance % :- -14.17%

Planned Incrementle %:- 07.01%
Actual Incrementle %:- 00.00%

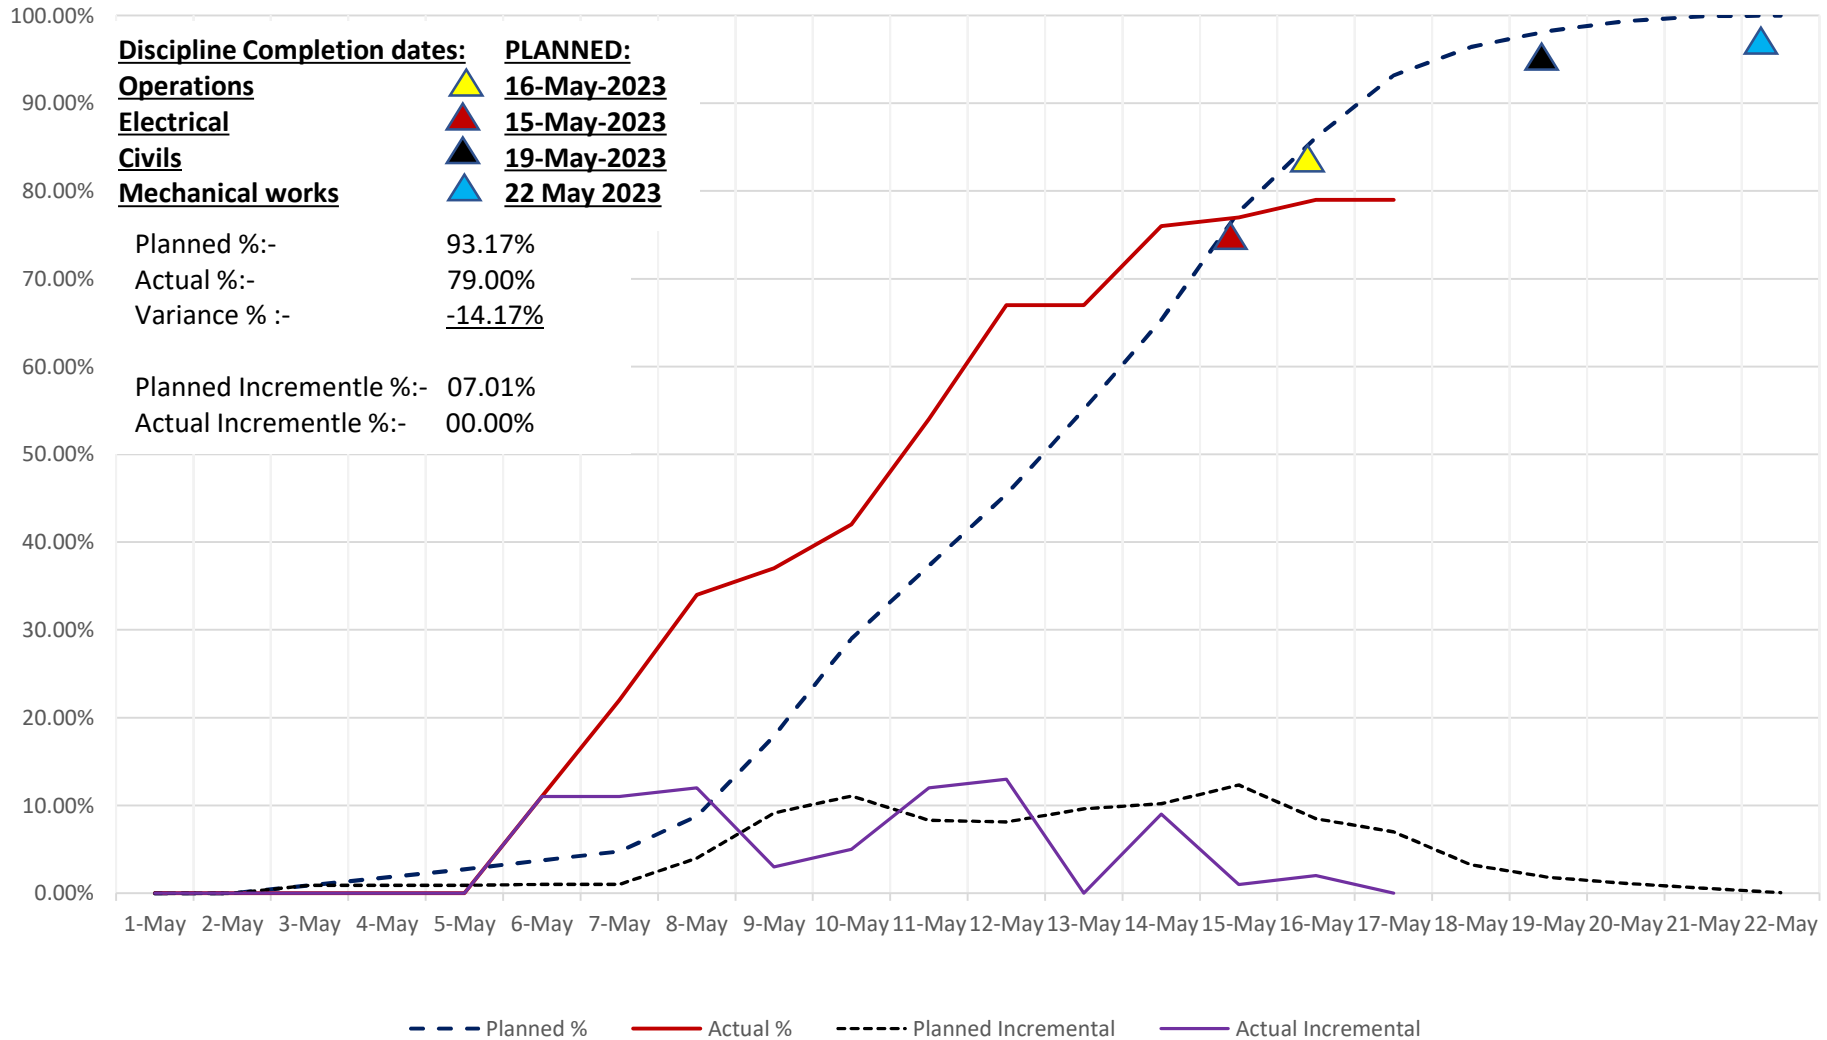




INSTRUMENT & COMPRESSED AIR - Update 17 May 2023

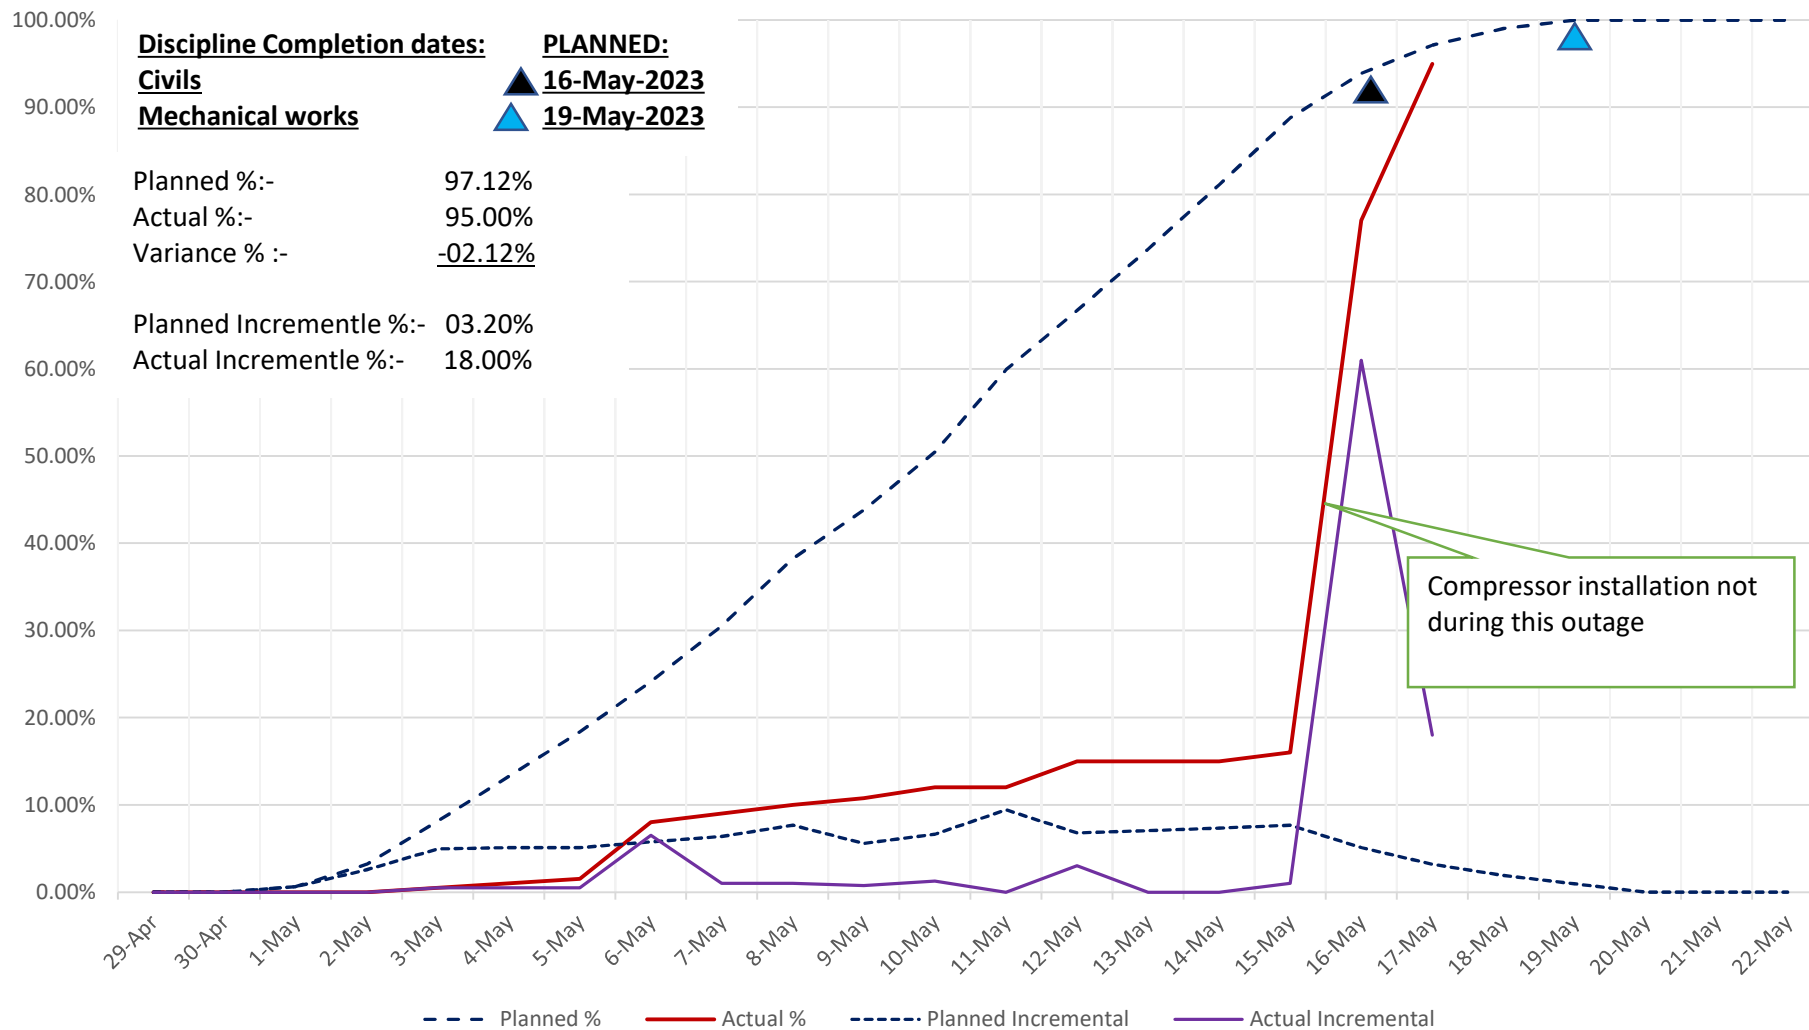




STEAM AND CONDENSATE- Update 17 May 2023

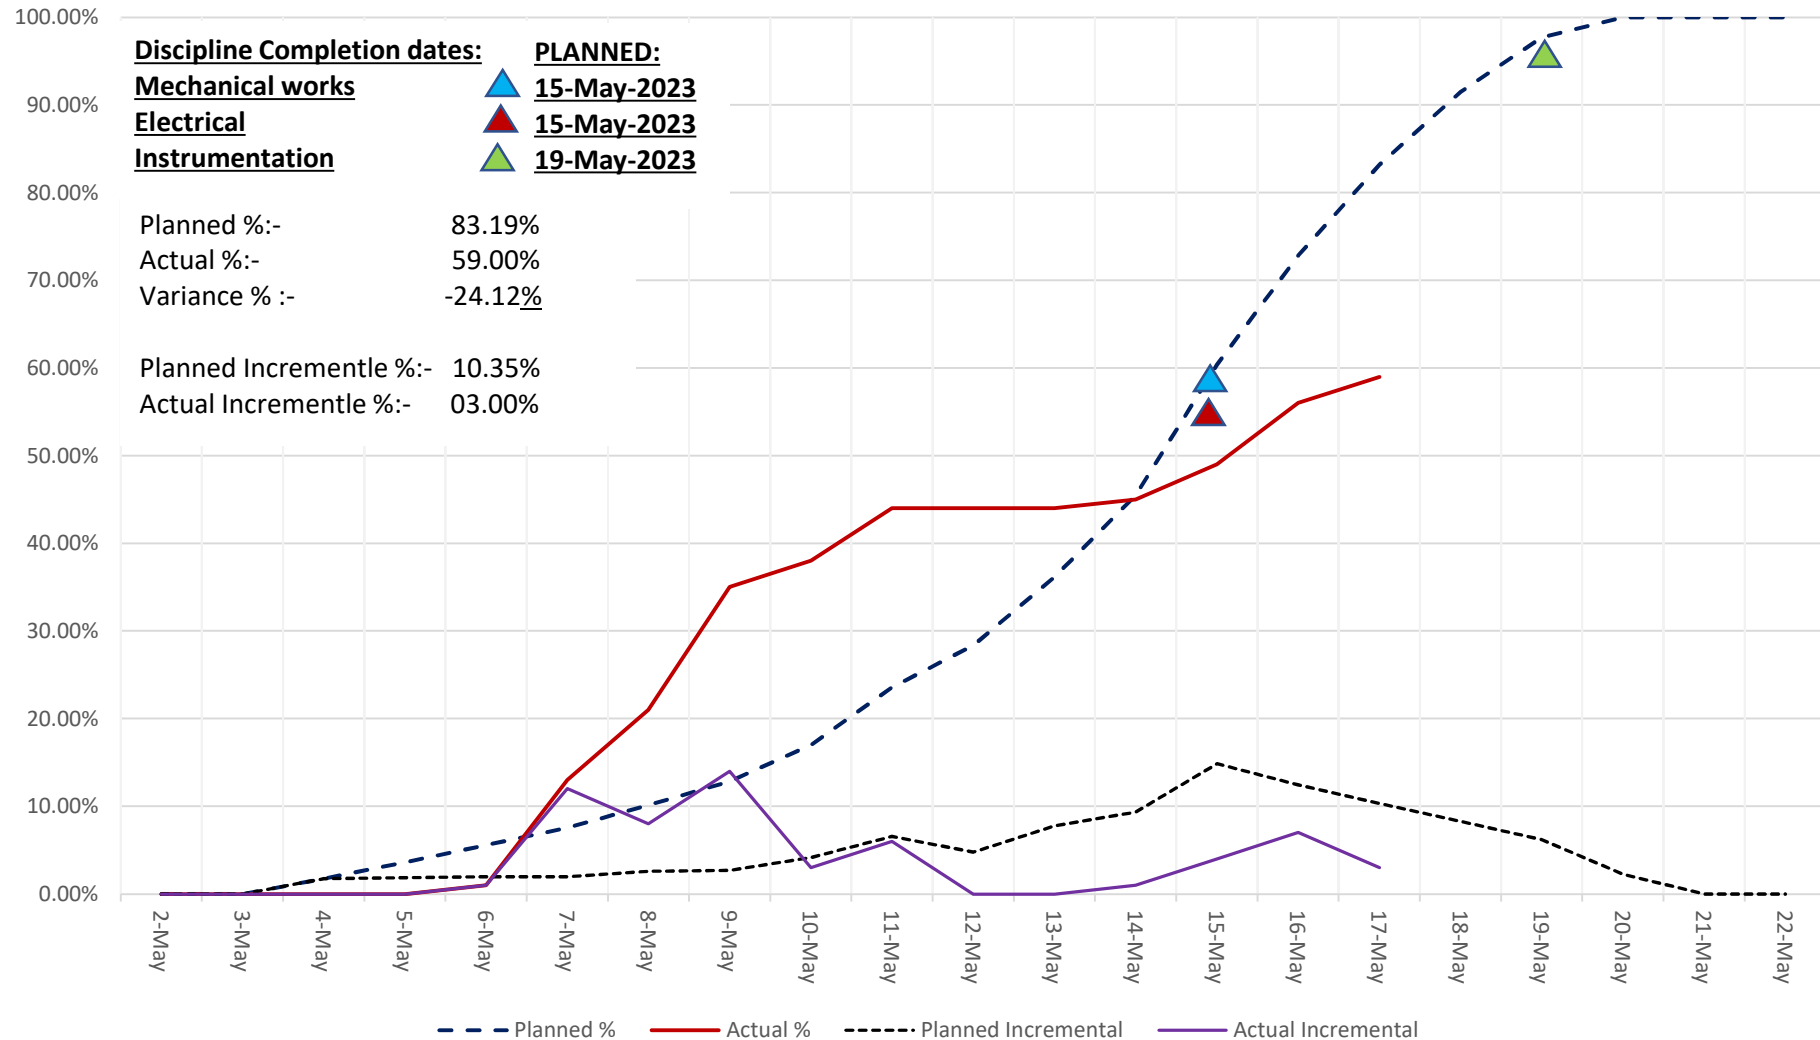




TURBINE - Update 17 May 2023

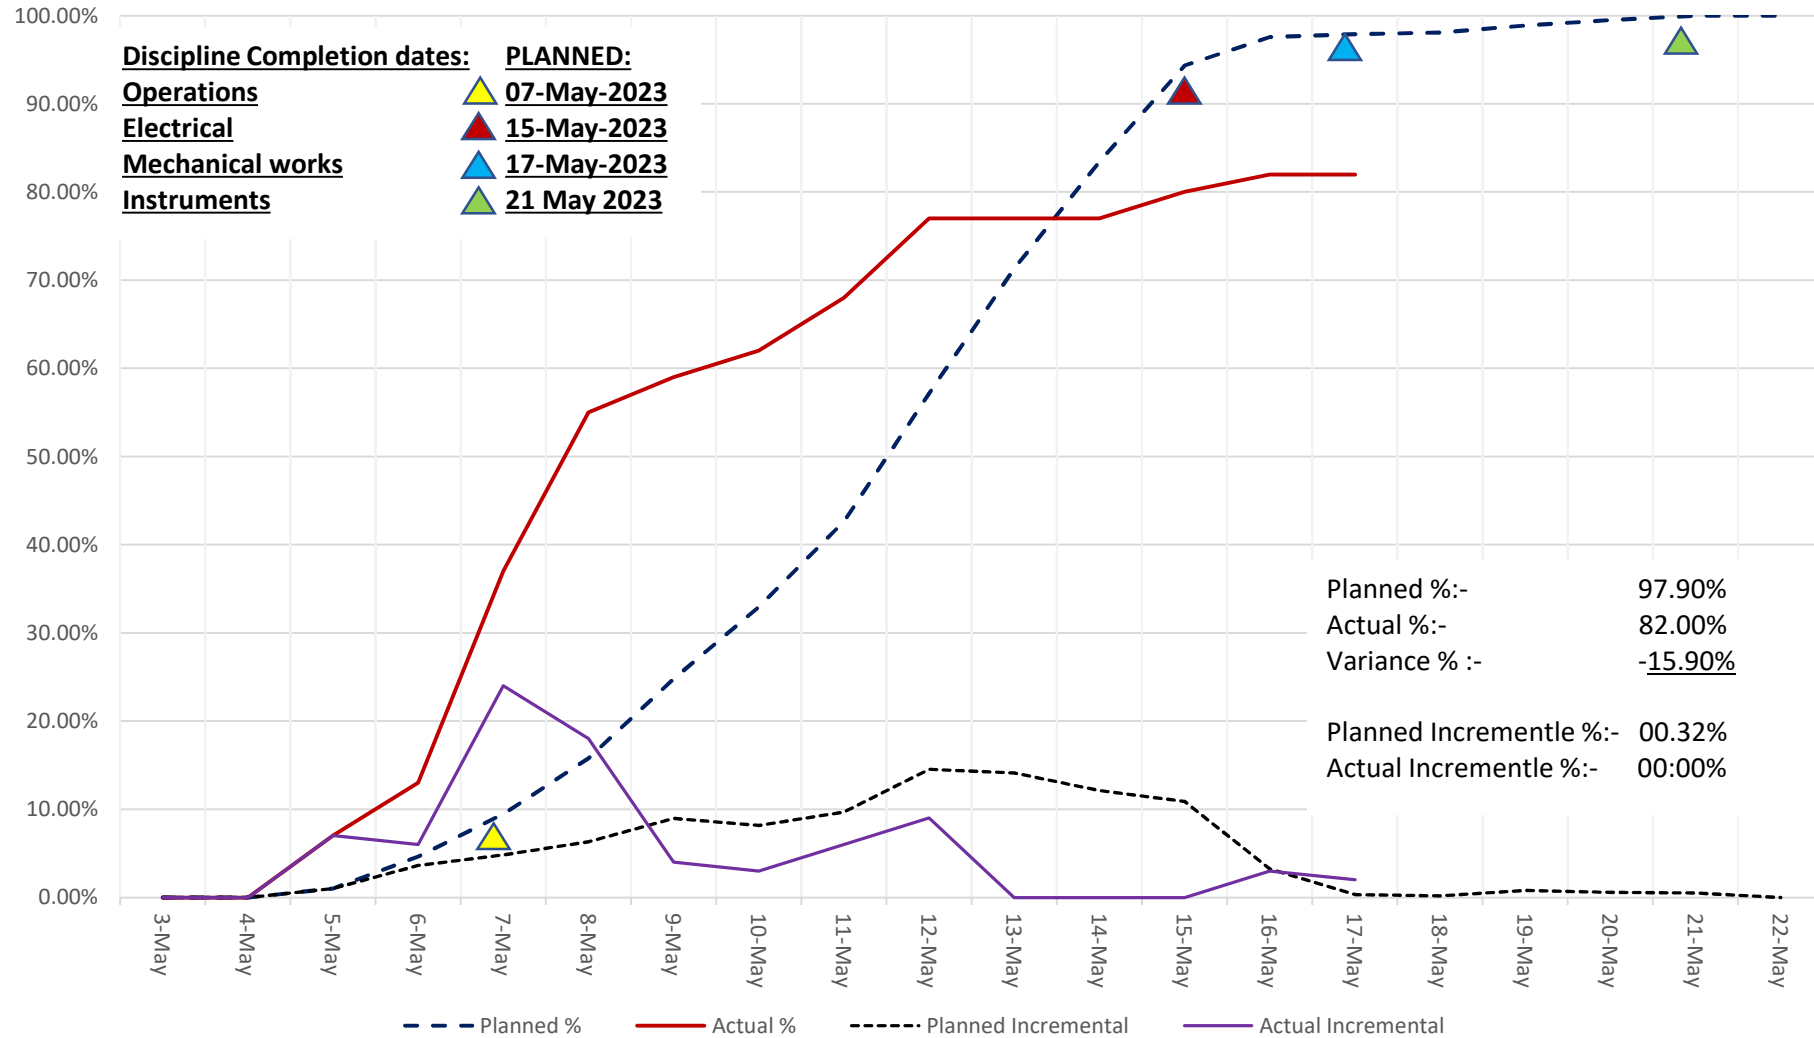



MV RETICULATION - Update 17 May 2023

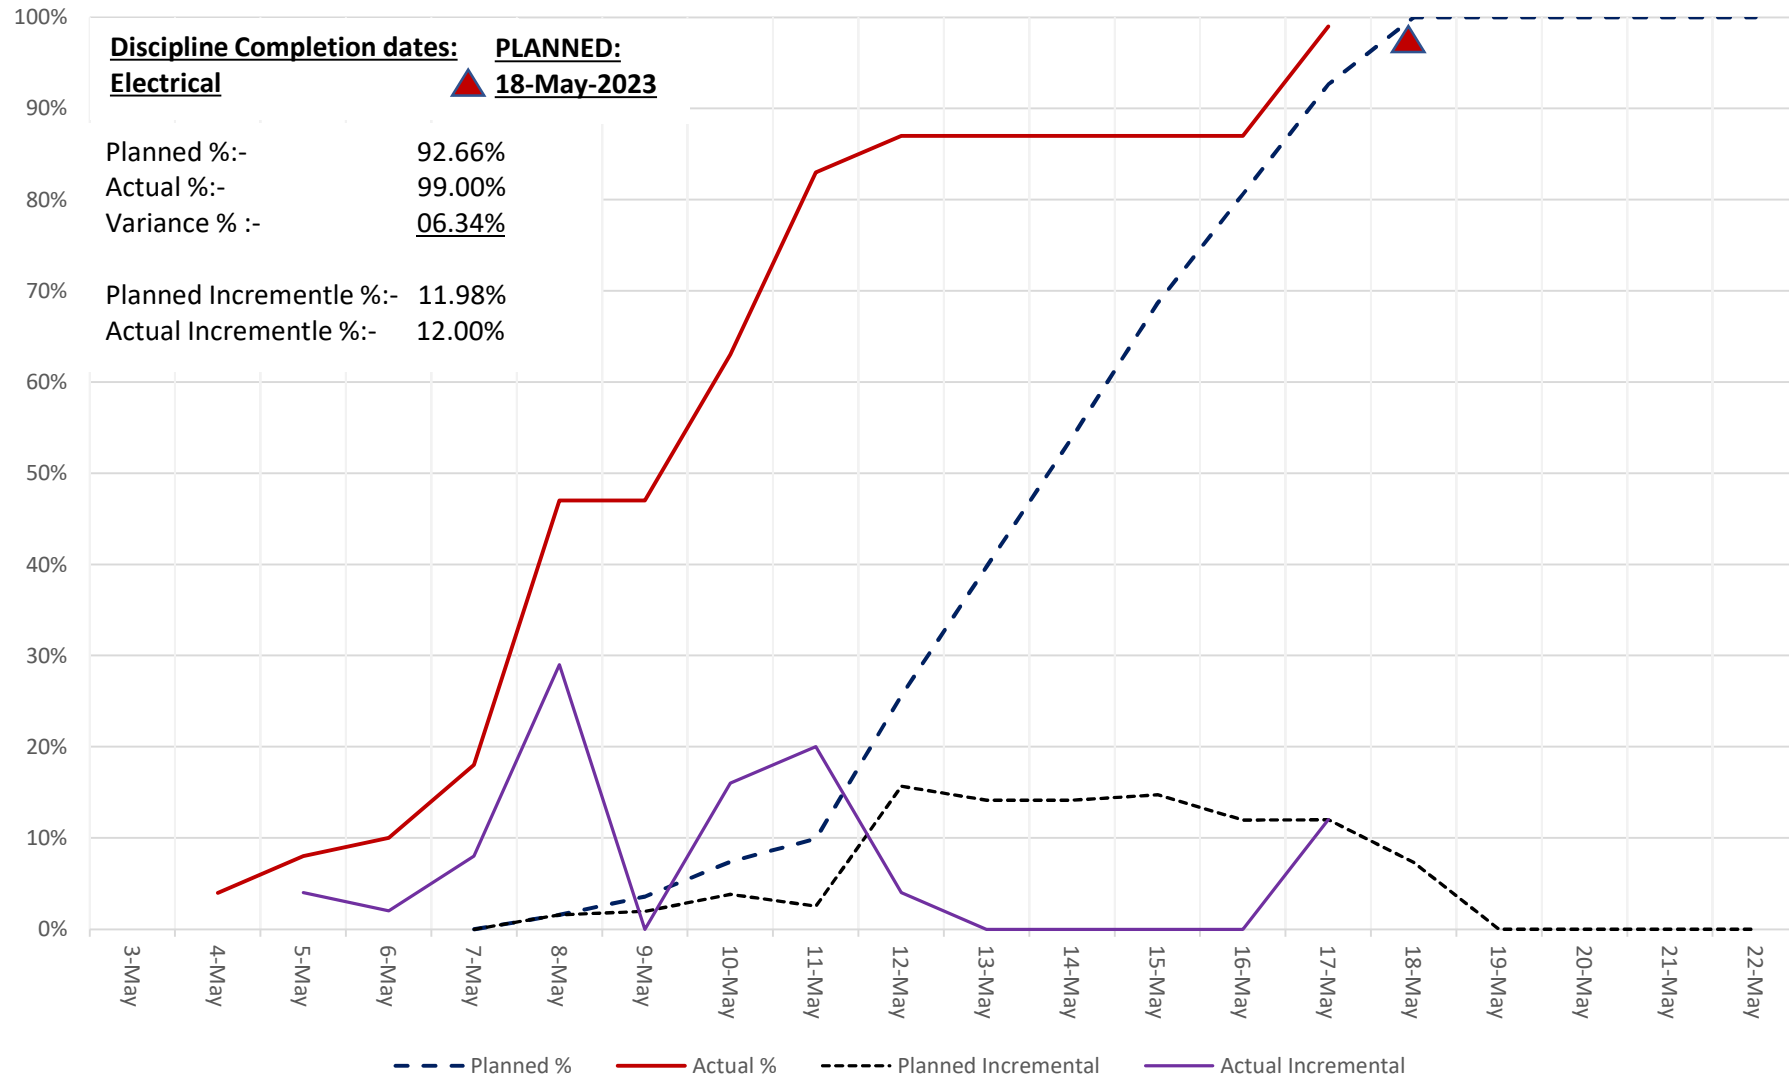



LV RETICULATION - Update 17 May 2023

Discipline Completion dates: **PLANNED:**
Electrical ▲ **18-May-2023**

Planned %:- 90.56%
Actual %:- 84.00%
Variance % :- -06.56%

Planned Incrementle %:- 12.98%
Actual Incrementle %:- 23.00%

