




BOTSWANA - BOTASH REFURBISHMENT PROJECT 2023 - UTILITY PLANT

Update:- 20 May 2023

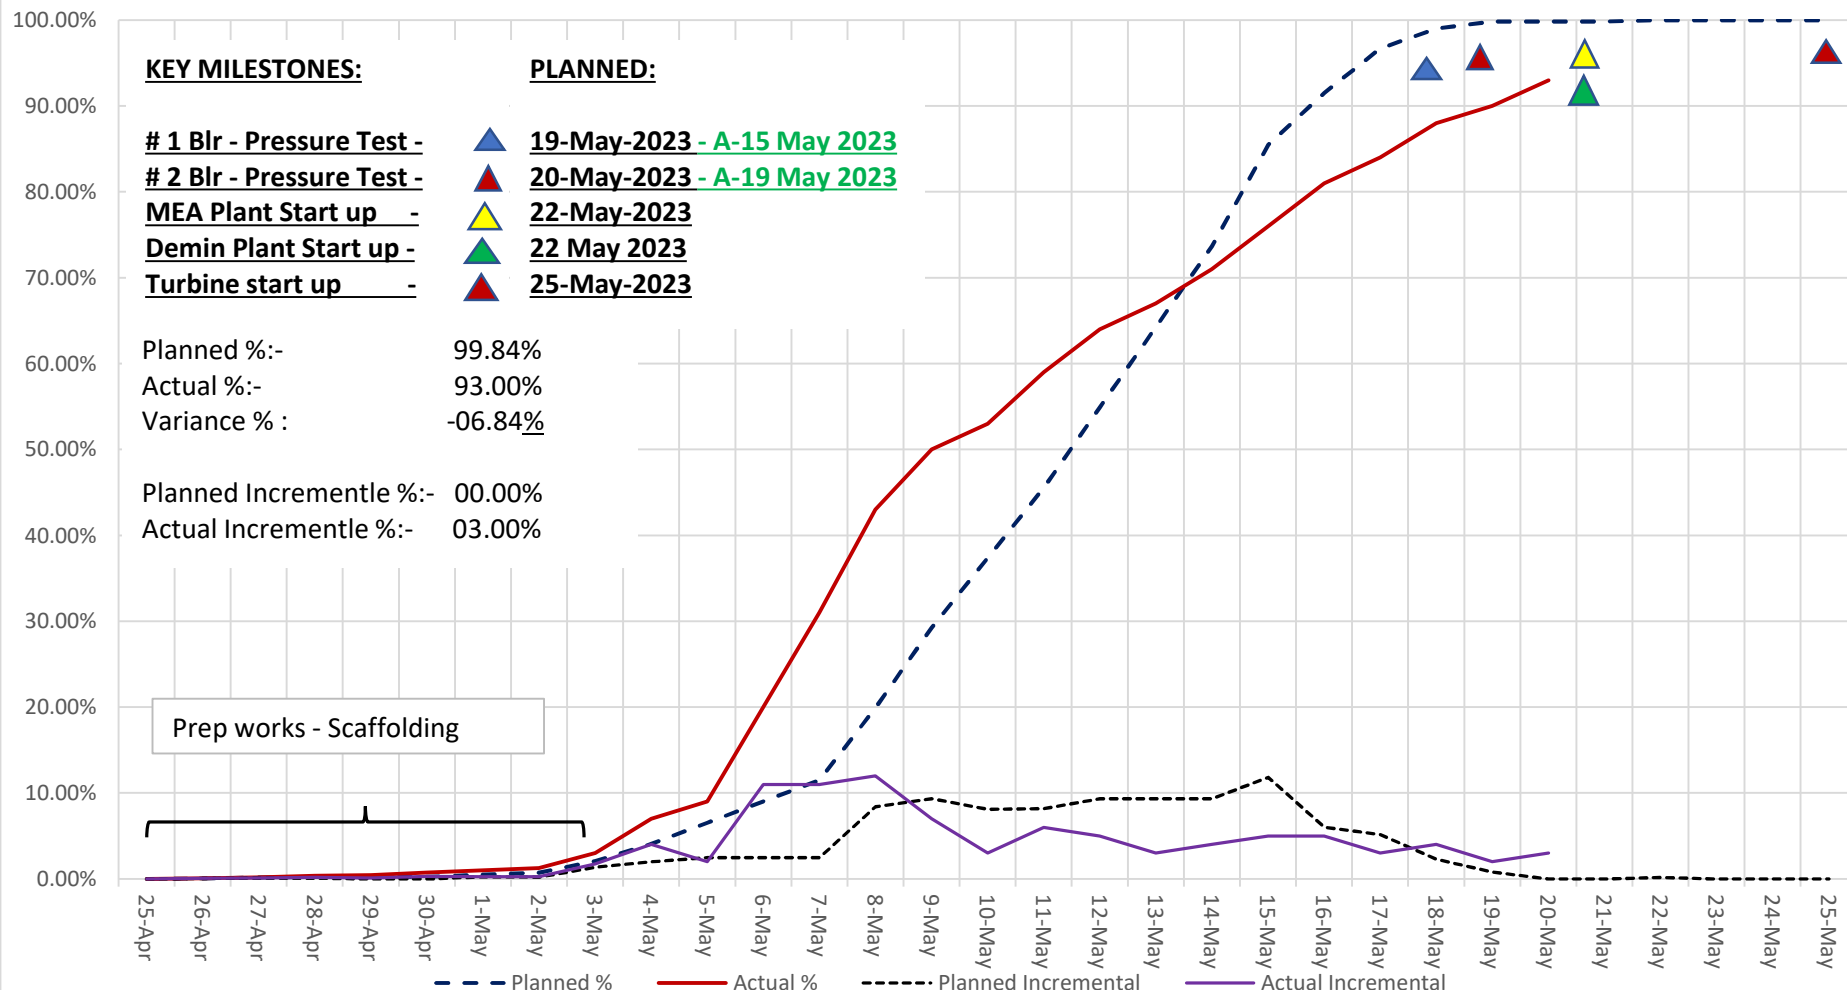

Discipline completion date

Operations :-


Electrical Works :-

Instrumentation works :-

 21-May-2023


Mechanical Works :-

 22 May 2023

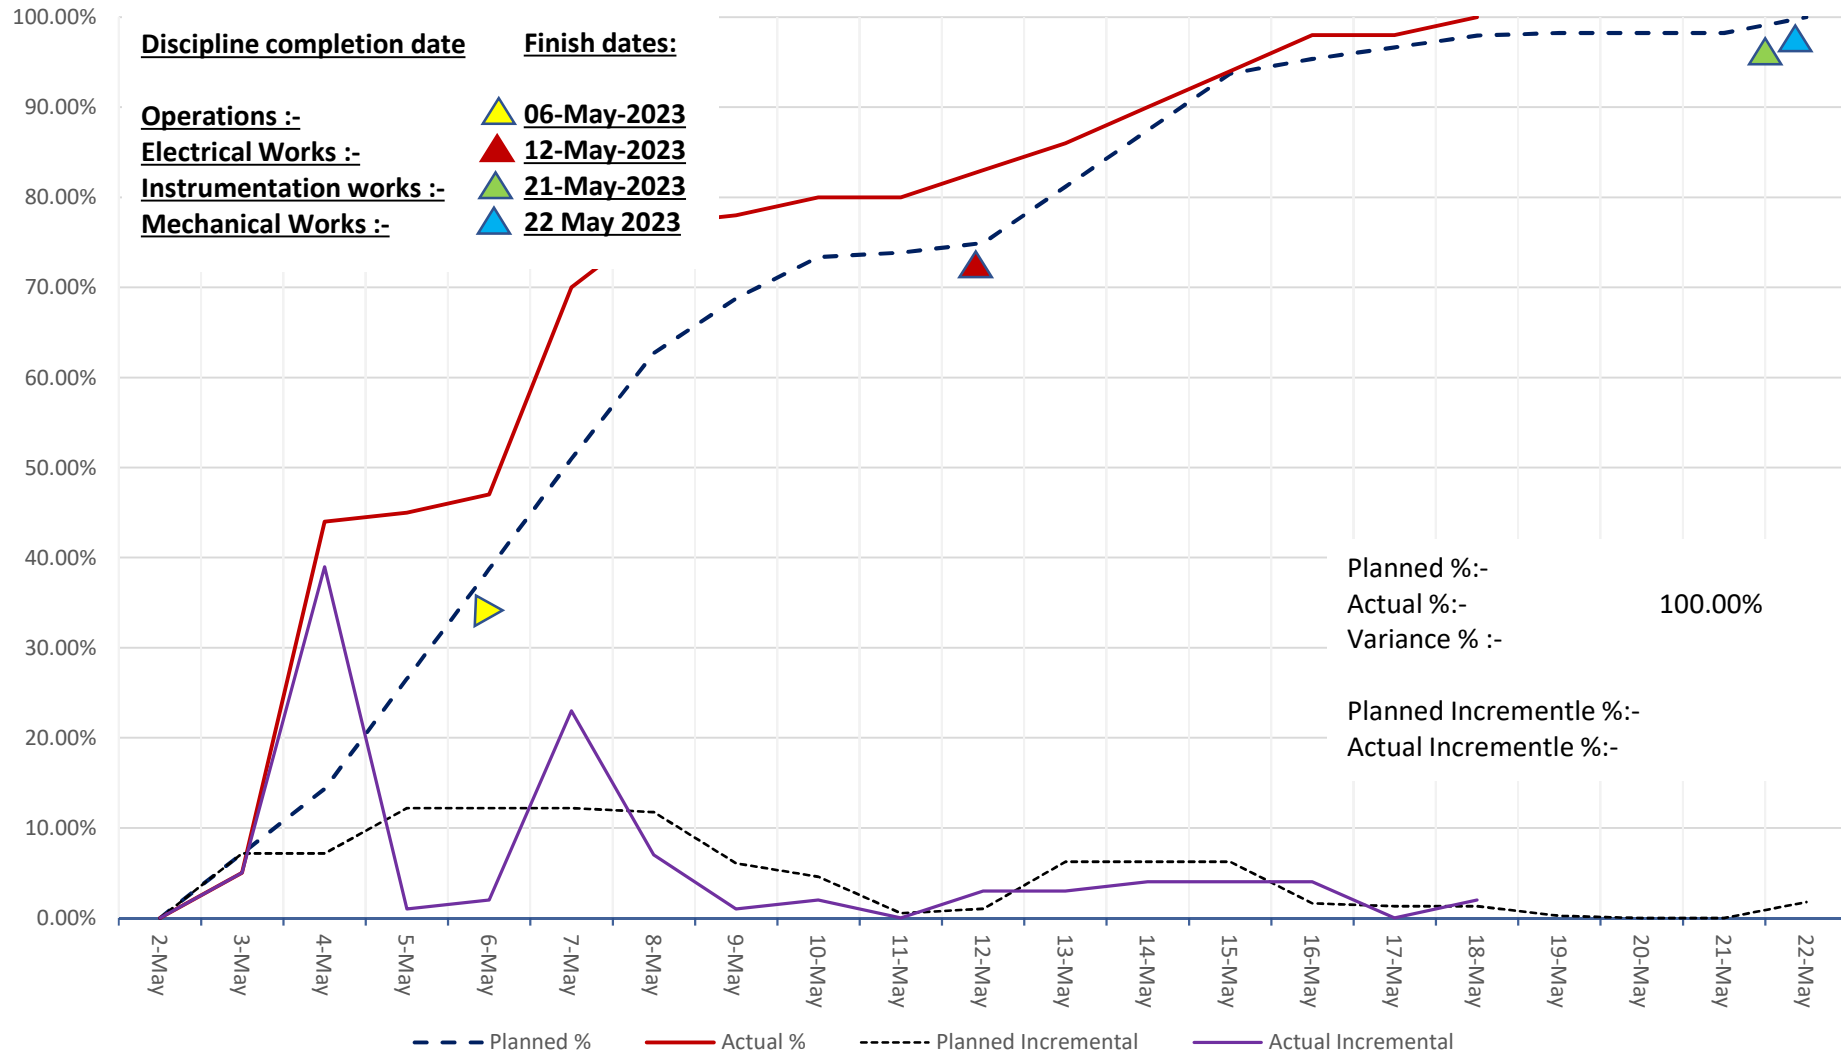




MEA SYSTEM ABSORPTION - Update 20 May 2023

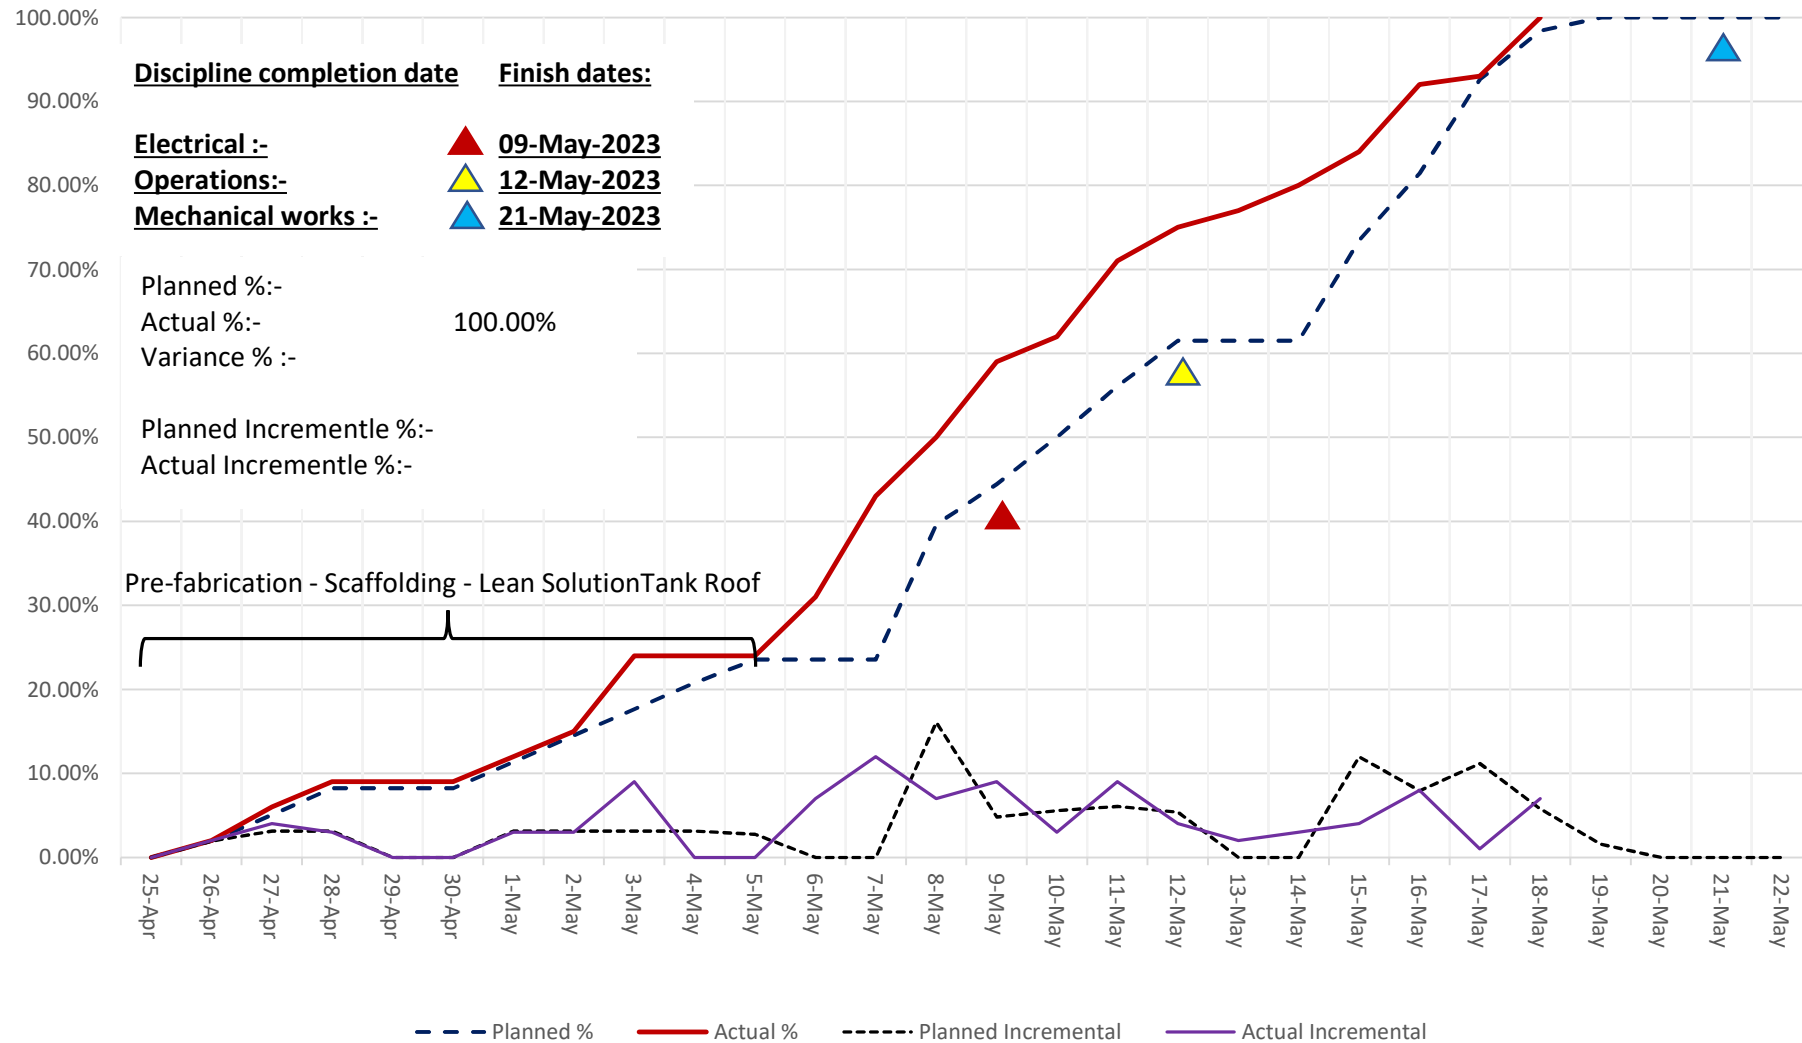




MEA SYSTEM STRIPPING - Update 20 May 2023

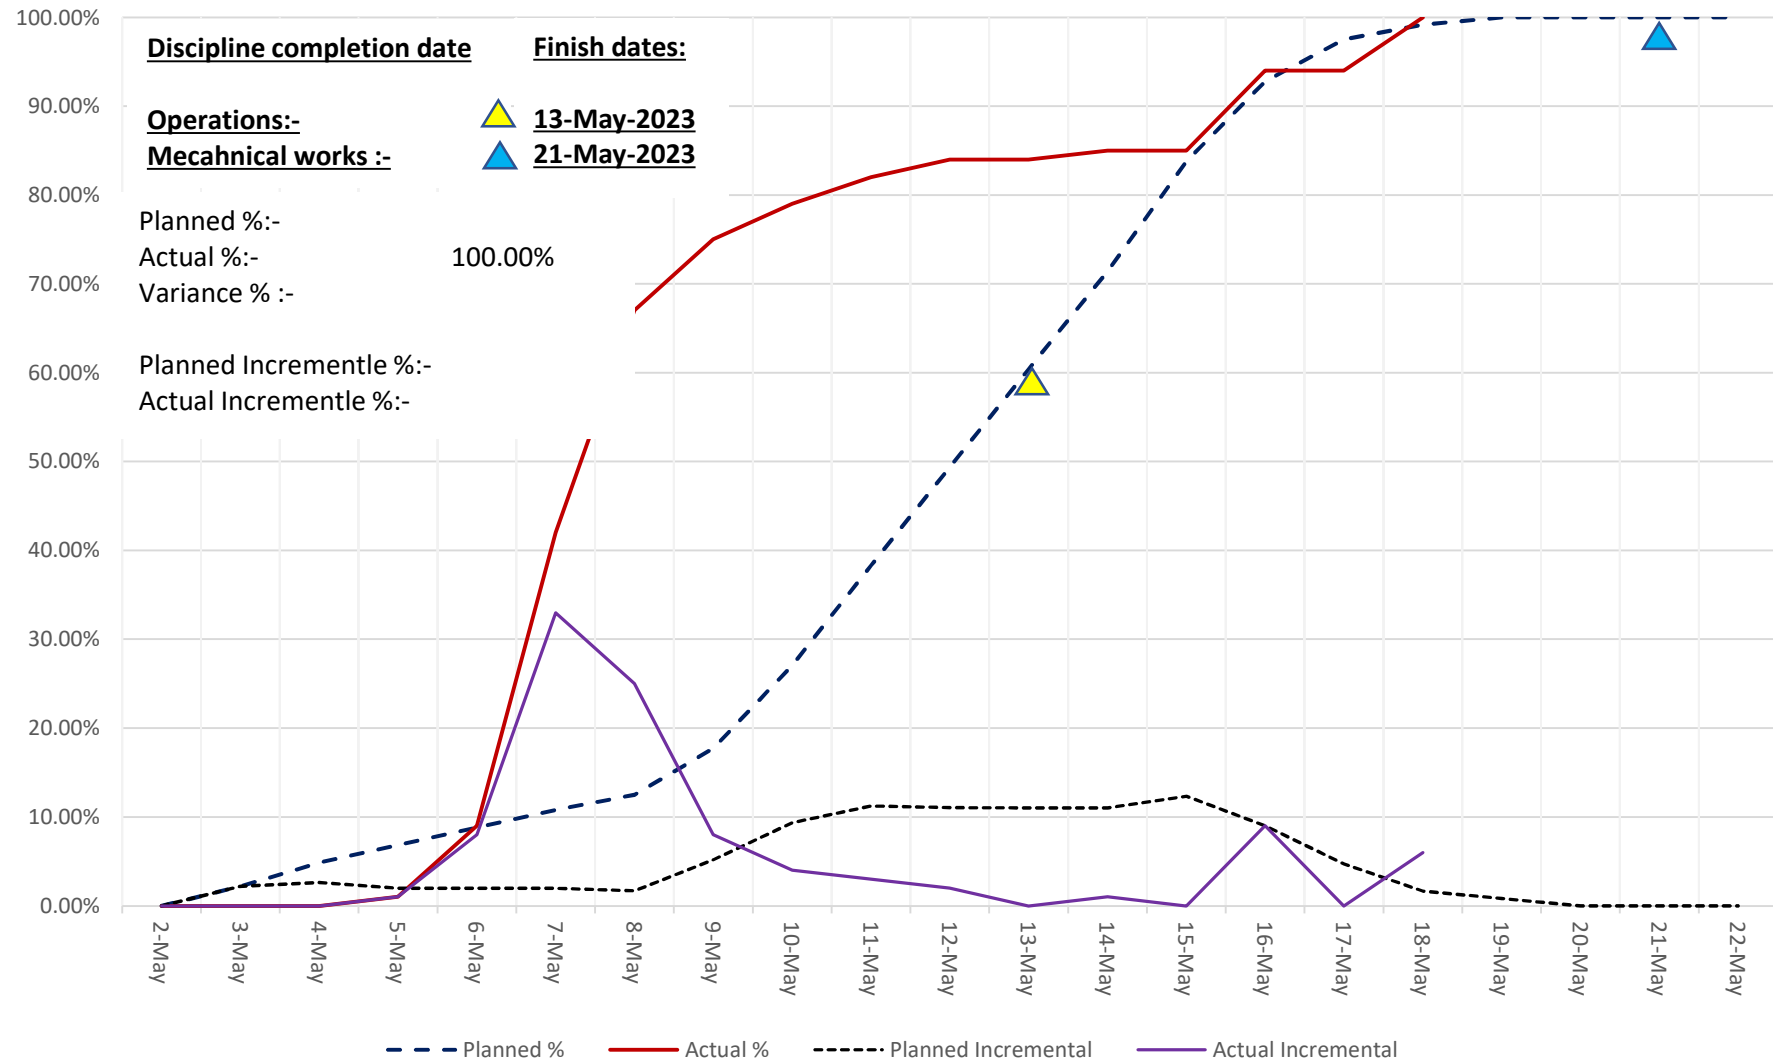




MEA SYSTEM RECLAIMER - Update 20May 2023

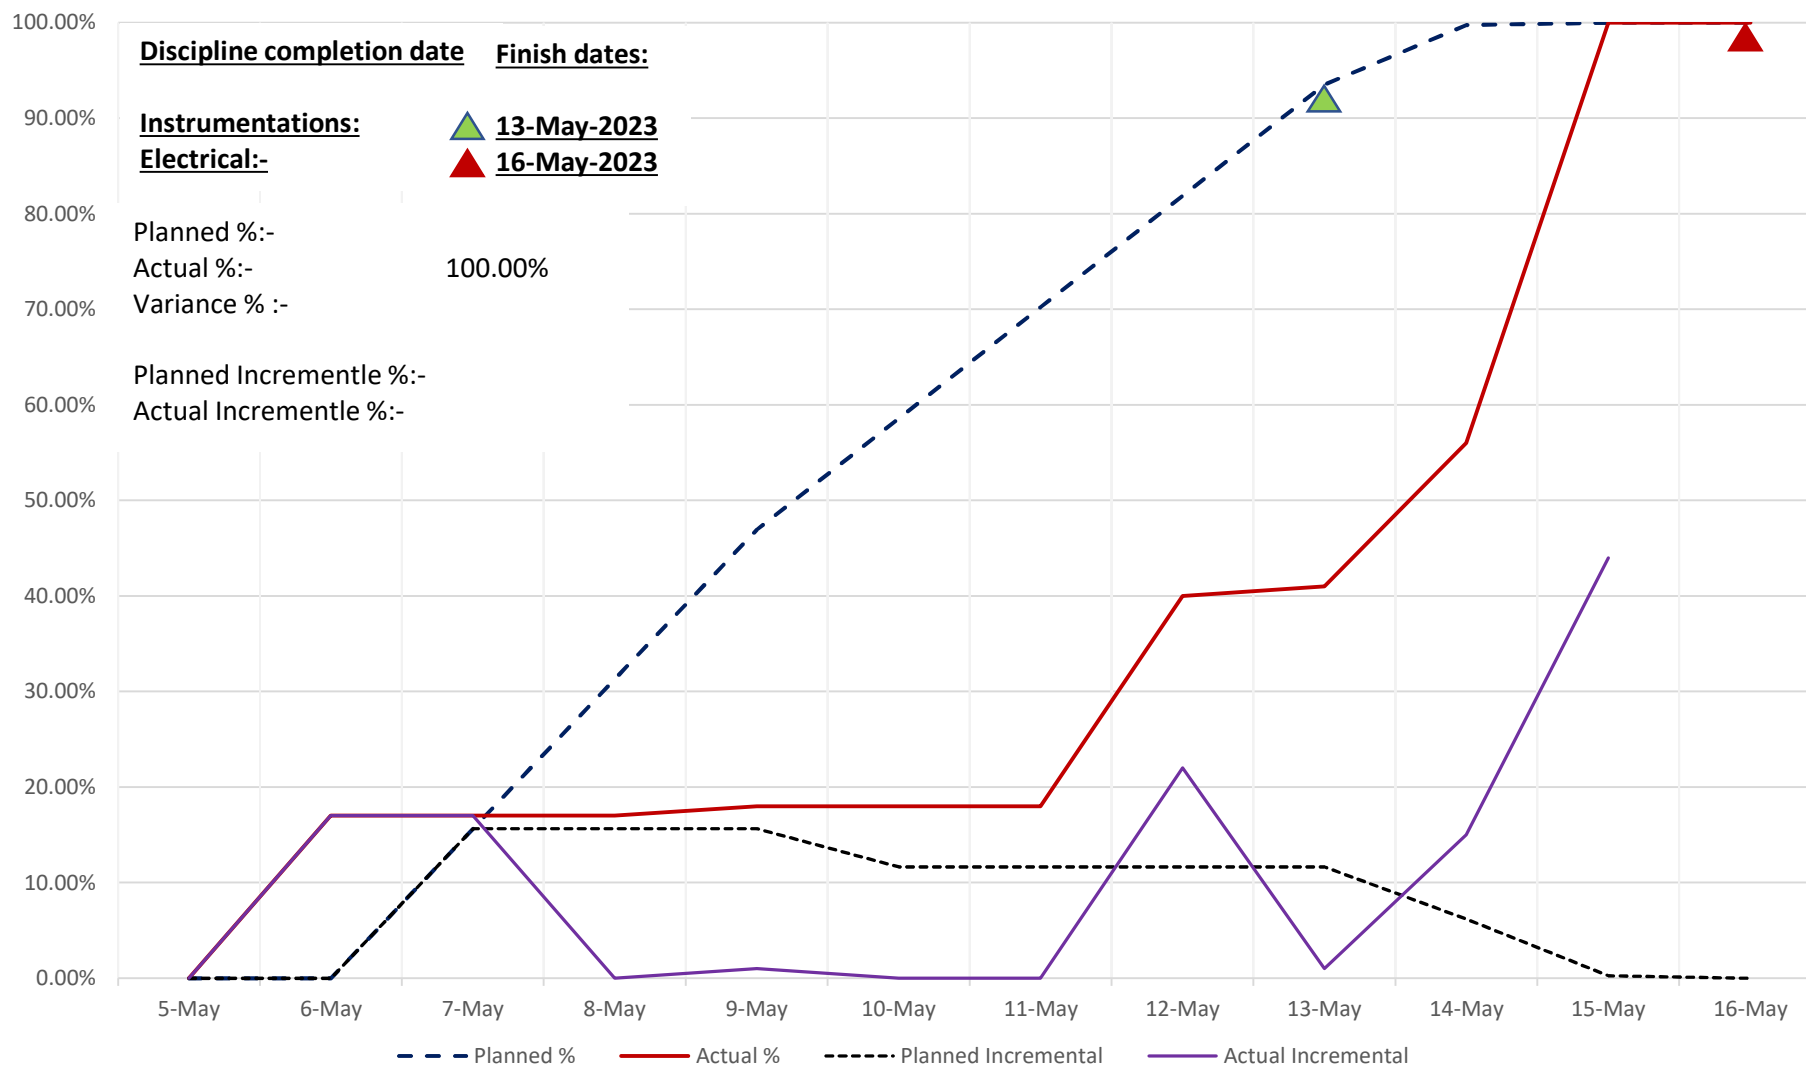




BOILER # 1 - Update 20 May 2023

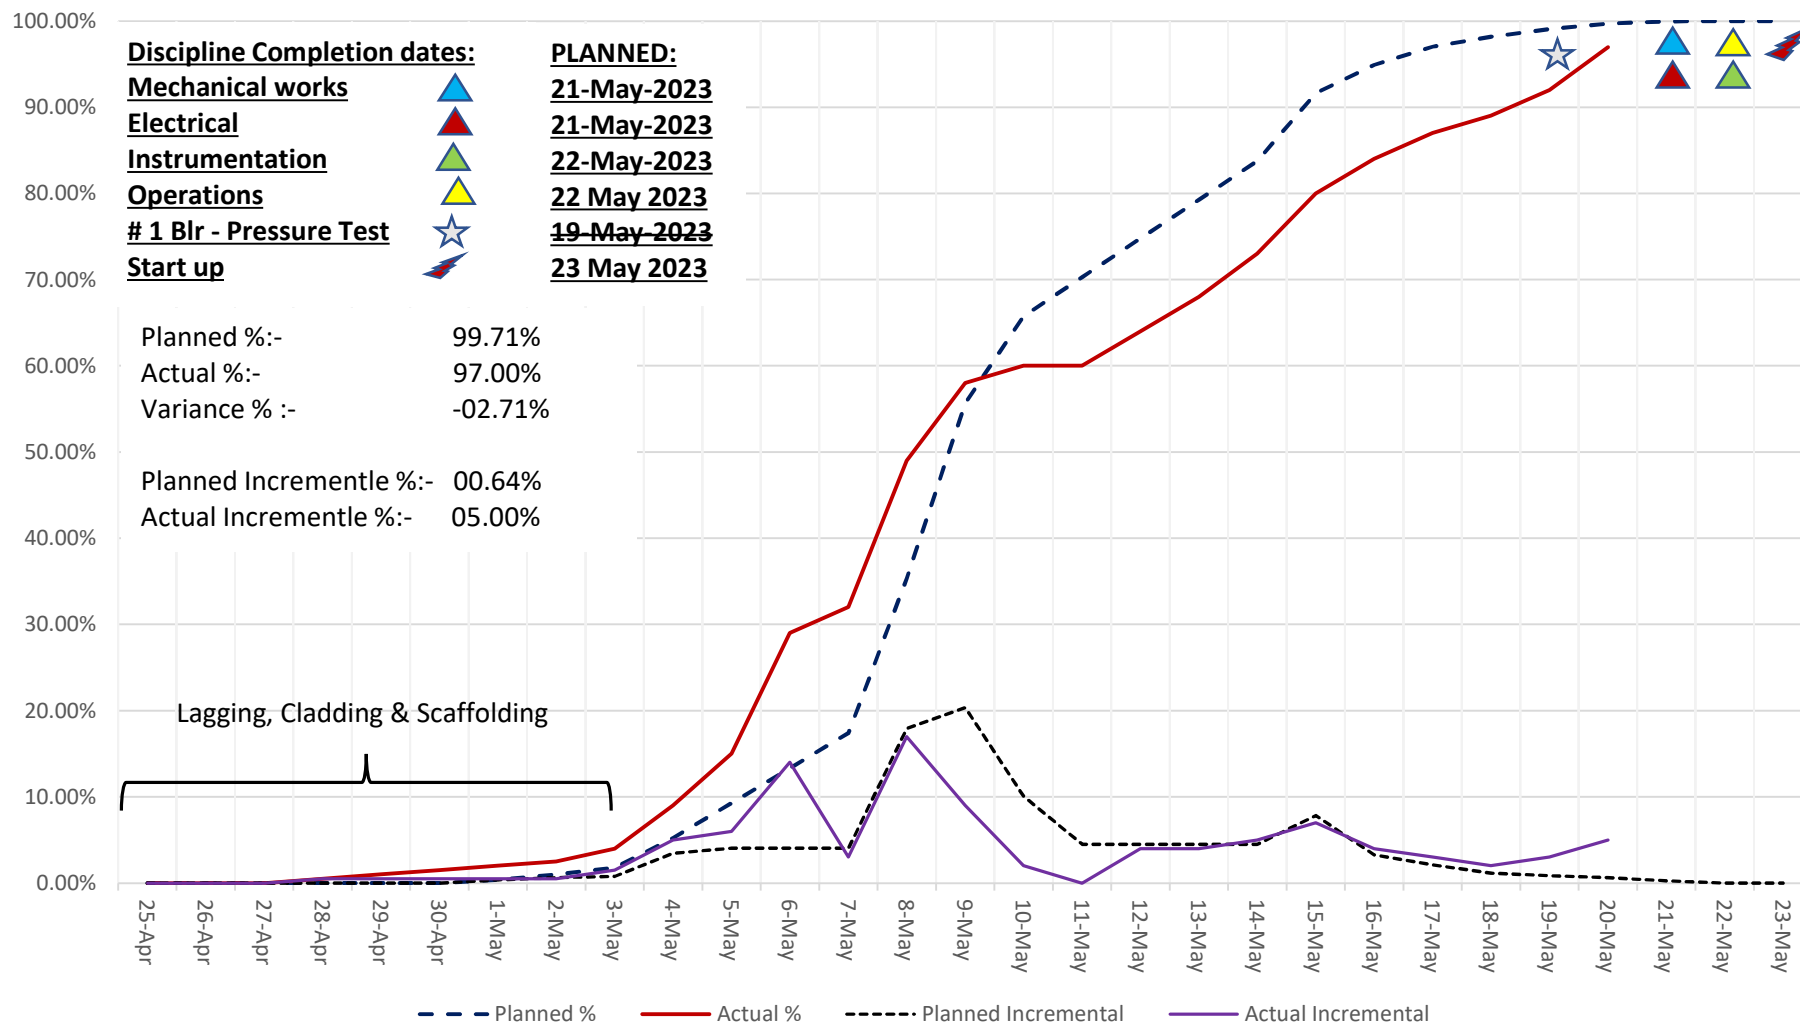




Botswana Ash (Pty) Ltd

BOILER # 2 - Update 20 May 2023

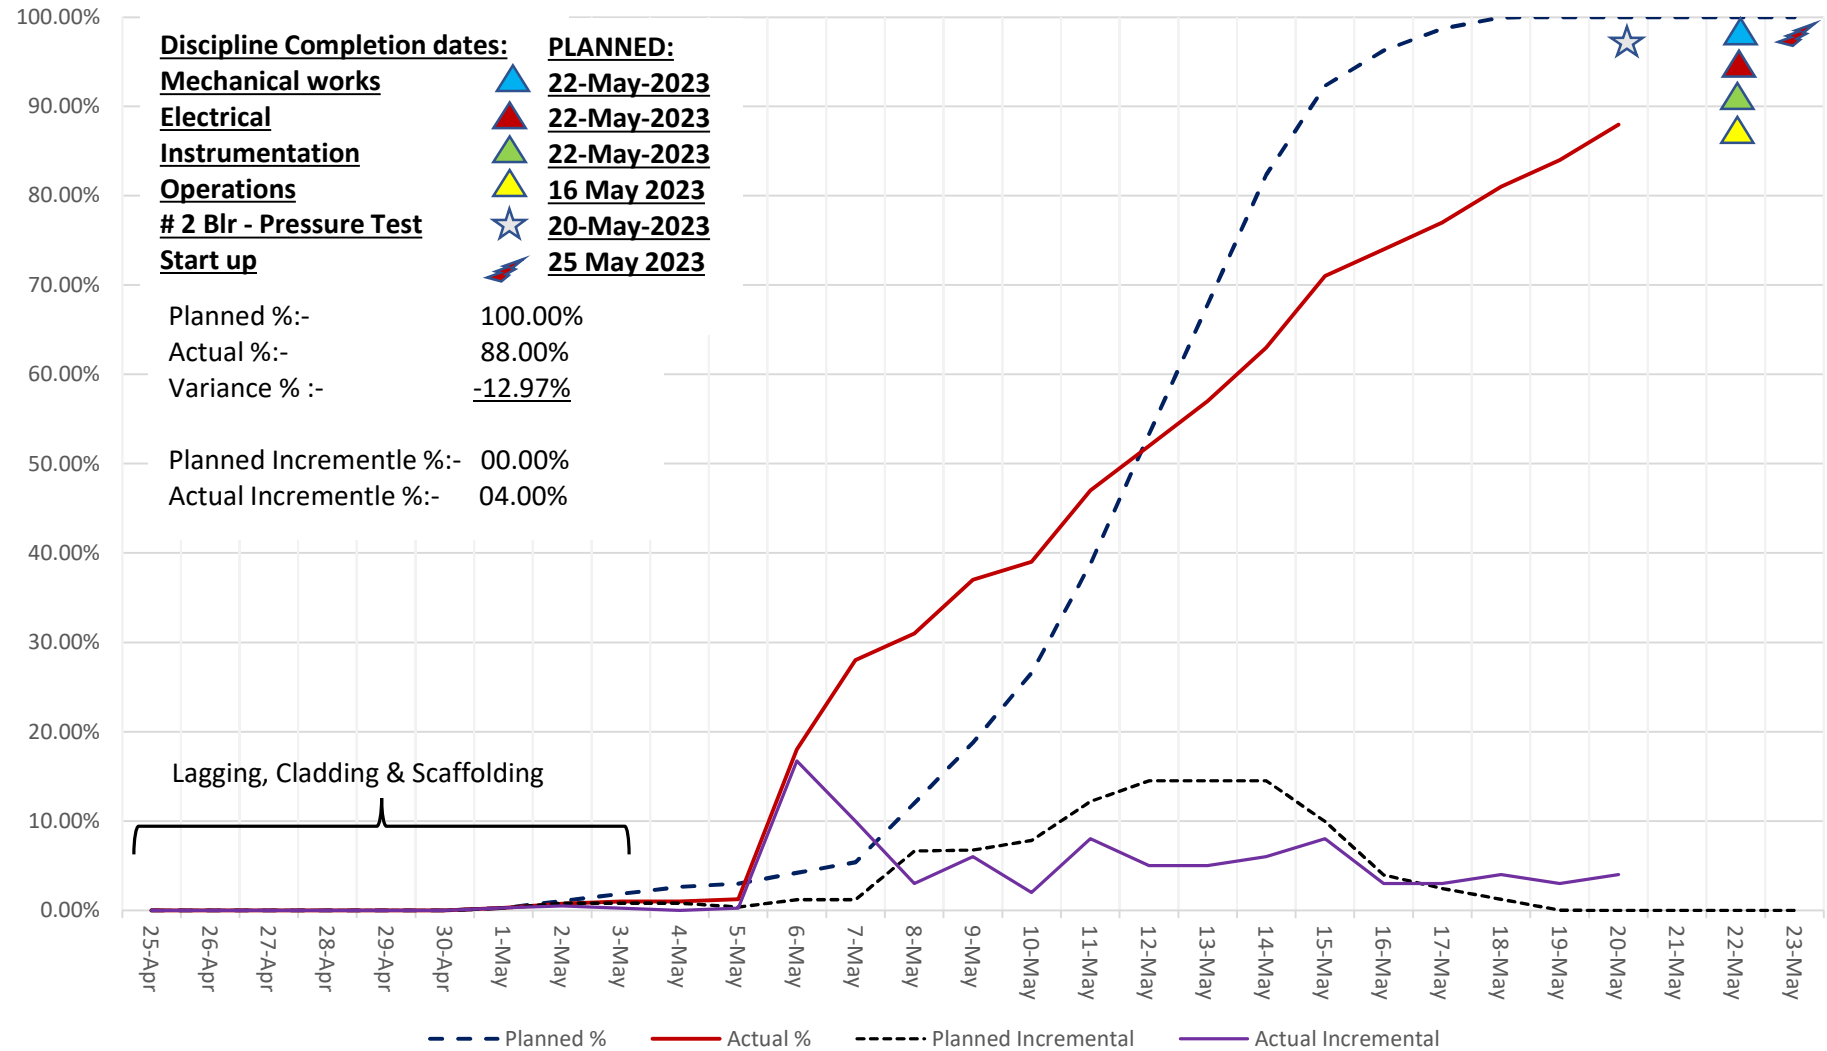




COAL HANDLING PLANT- Update 20 May 2023

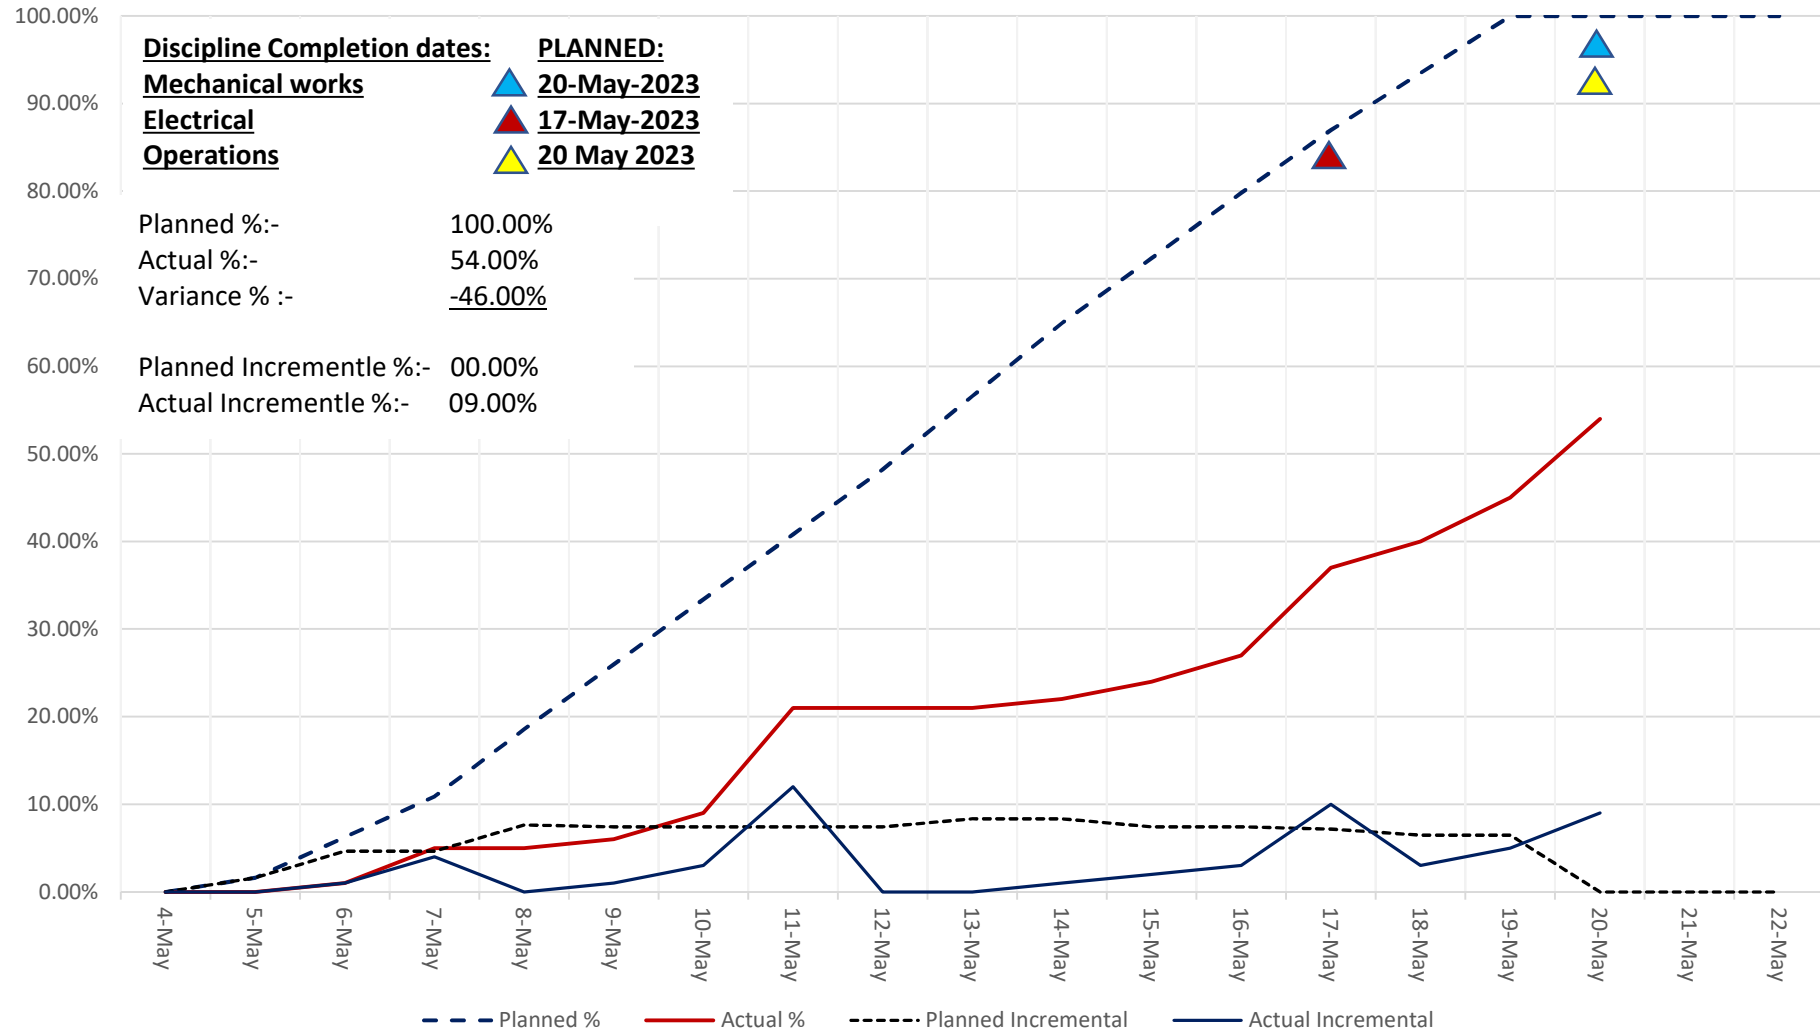



BOILER PLANT COMMON - Update 20 May 2023

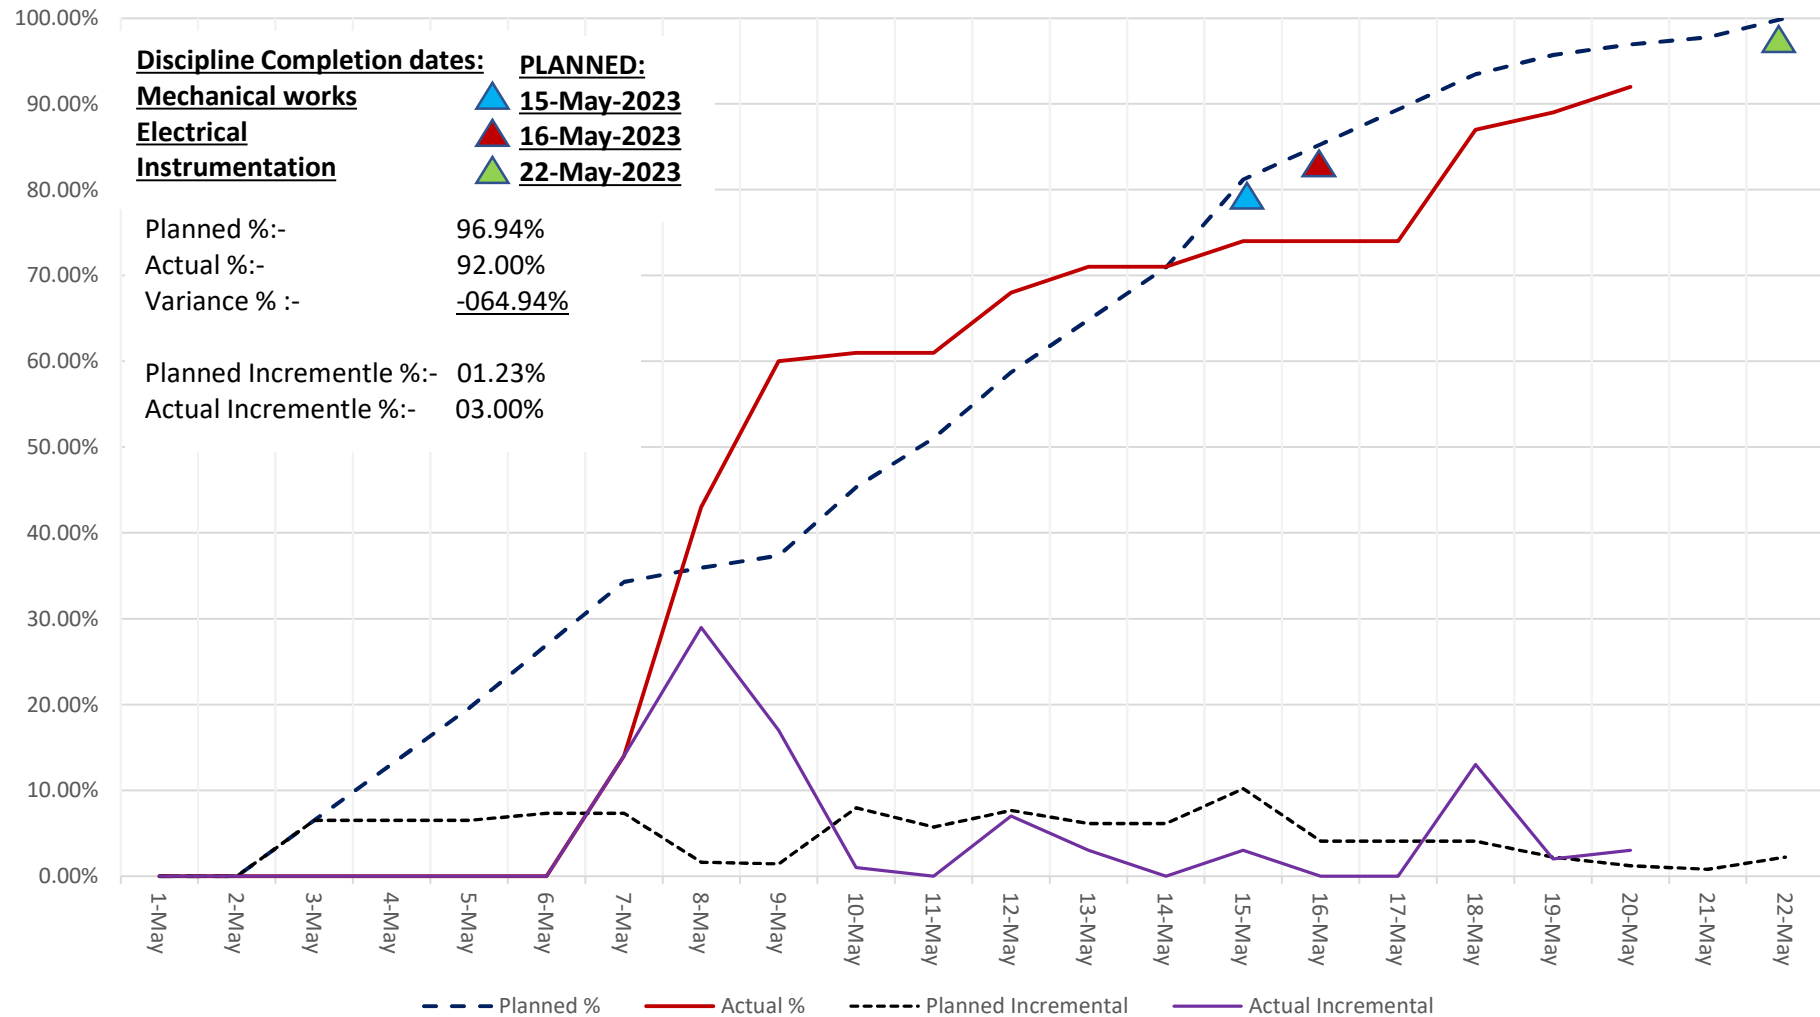



Botswana Ash (Pty) Ltd


WATER TREATMENT PLANT - Update 20 May 2023

Discipline Completion dates:

Operations	 16-May-2023
Electrical	 15-May-2023
Civils	 19-May-2023
Mechanical works	 22 May 2023


Planned %:- 99.38%
Actual %:- 88.00%
Variance % :- -12.43%

Planned Incrementle %:- 01.13%
Actual Incrementle %:- 02.00%

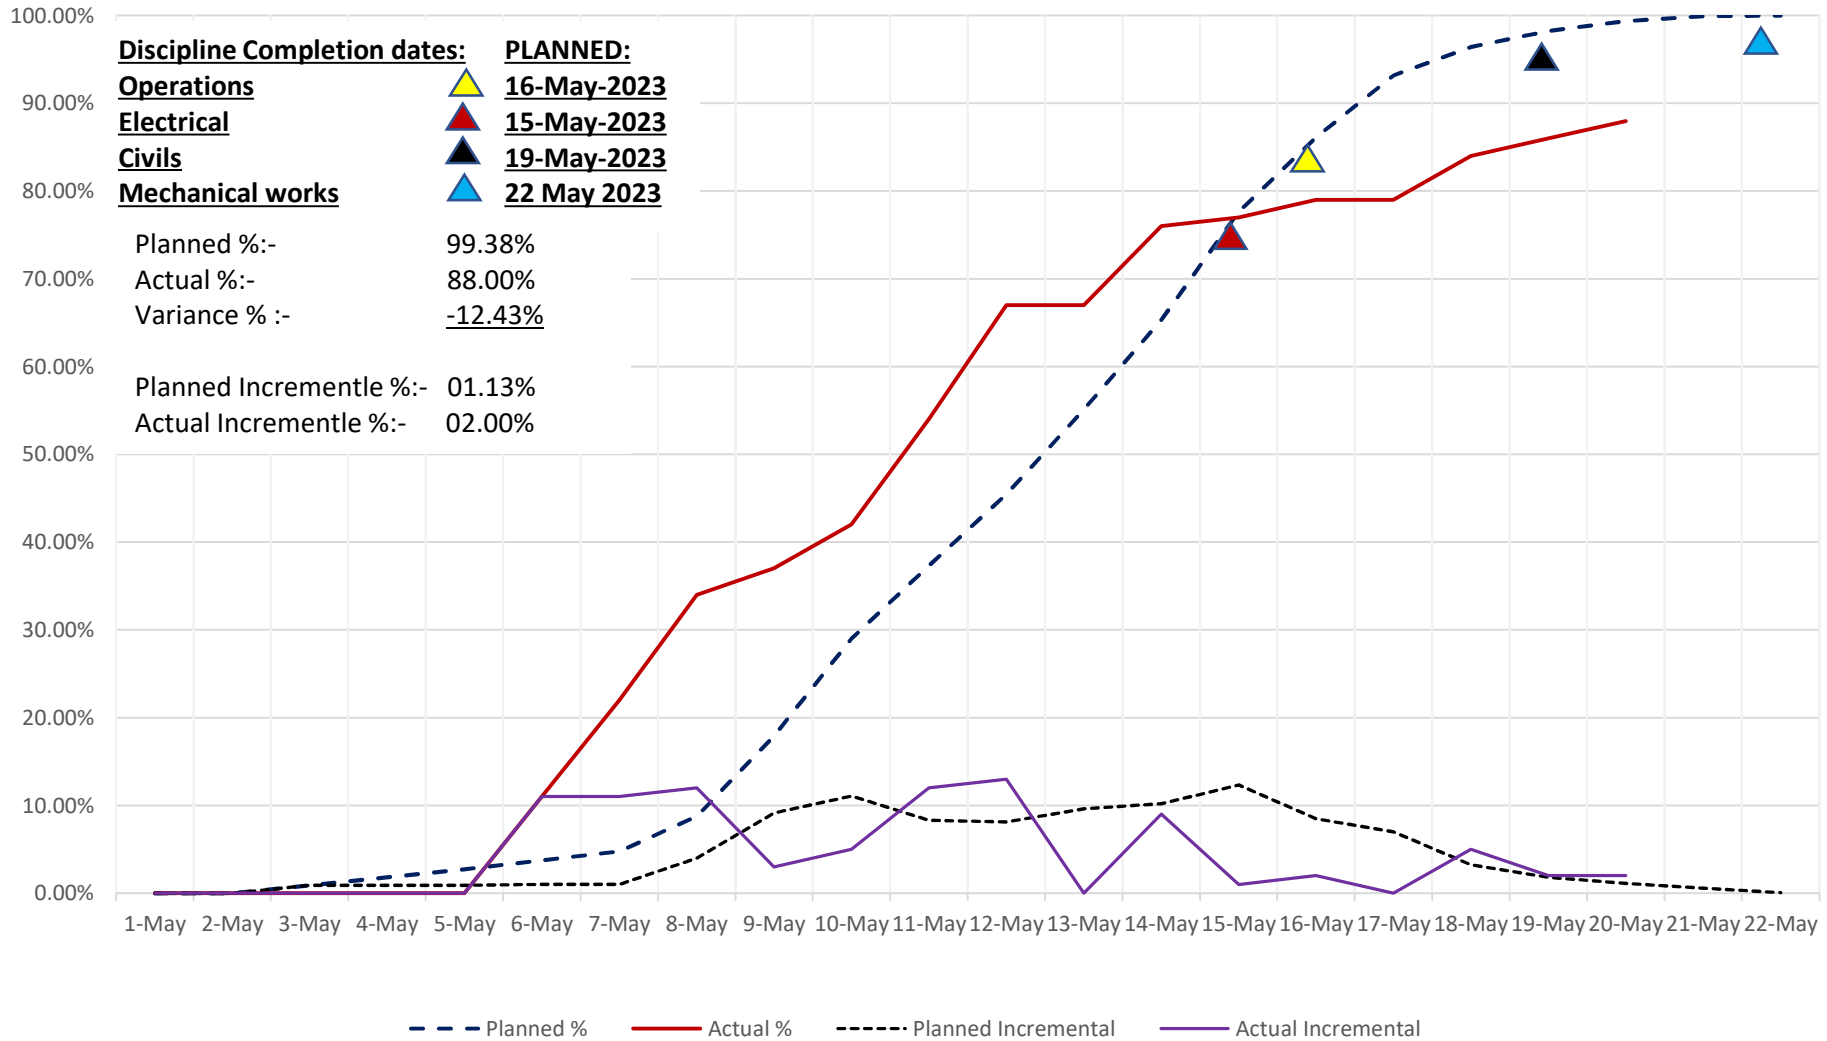




INSTRUMENT & COMPRESSED AIR - Update 20 May 2023

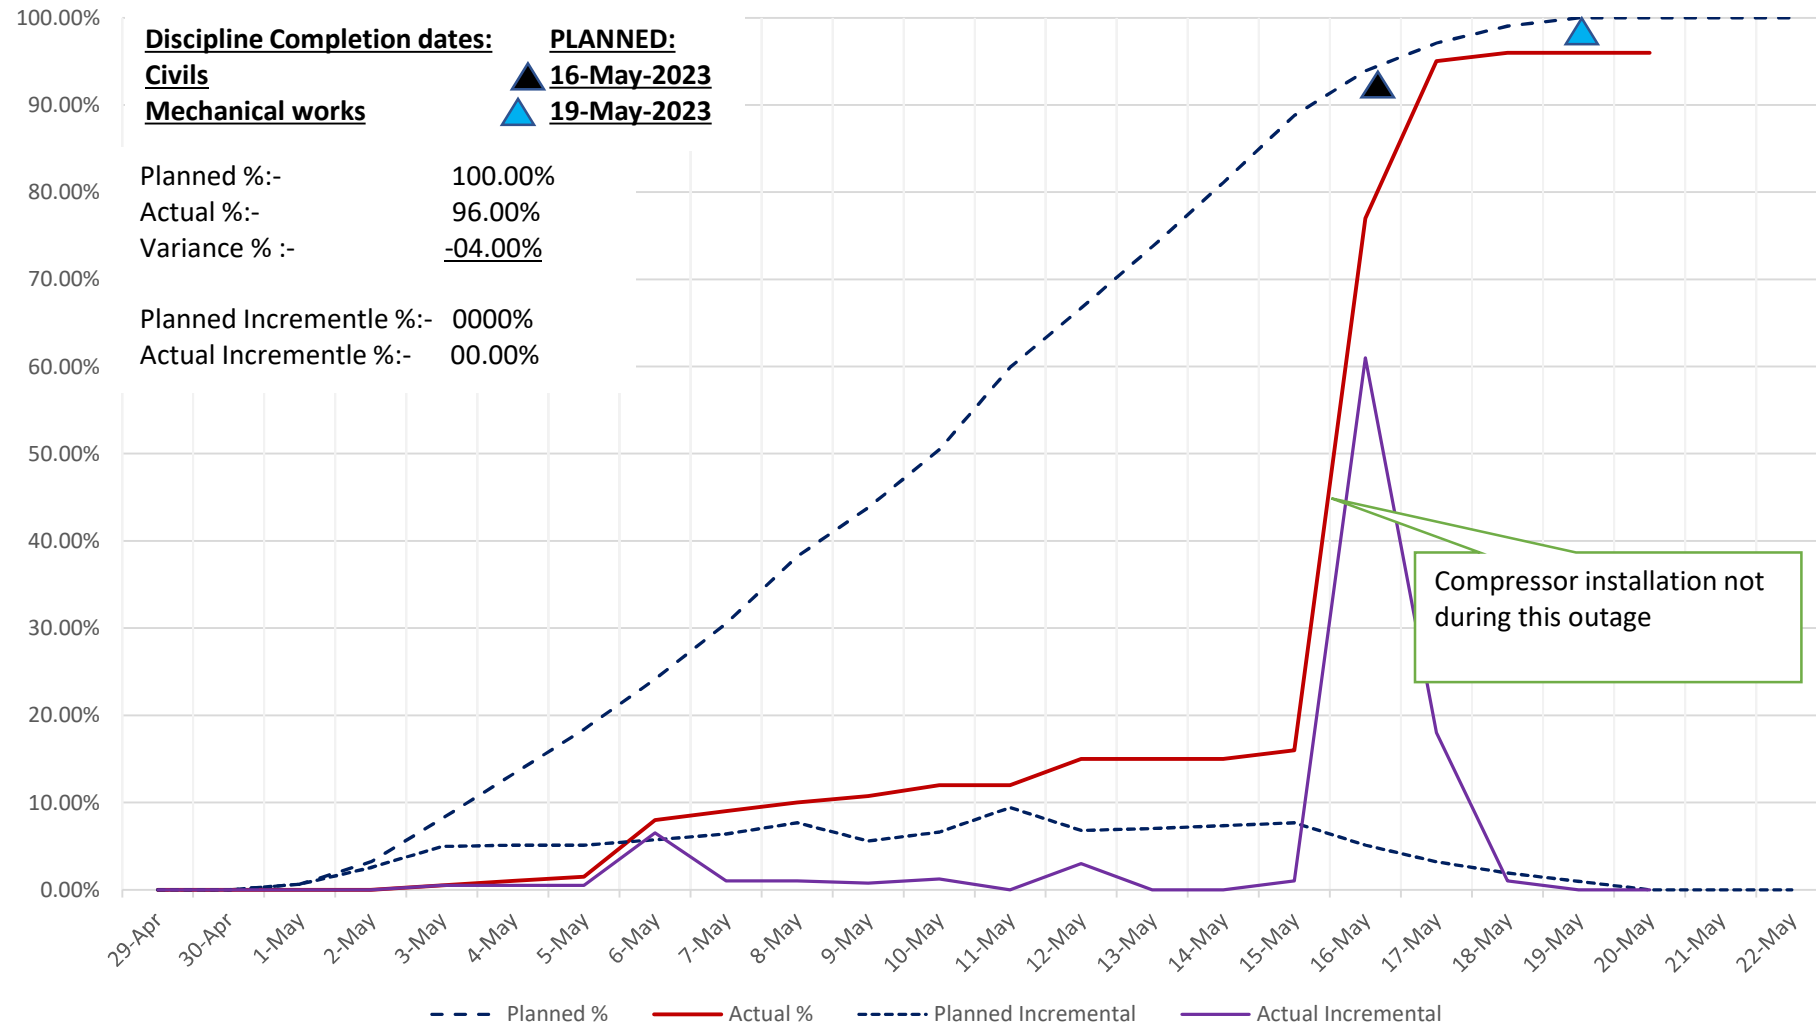




Botswana Ash (Pty) Ltd

STEAM AND CONDENSATE- Update 20 May 2023

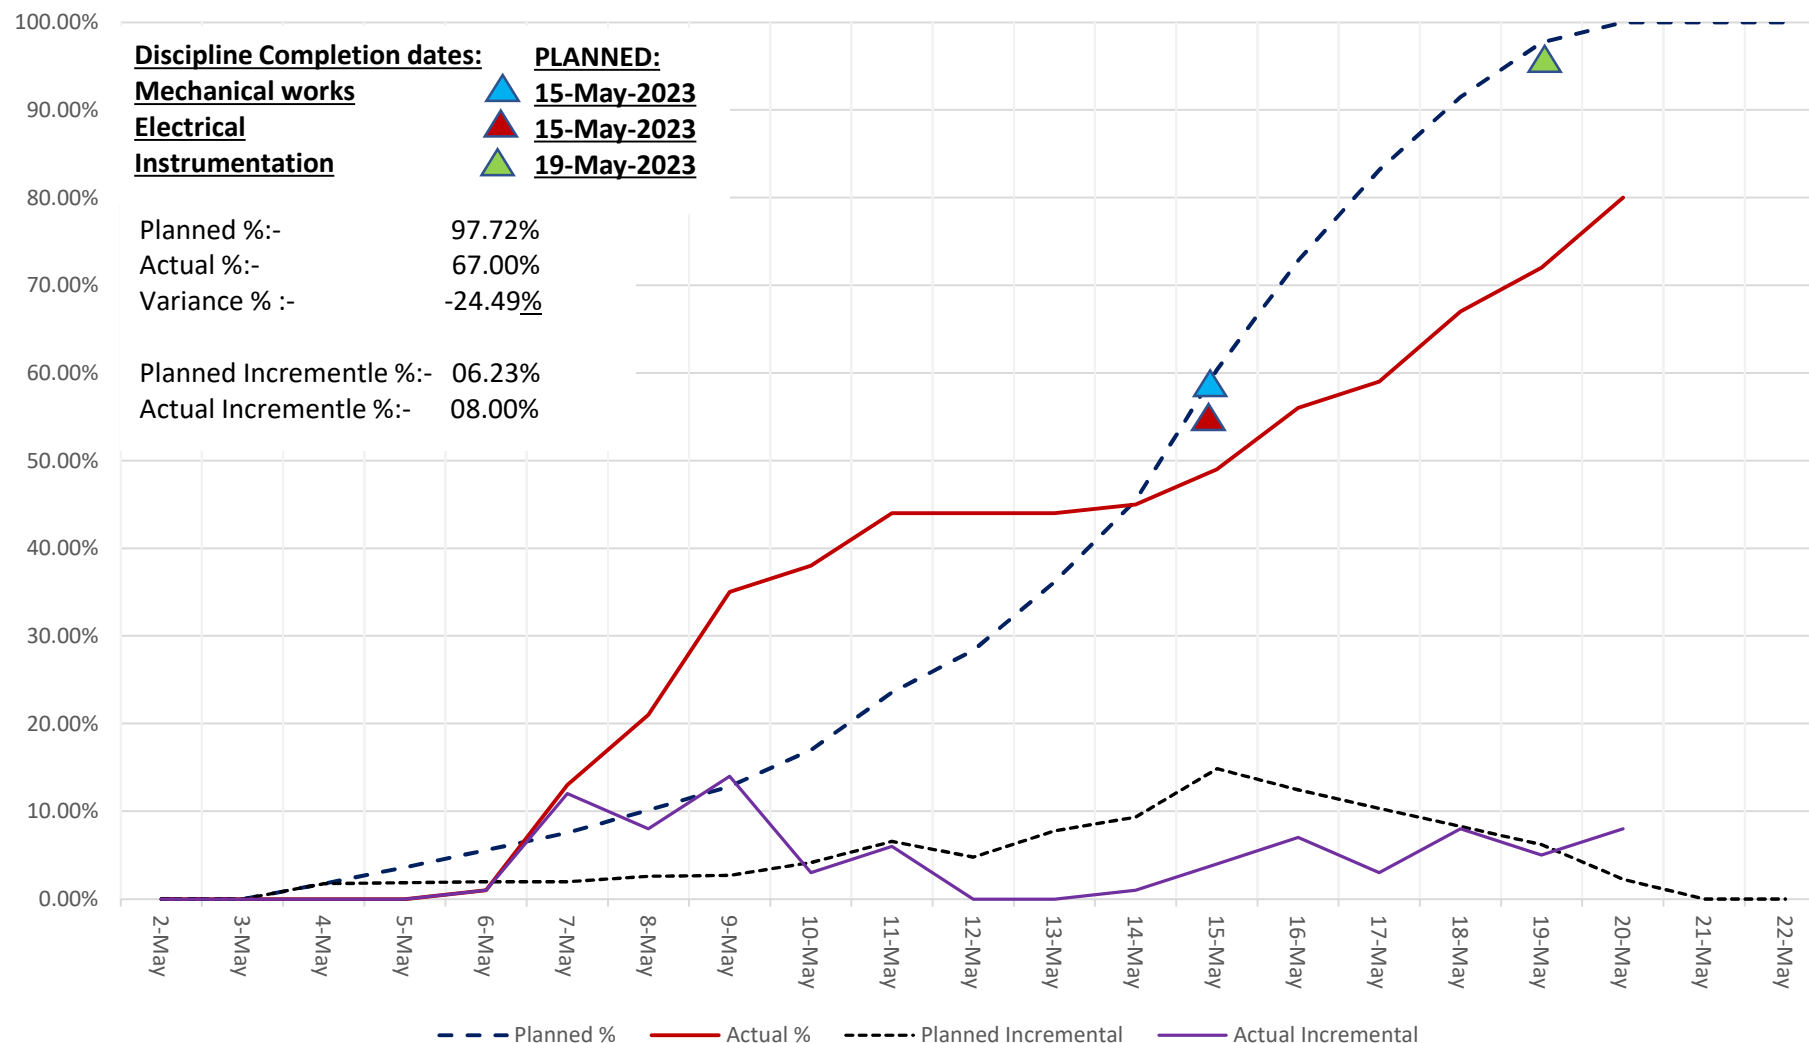




TURBINE - Update 20 May 2023

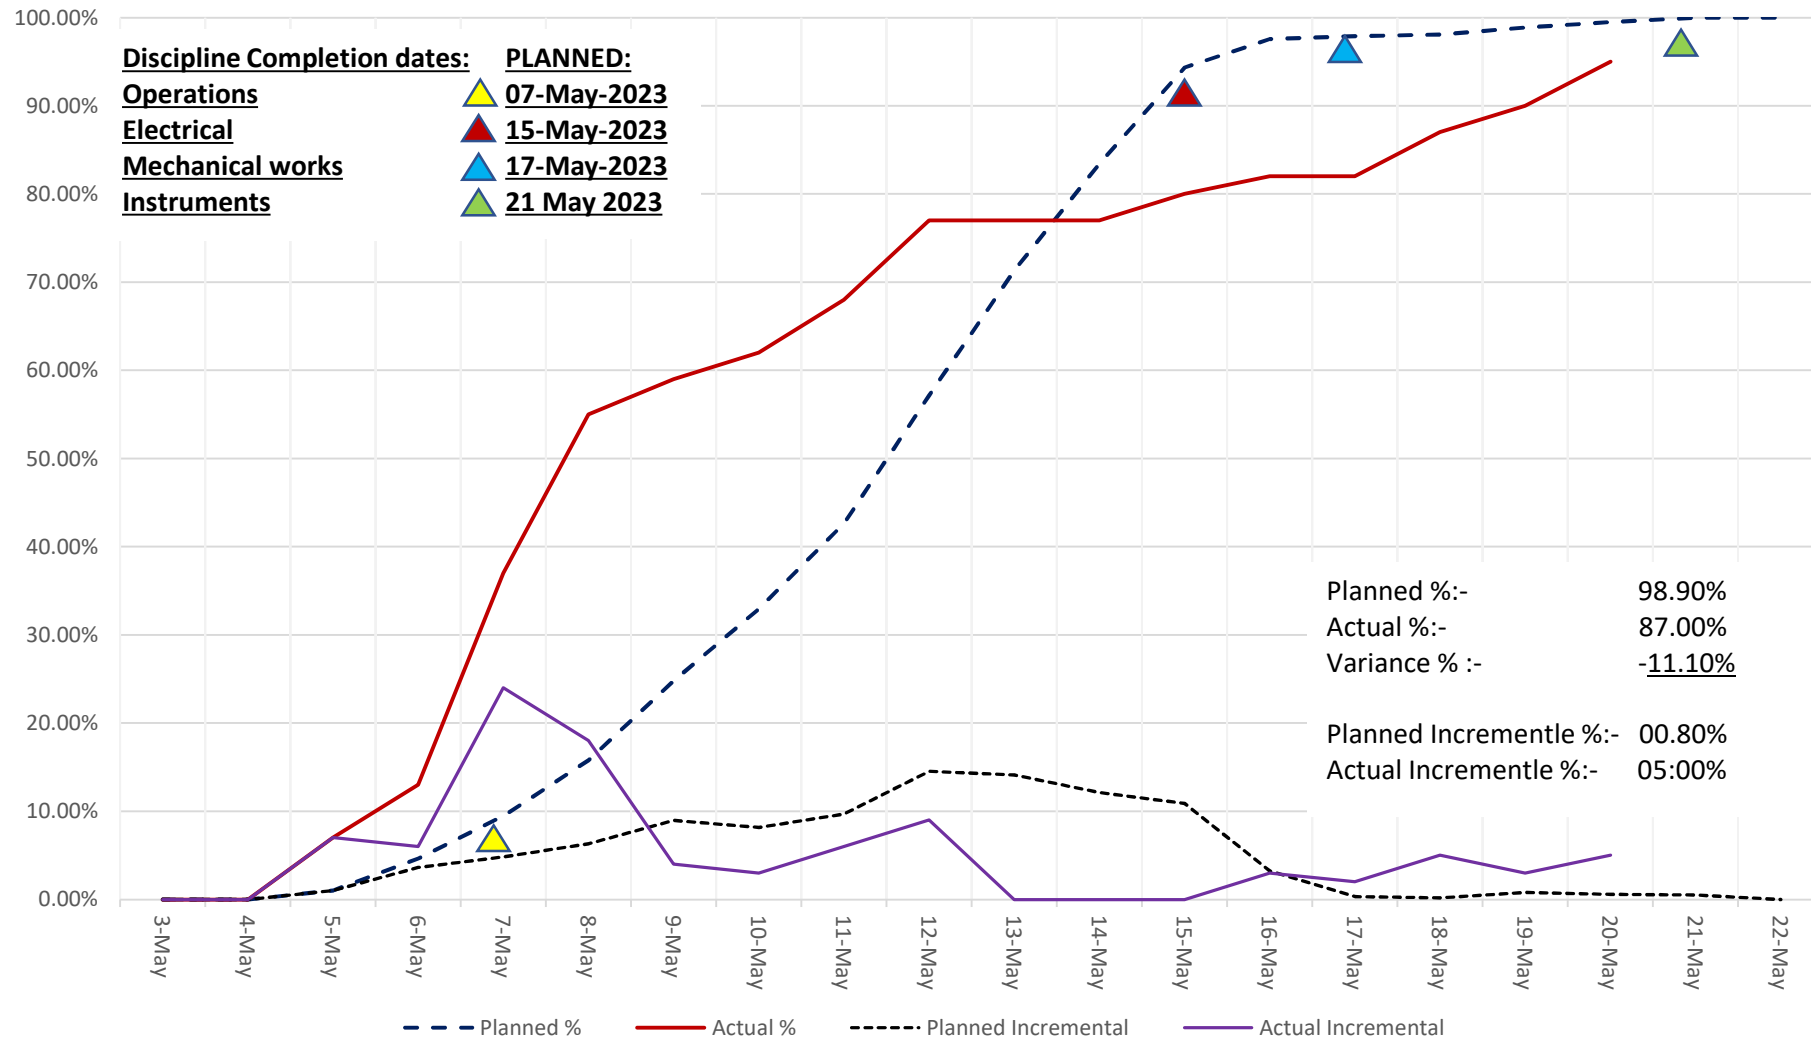



MV RETICULATION - Update 20 May 2023

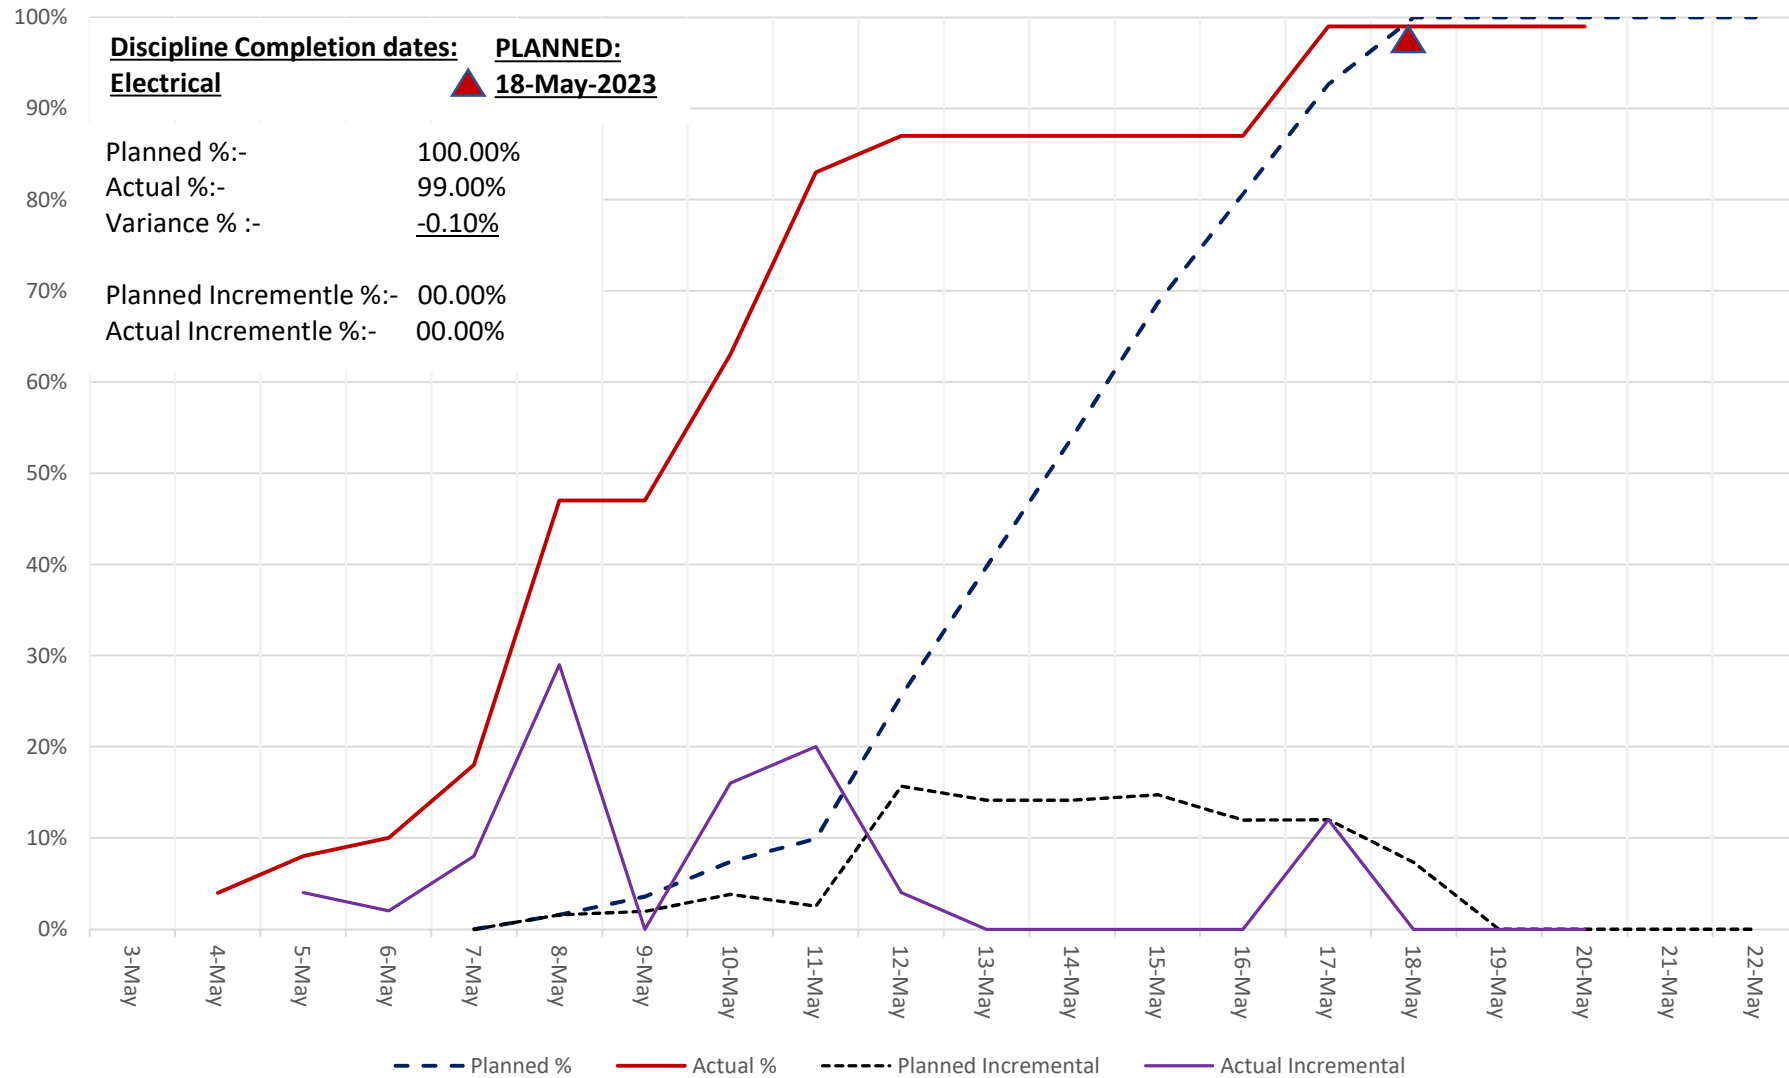



LV RETICULATION - Update 20 May 2023

