




BOTSWANA - BOTASH REFURBISHMENT PROJECT 2023 - SODA ASH PLANT

- Update:- 17 May 2023 - Rev 02

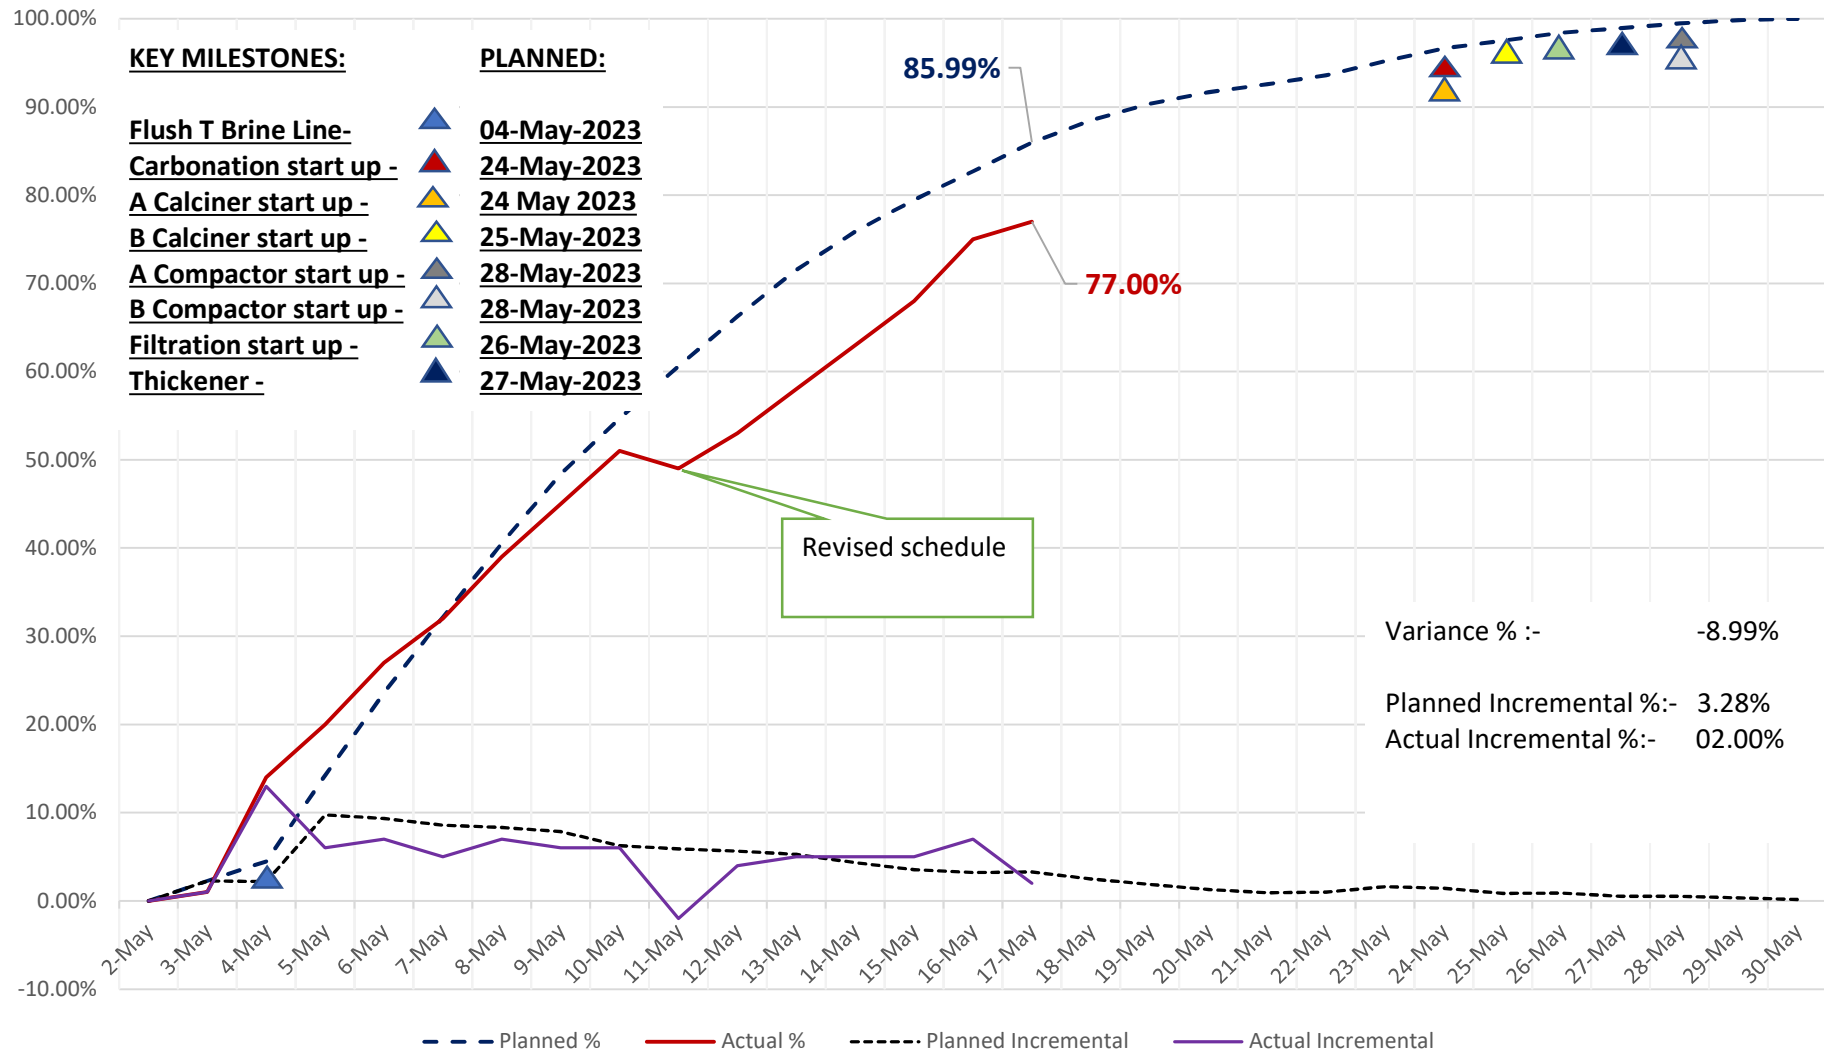


18-May-2023

	Progress		Variance	Incremental	
	Planned	Actual		Planned	Actual
SHUTDOWN PLAN 2023 - SODA ASH PLANT	88.48%	0.00%	-88.48%	2.49%	0.00%
POTABLE & BRACKISH WATER SUPPLY	90.08%	0.00%	-90.08%	0.00%	0.00%
FIRE HYDRANT SYSTEM	93.46%	0.00%	-93.46%	5.78%	0.00%
HOT WASH WATER SYSTEM	0.00%	0.00%	0.00%	0.00%	0.00%
CARBONATION	94.48%	0.00%	-94.48%	3.49%	0.00%
CRYSTALLISATION	89.28%	0.00%	-89.28%	4.31%	0.00%
BICARBONATE THICKENING	70.63%	0.00%	-70.63%	3.29%	0.00%
BICARBONATE FILTRATION - A LINE	100.00%	0.00%	-100.00%	0.00%	0.00%
BICARBONATE FILTRATION - B LINE	84.94%	0.00%	-84.94%	2.91%	0.00%
CALCINER - A LINE	95.37%	0.00%	-95.37%	2.72%	0.00%
CALCINER - B LINE	96.24%	0.00%	-96.24%	1.70%	0.00%
CALCINER GAS TREATMENT - A LINE	98.31%	0.00%	-98.31%	1.45%	0.00%
CALCINER GAS TREATMENT - B LINE	87.41%	0.00%	-87.41%	0.00%	0.00%
COMPACTION - A LINE	97.84%	0.00%	-97.84%	2.38%	0.00%
COMPACTION - B LINE	96.81%	0.00%	-96.81%	2.75%	0.00%
DENSE SODA ASH STORAGE			0.00%		
DENSE SODA ASH BAGGING			0.00%		




FIRE & HYDRANT SYSTEM :- Update 17 May 2023 - Rev 02

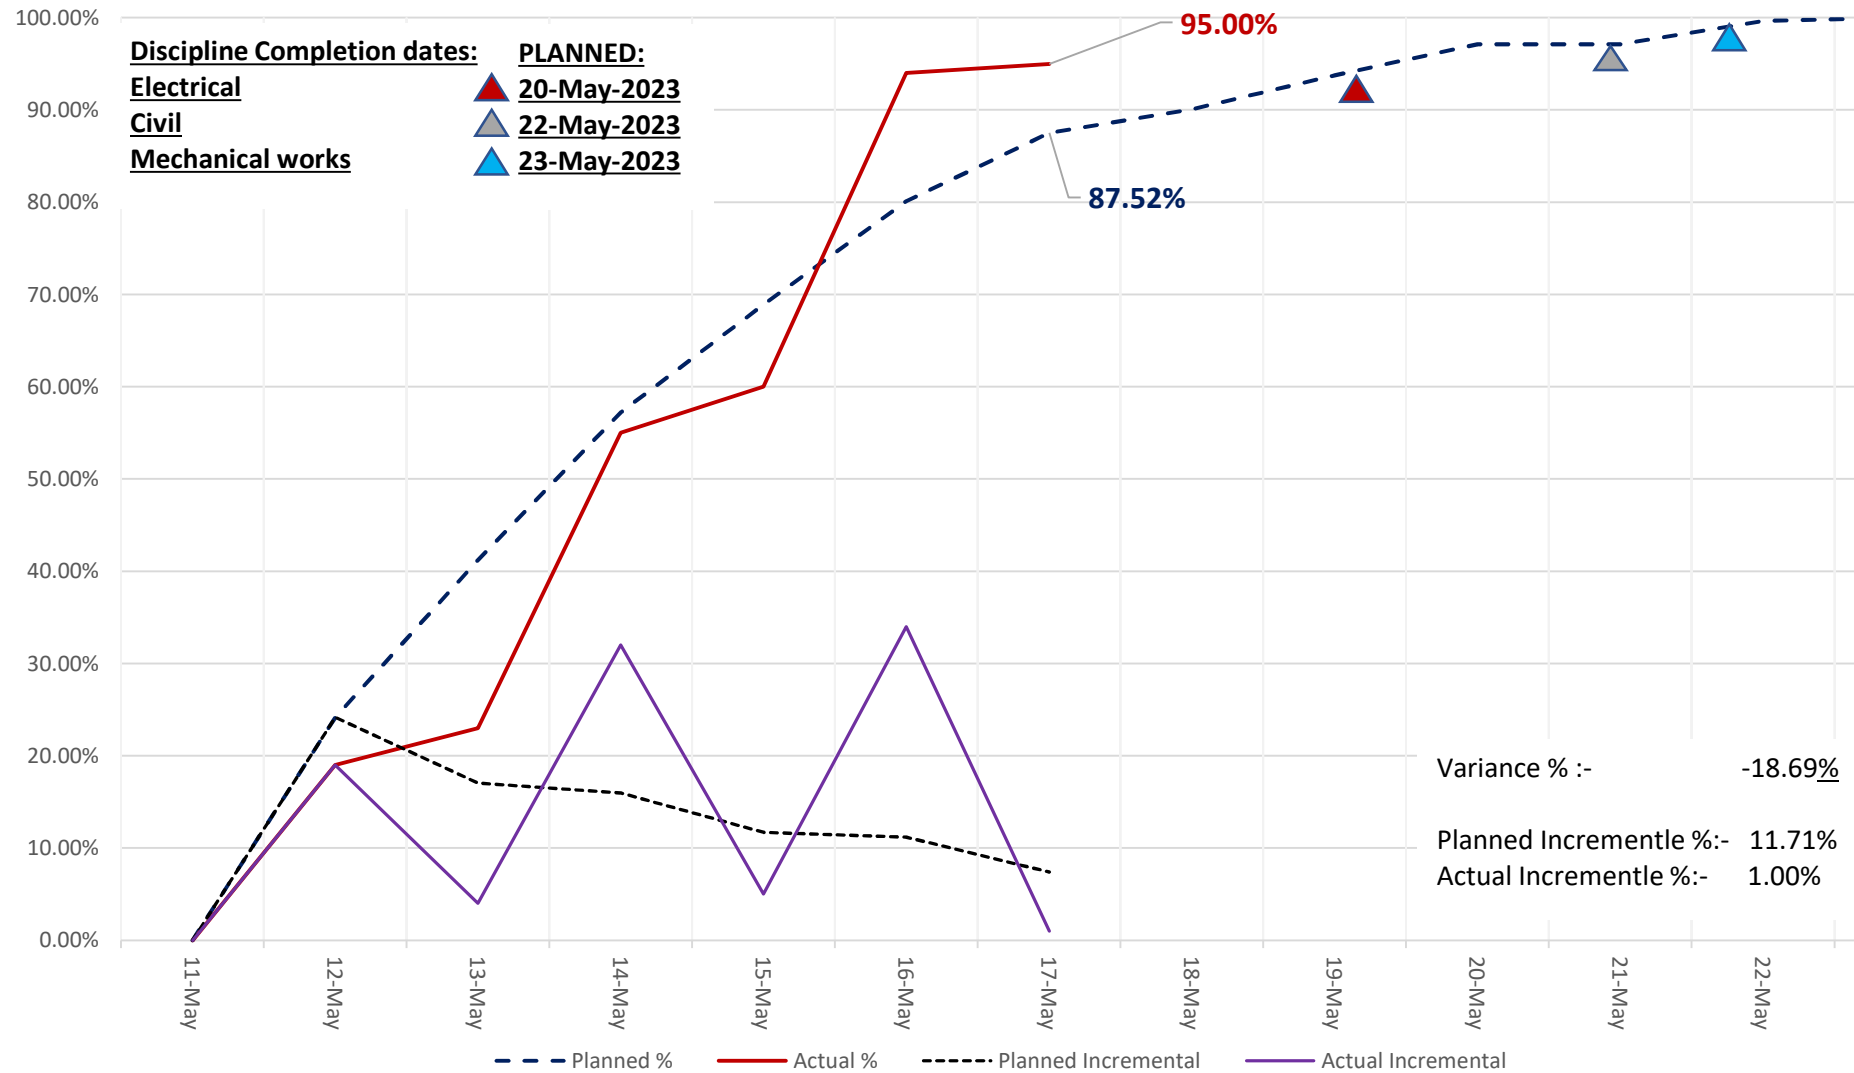



Botswana Ash (Pty) Ltd

POTABLE & BRACKISH WATER:- Update 17 May 2023 - Rev 02

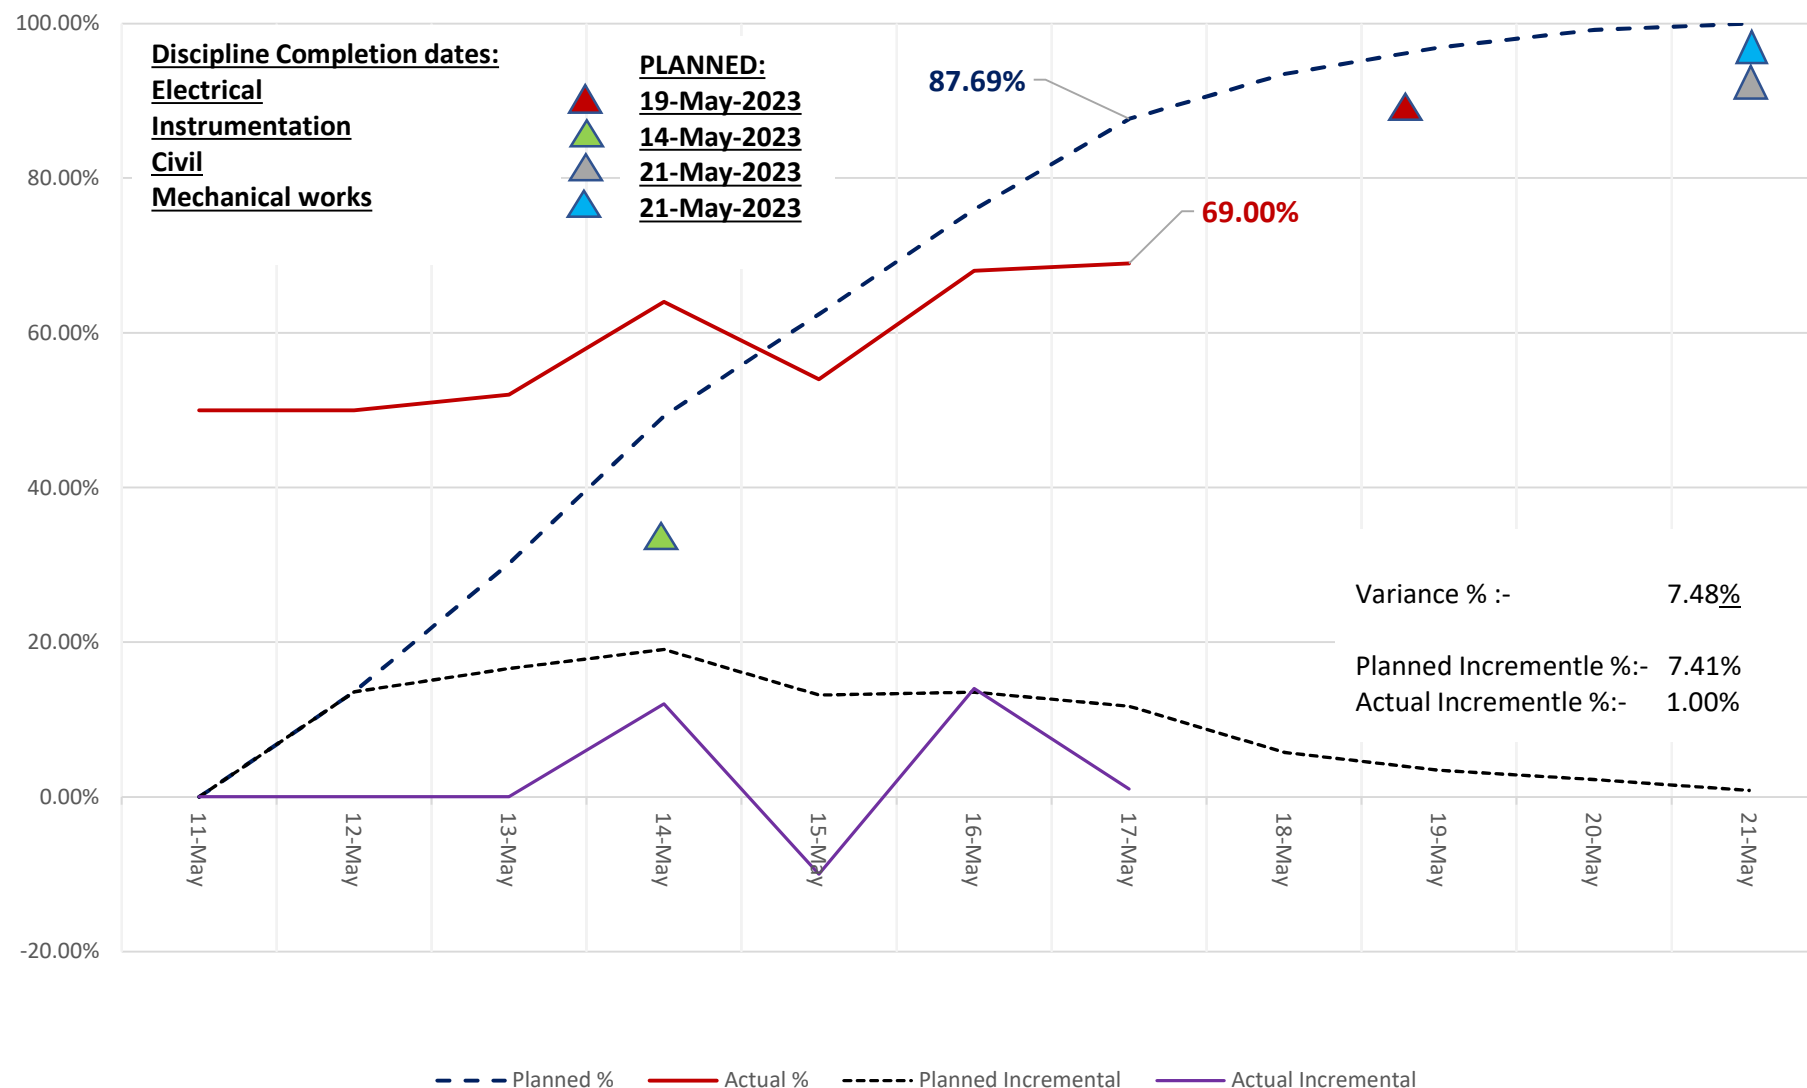






Botswana Ash (Pty) Ltd


HOT WASH WATER SYSTEM:- Update 17 May 2023 - Rev 02

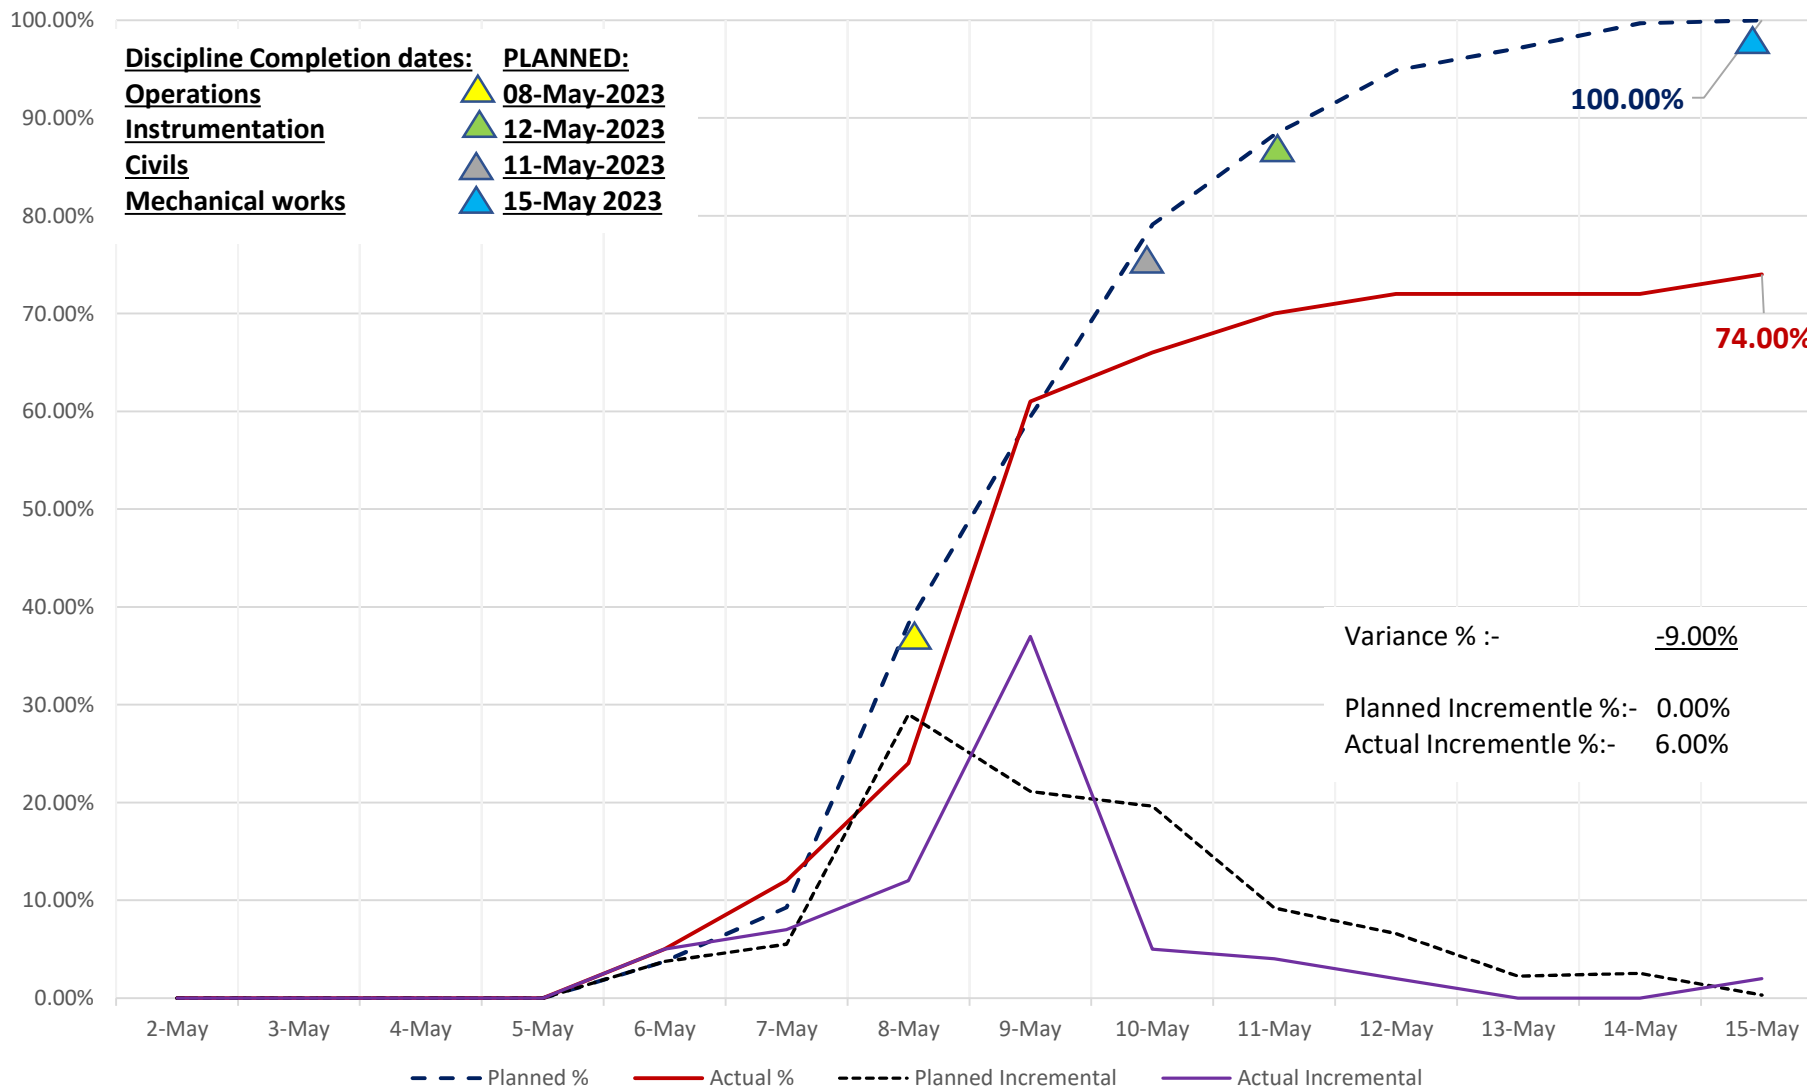




Botswana Ash (Pty) Ltd

CARBONATION:- Update 17 May 2023 - Rev 02

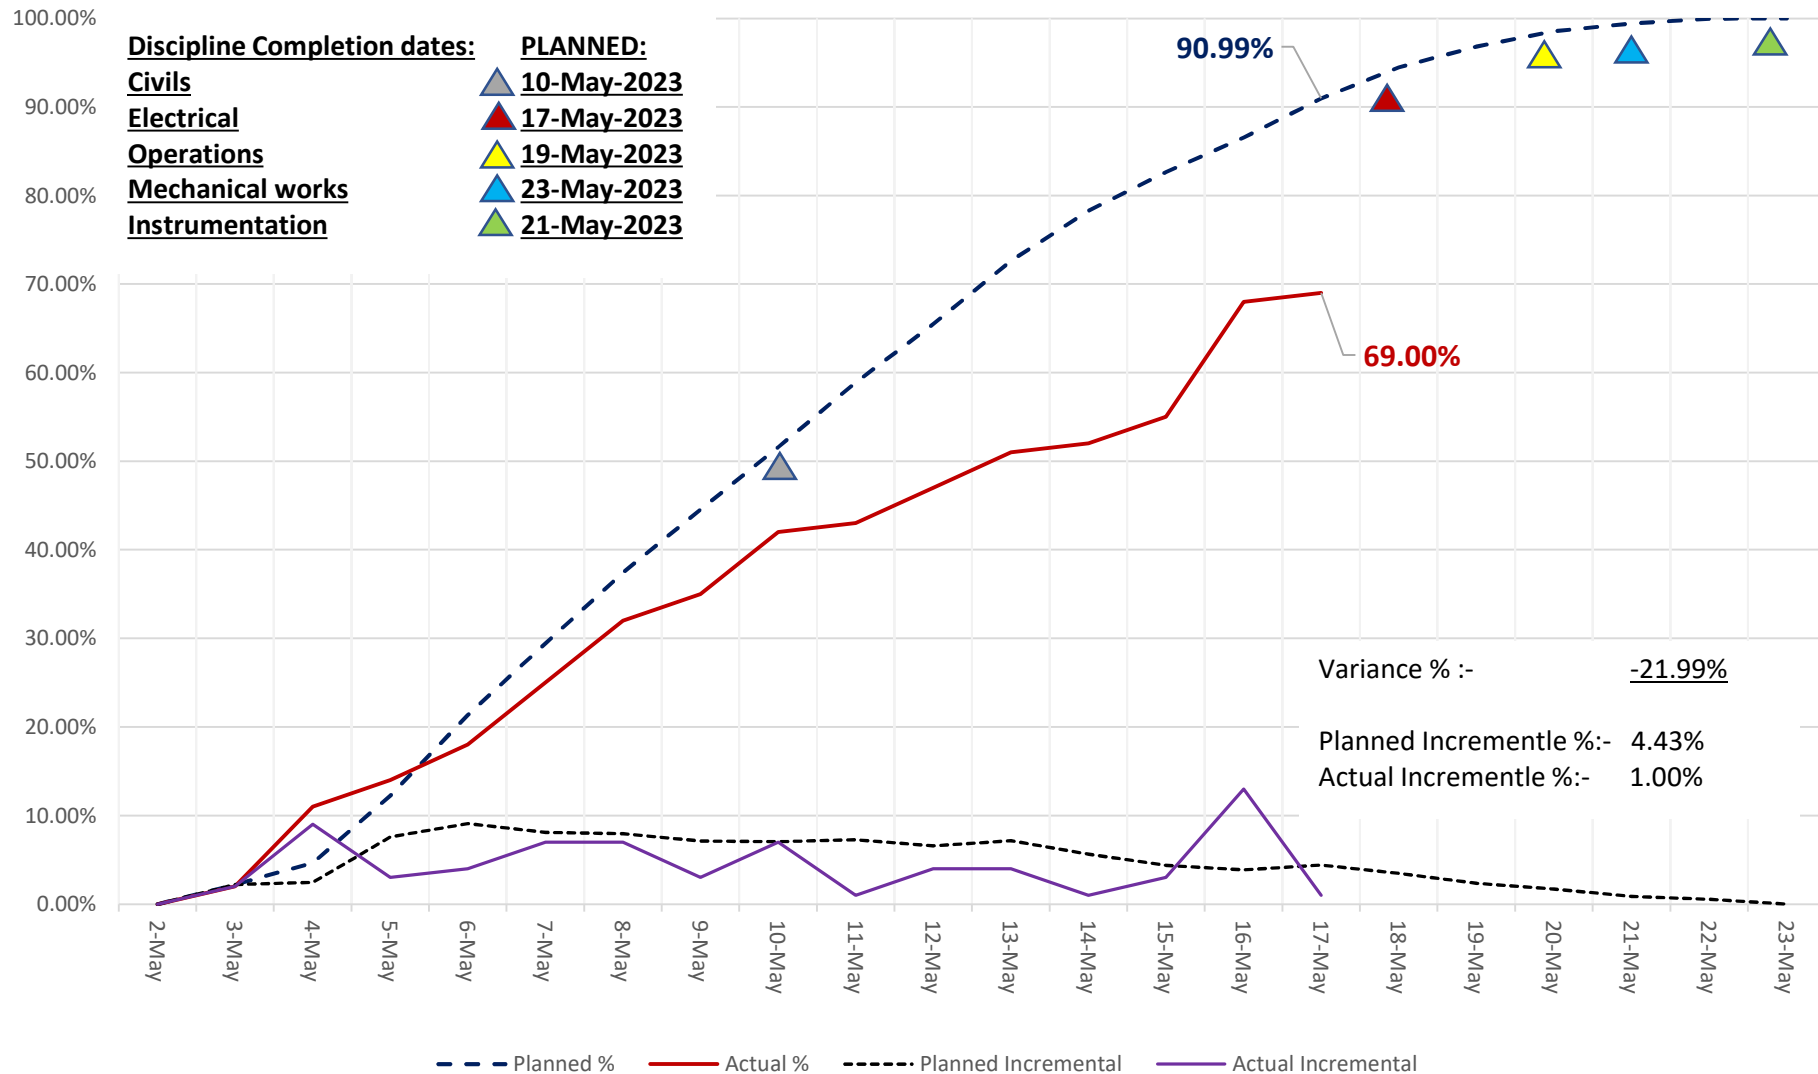




CRYSTALLISATION:- Update 17 May 2023 - Rev 02

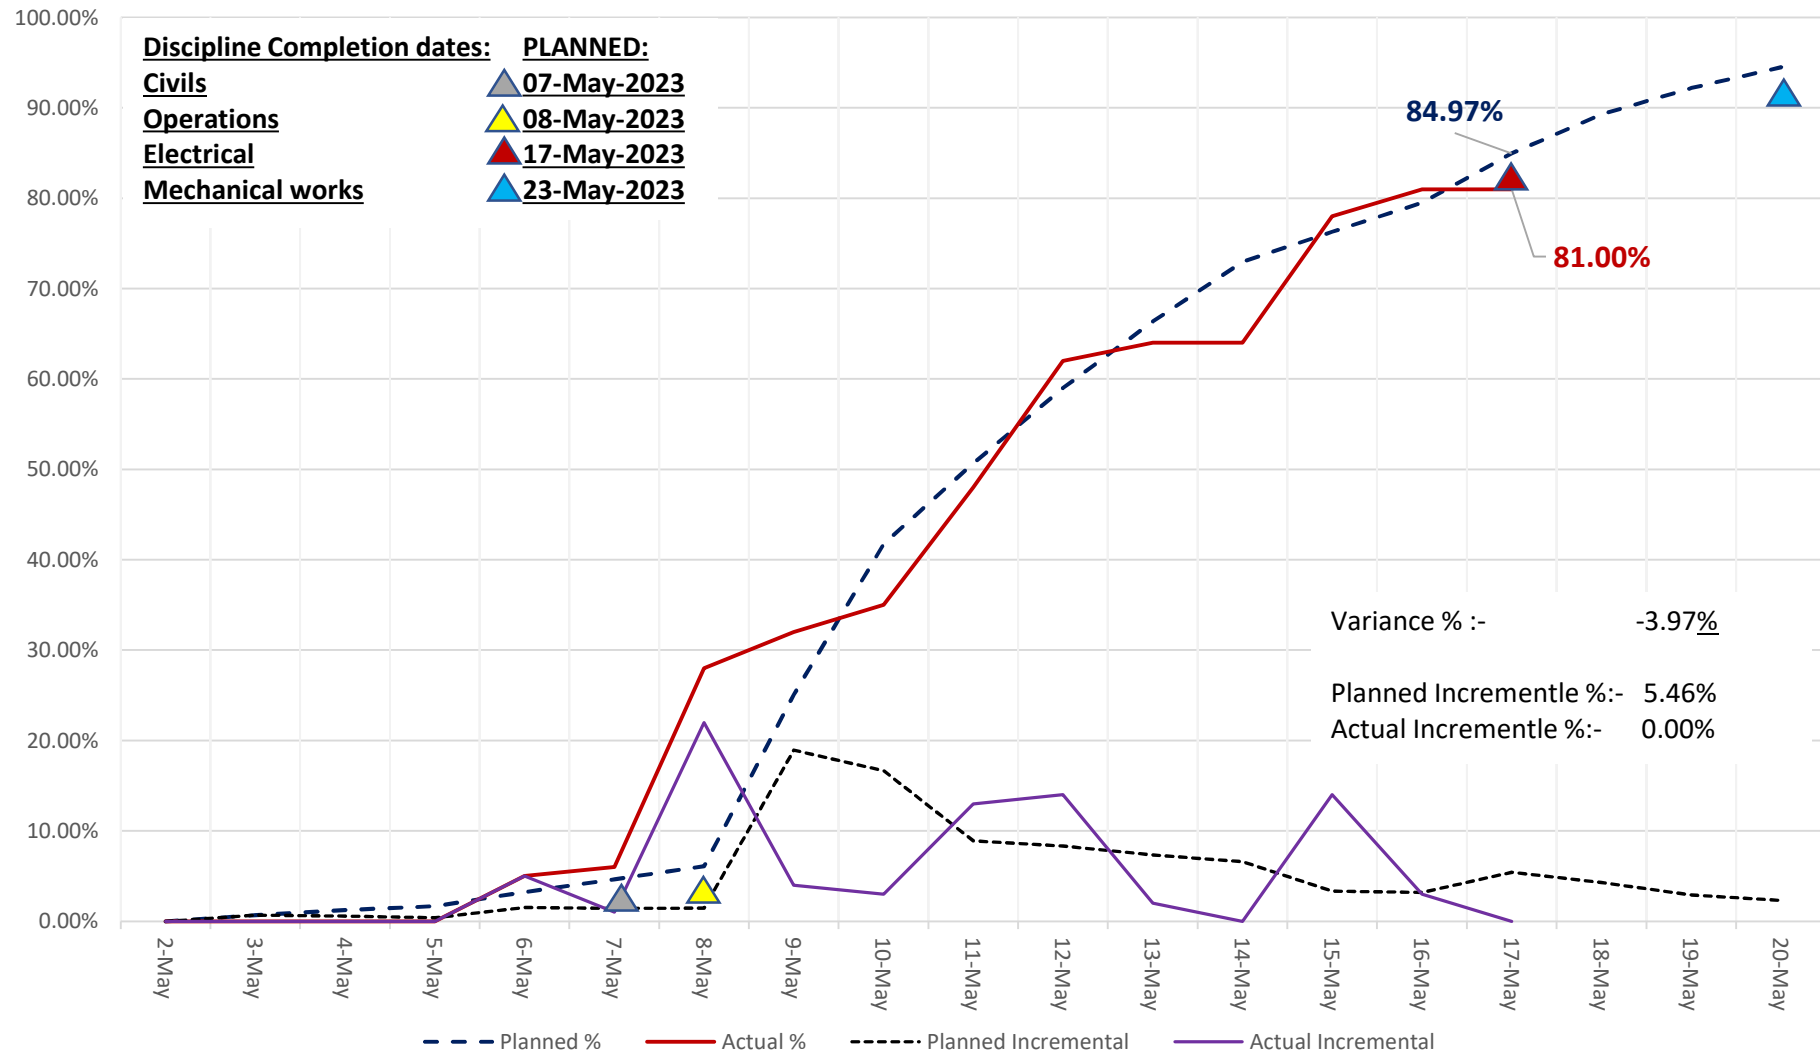




BICARBONATE THICKENING:- Update 17 May 2023 - Rev 02

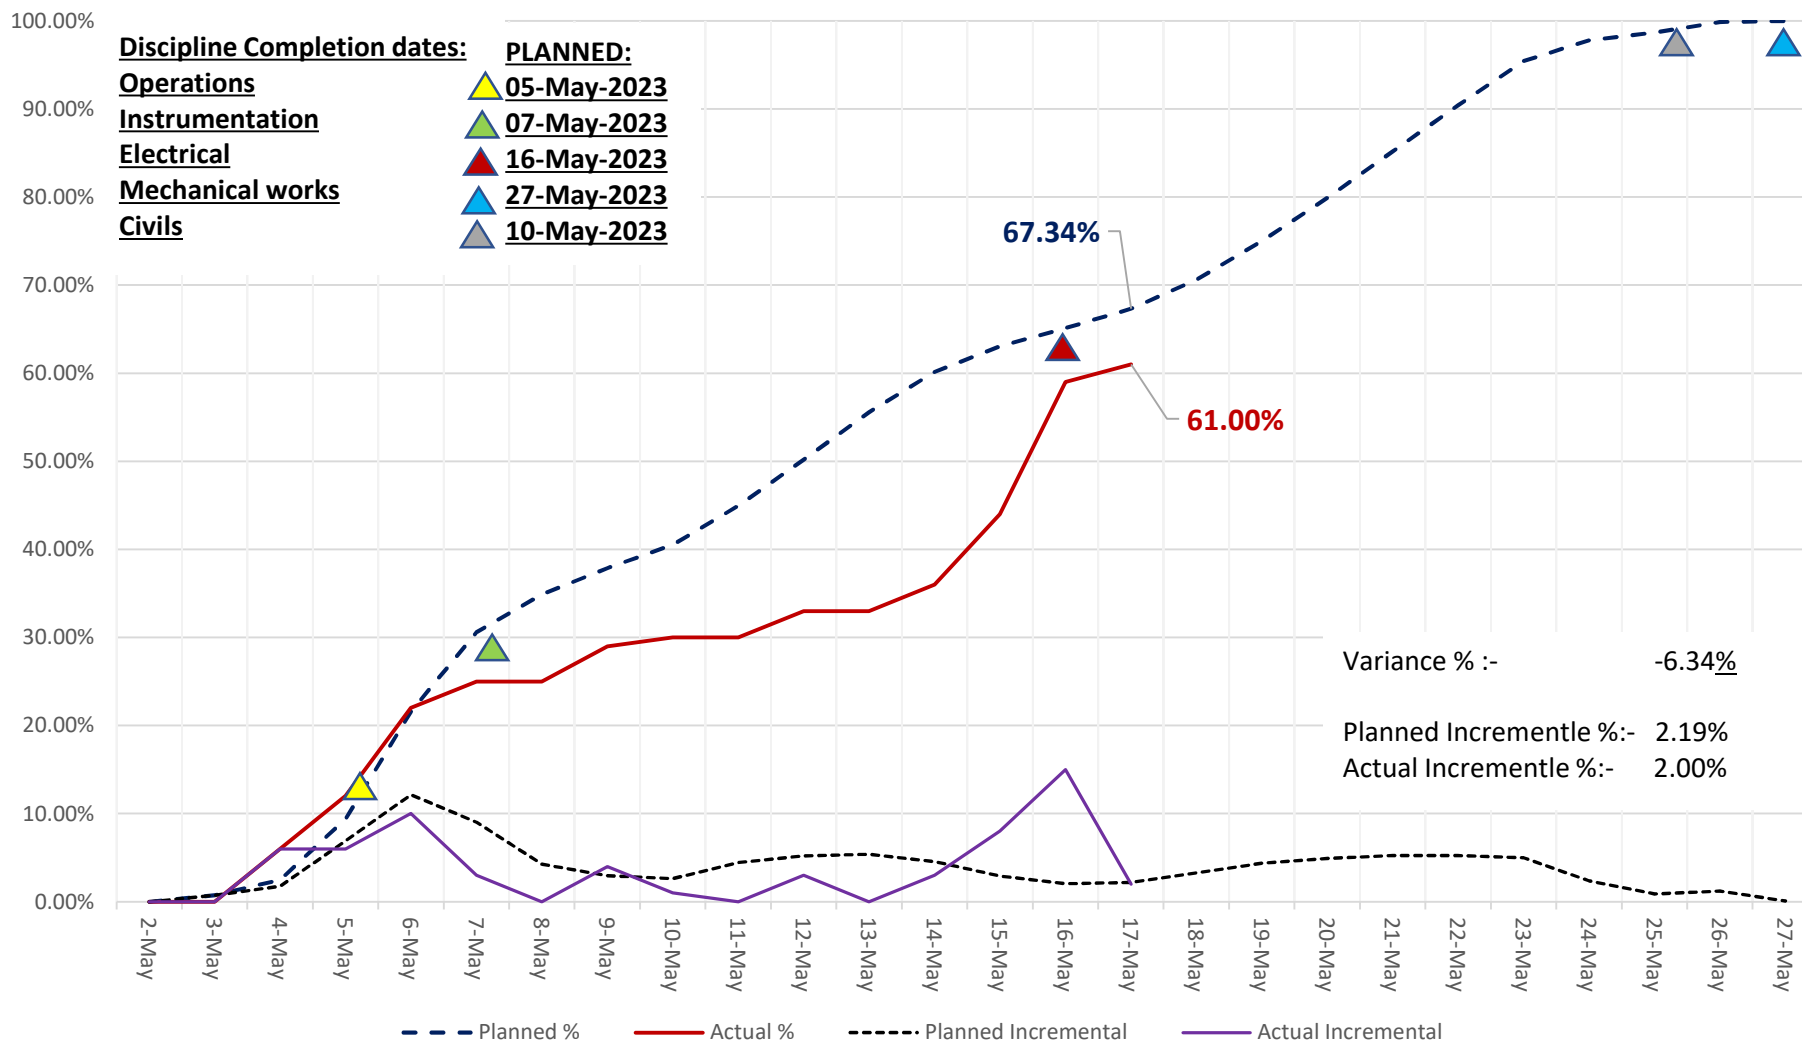




BICARBONATE FILTRATION A LINE:- Update 17 May 2023 - Rev 02

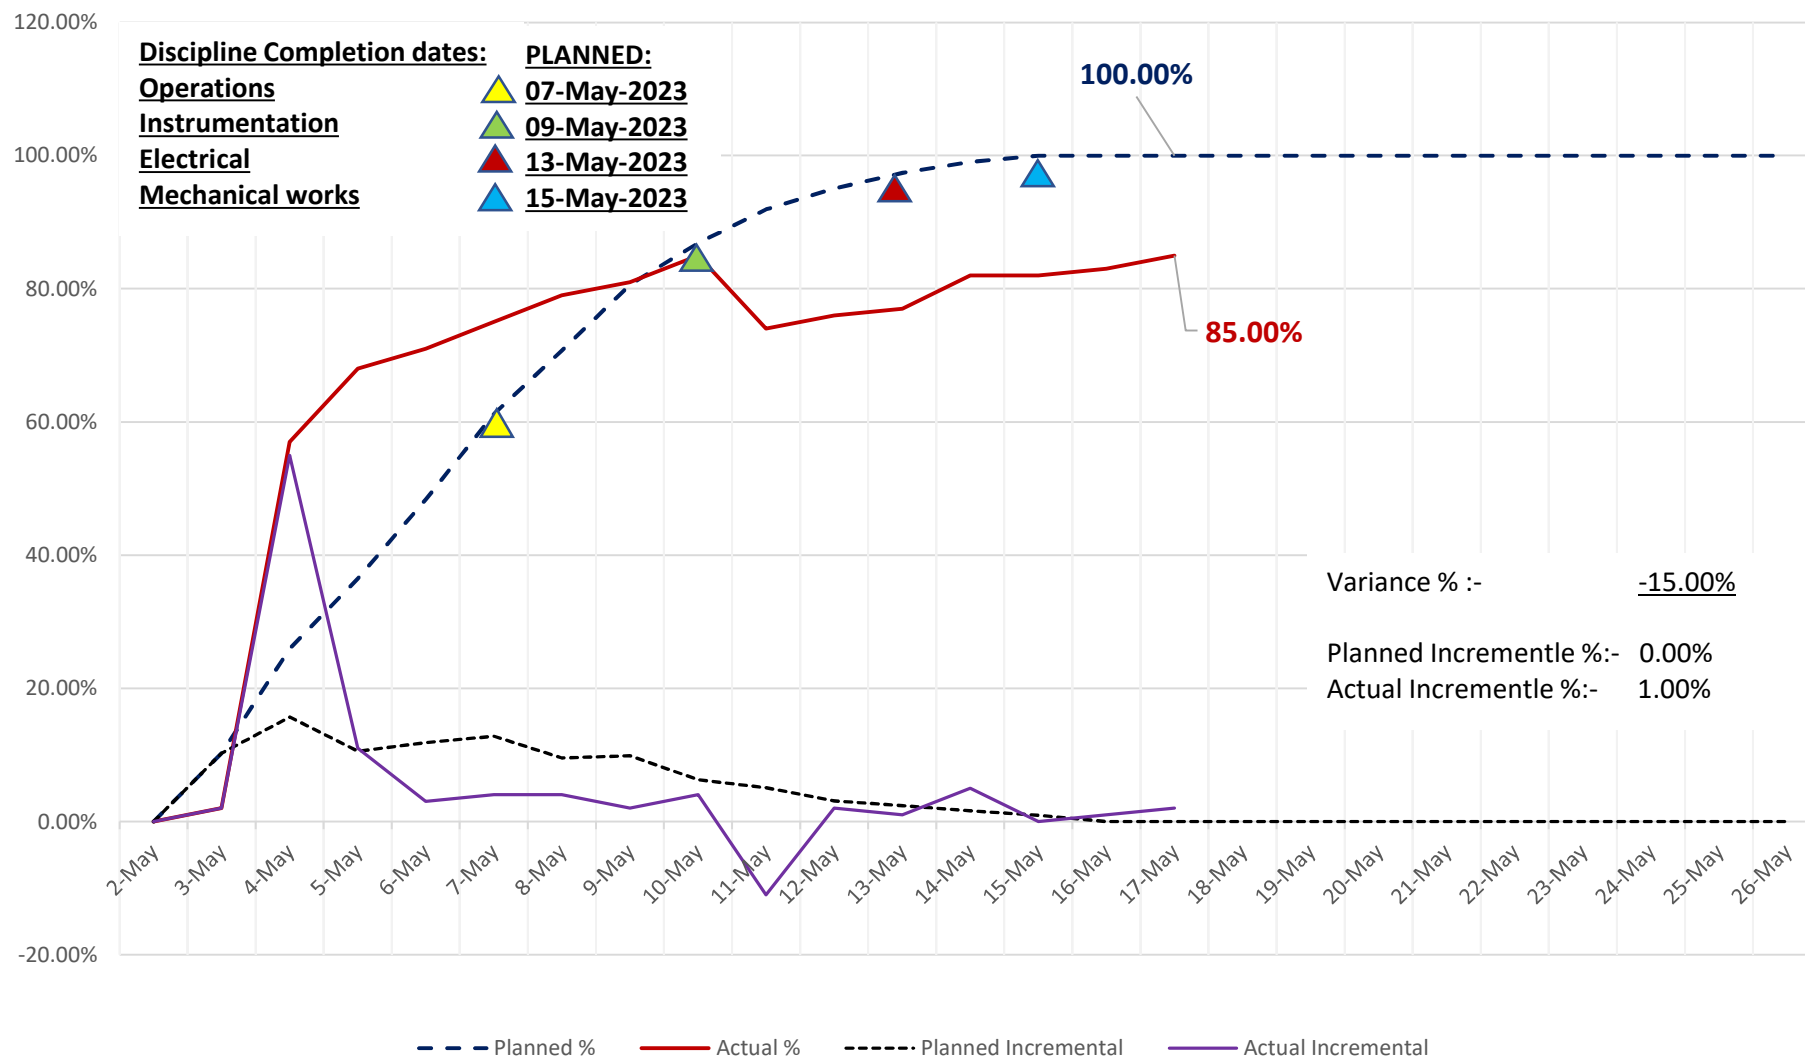




BICARBONATE FILTRATION B LINE:- Update 17 May 2023 - Rev 02

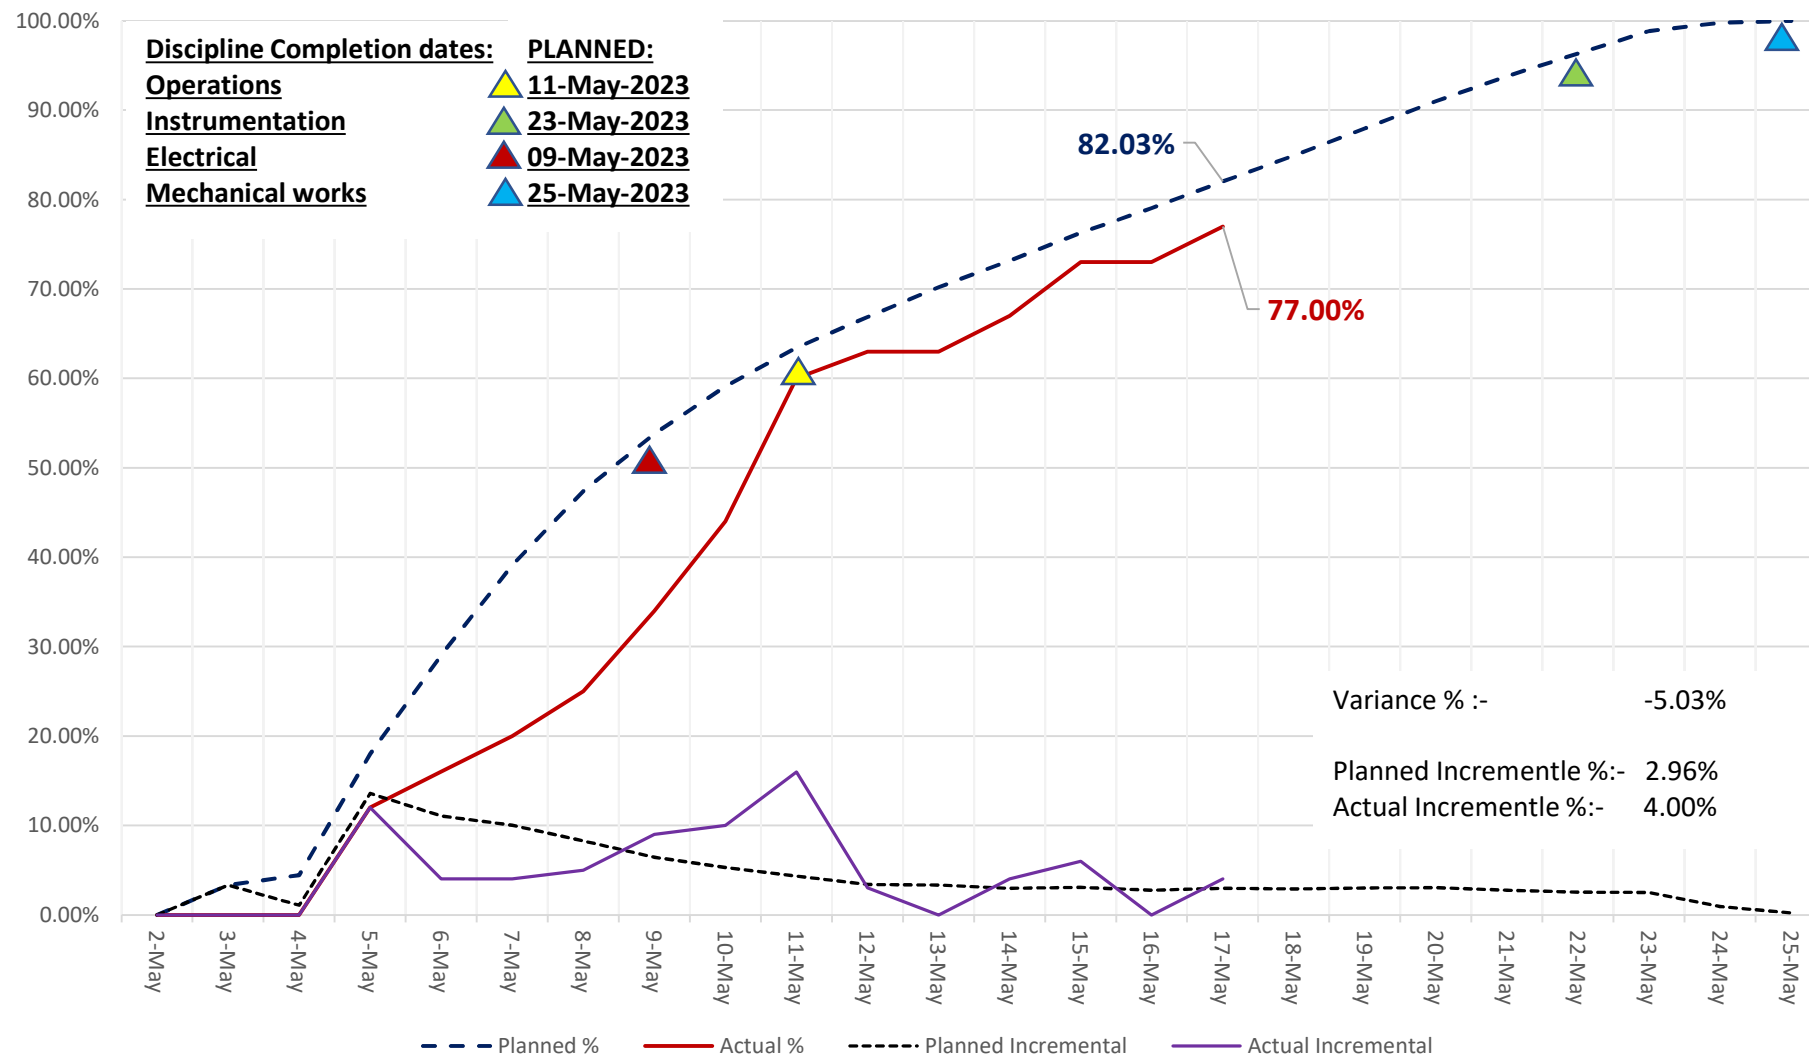




CALCINER - A LINE:- Update 17 May 2023 - Rev 02

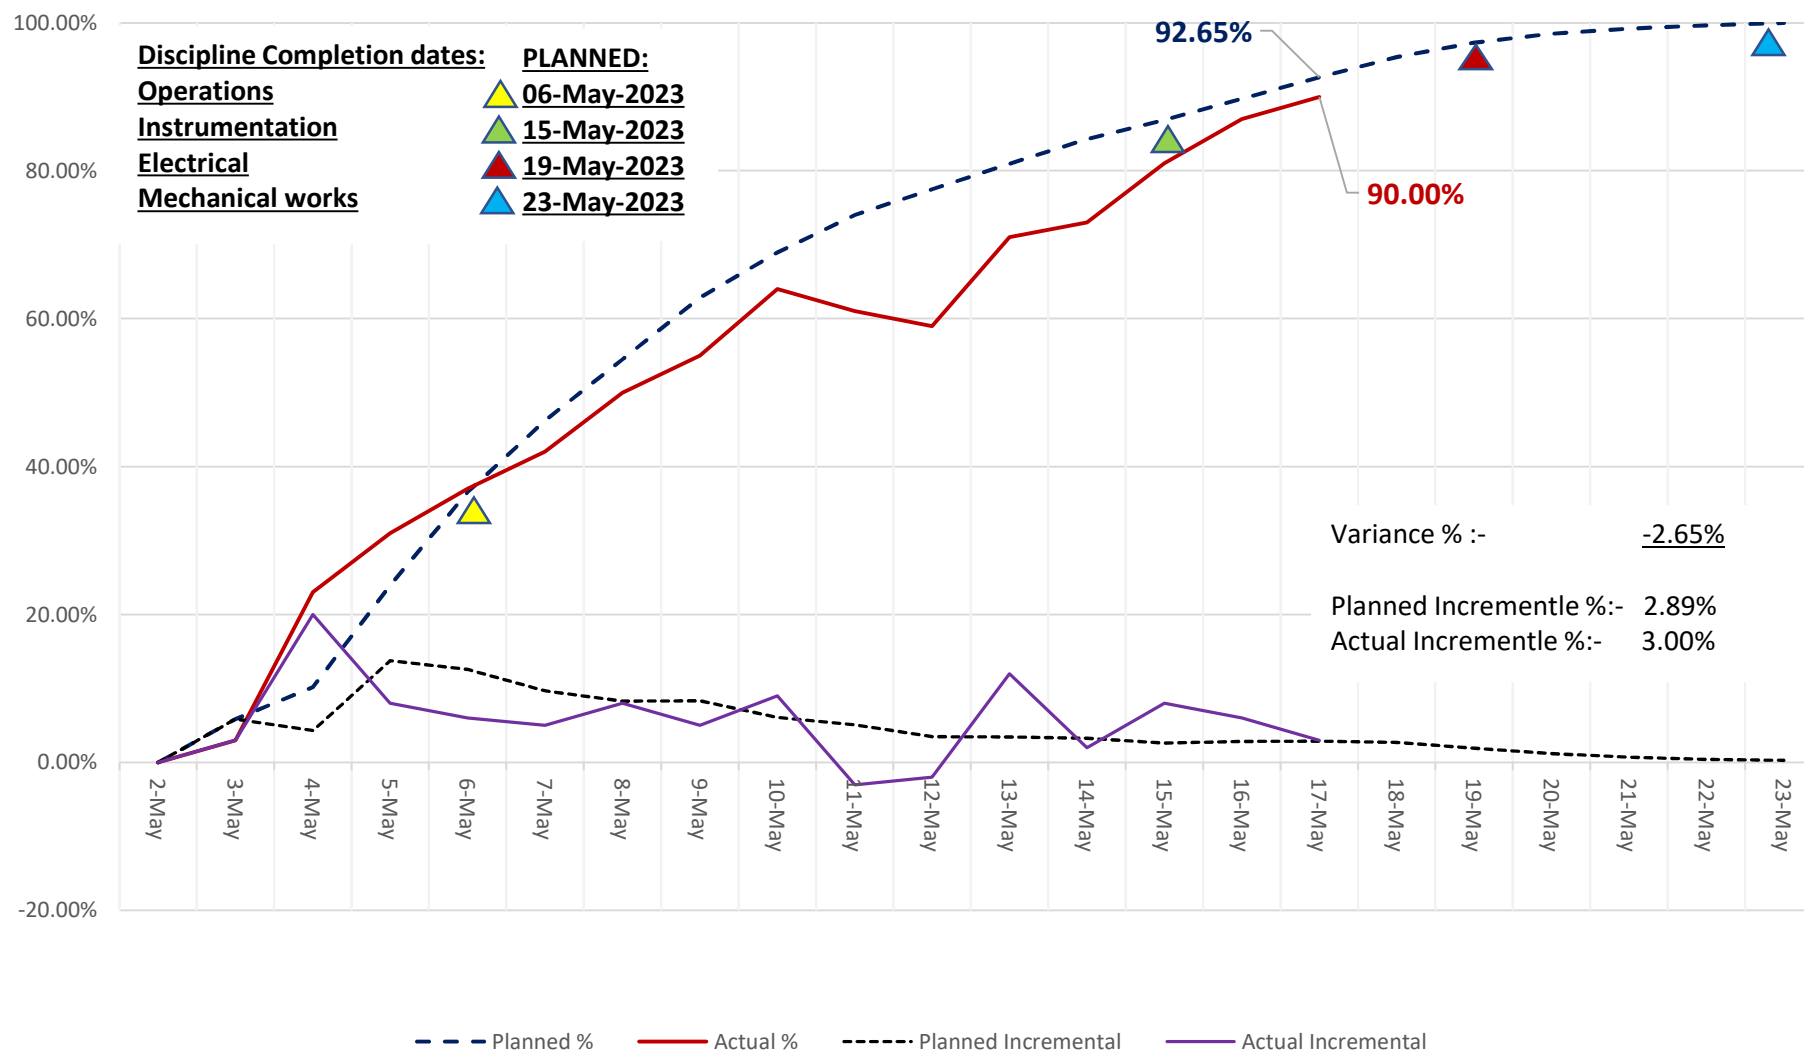




CALCINER - B LINE:- Update 17 May 2023 - Rev 02

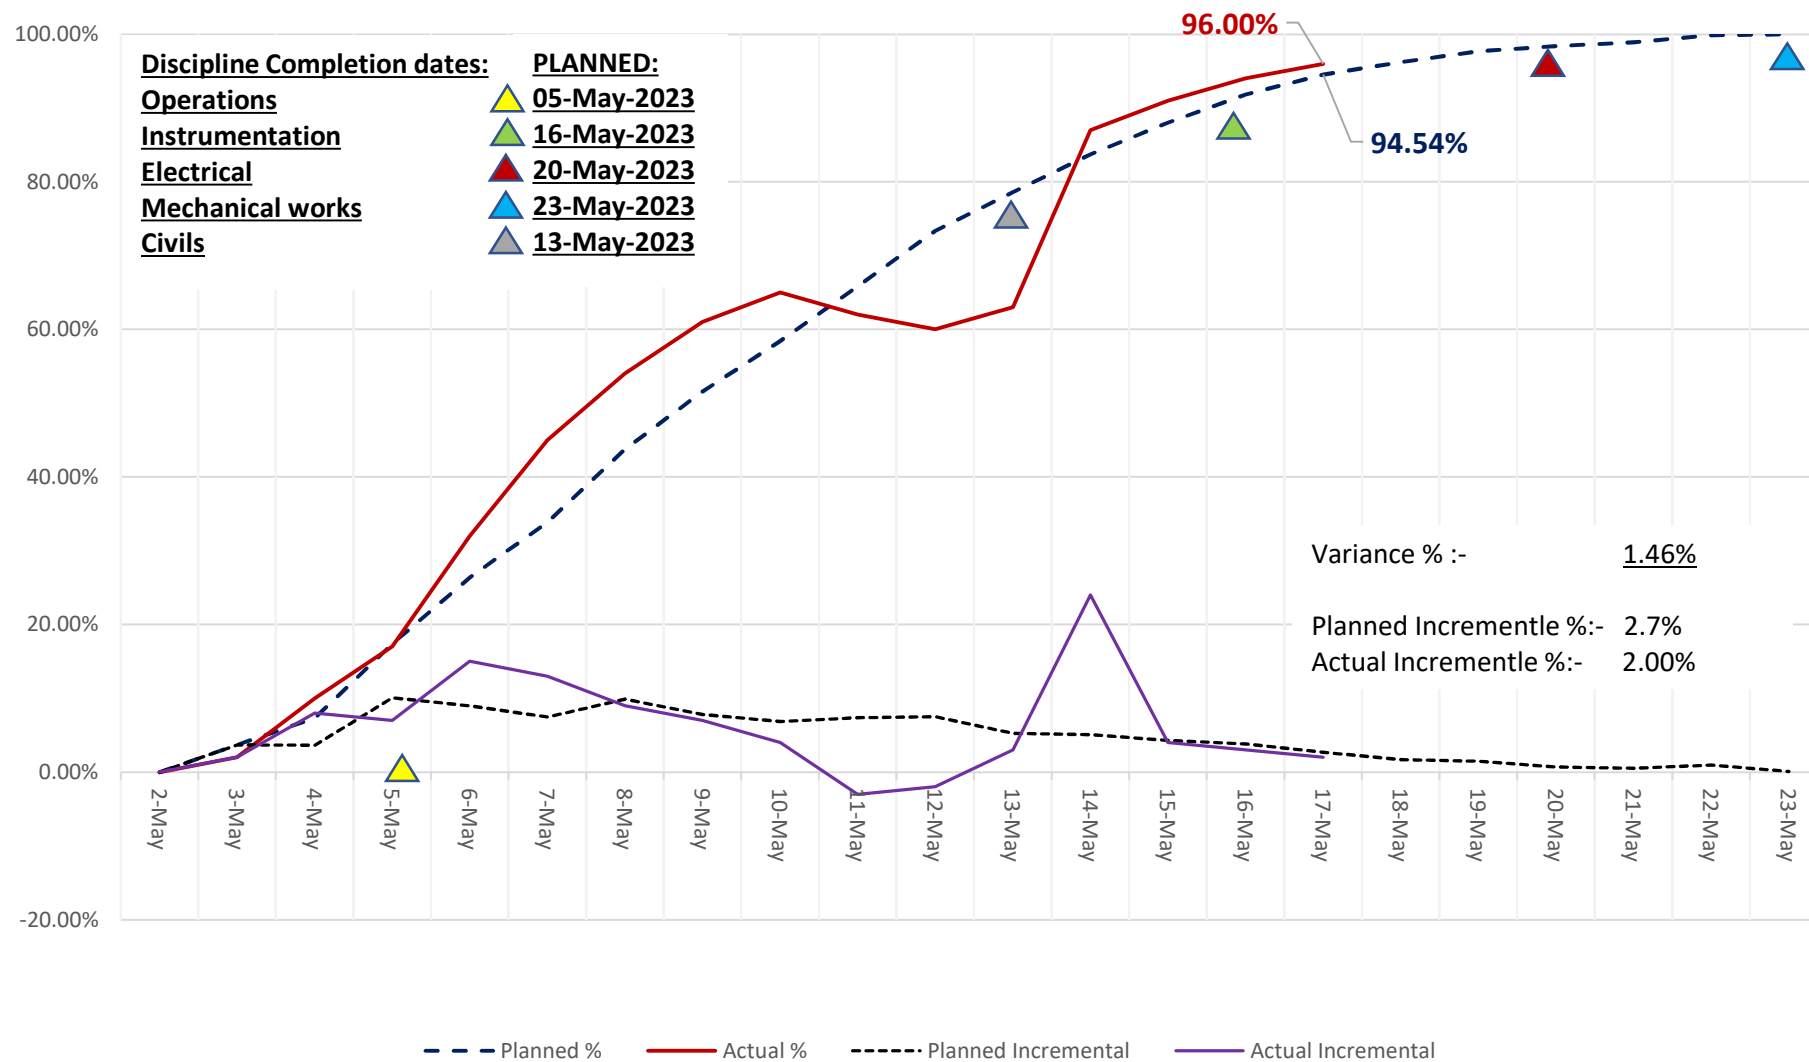

Progress			Incremental	
Planned	Actual	Variance	Planned	Actual
96.24%	0.00%	-96.24%	1.70%	0.00%




CALCINER GAS TREATMENT - A LINE:- Update 17 May 2023 - Rev 02

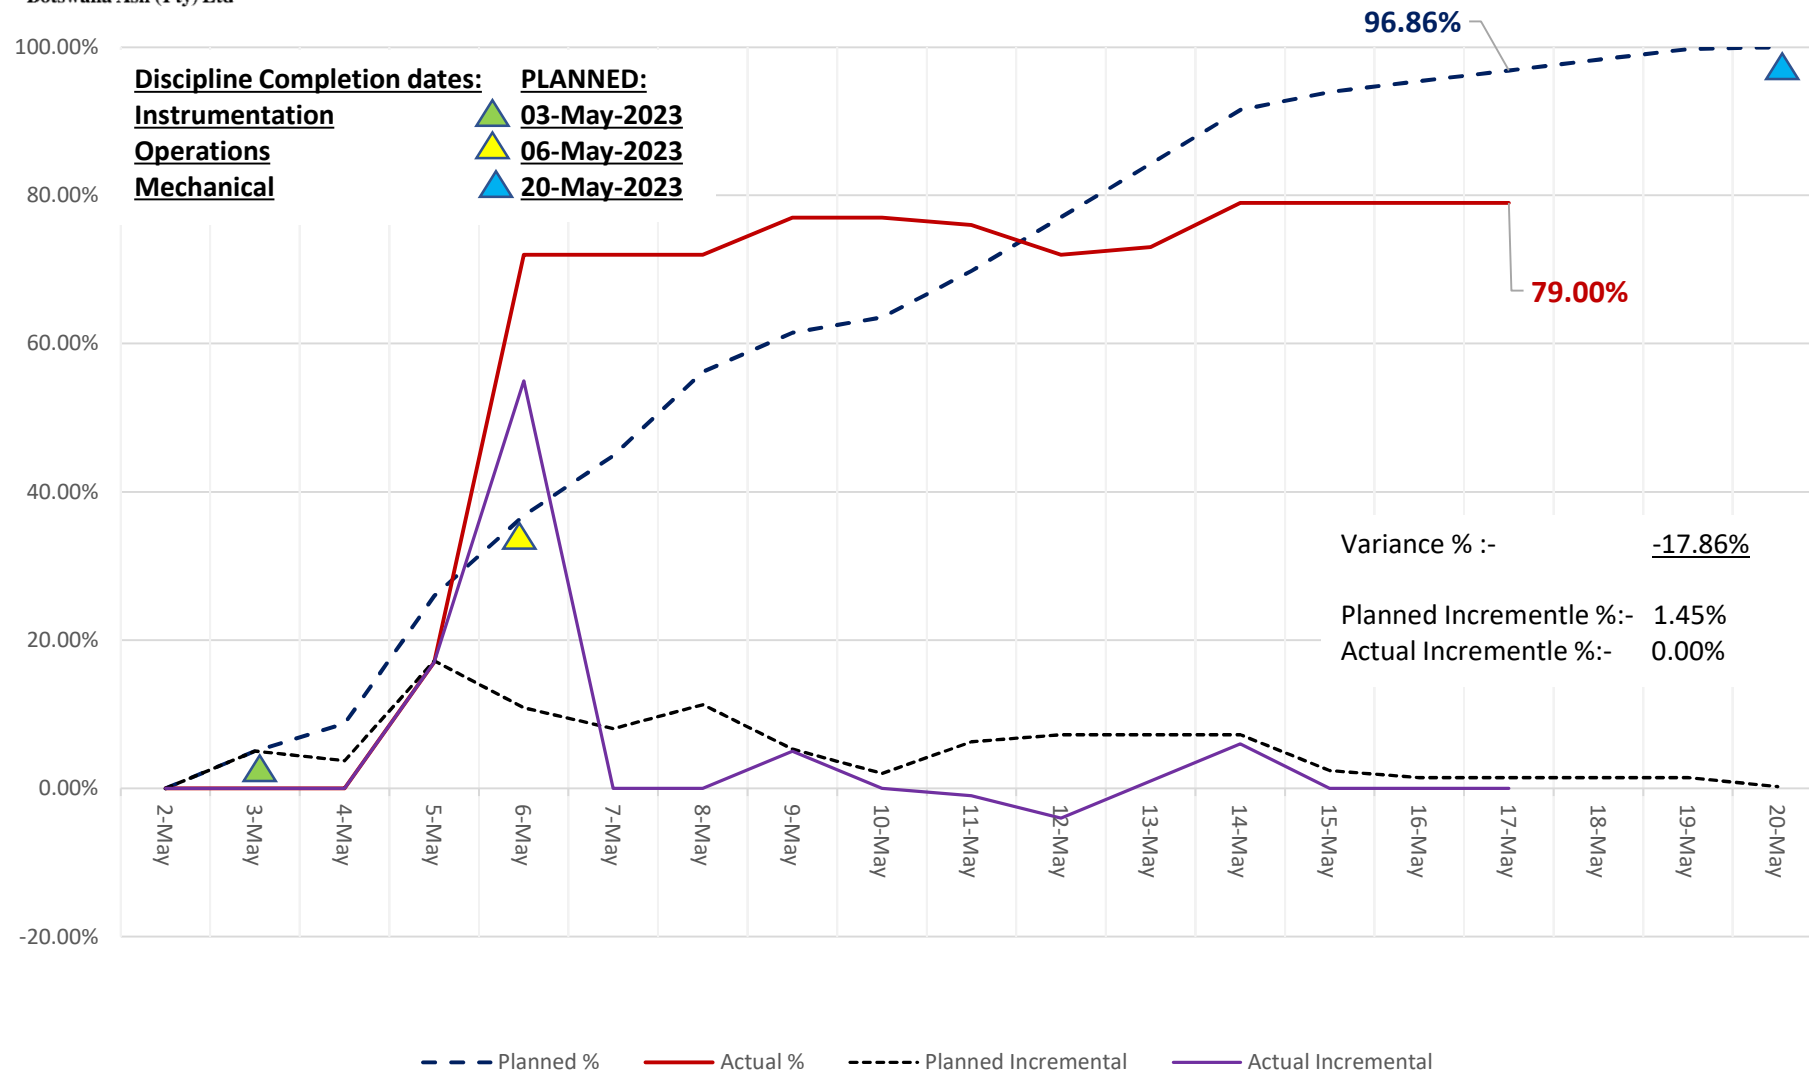

Progress			Incremental	
Planned	Actual	Variance	Planned	Actual
98.31%	0.00%	-98.31%	1.45%	0.00%




CALCINER GAS TREATMENT - B LINE:- Update 17 May 2023 - Rev 02

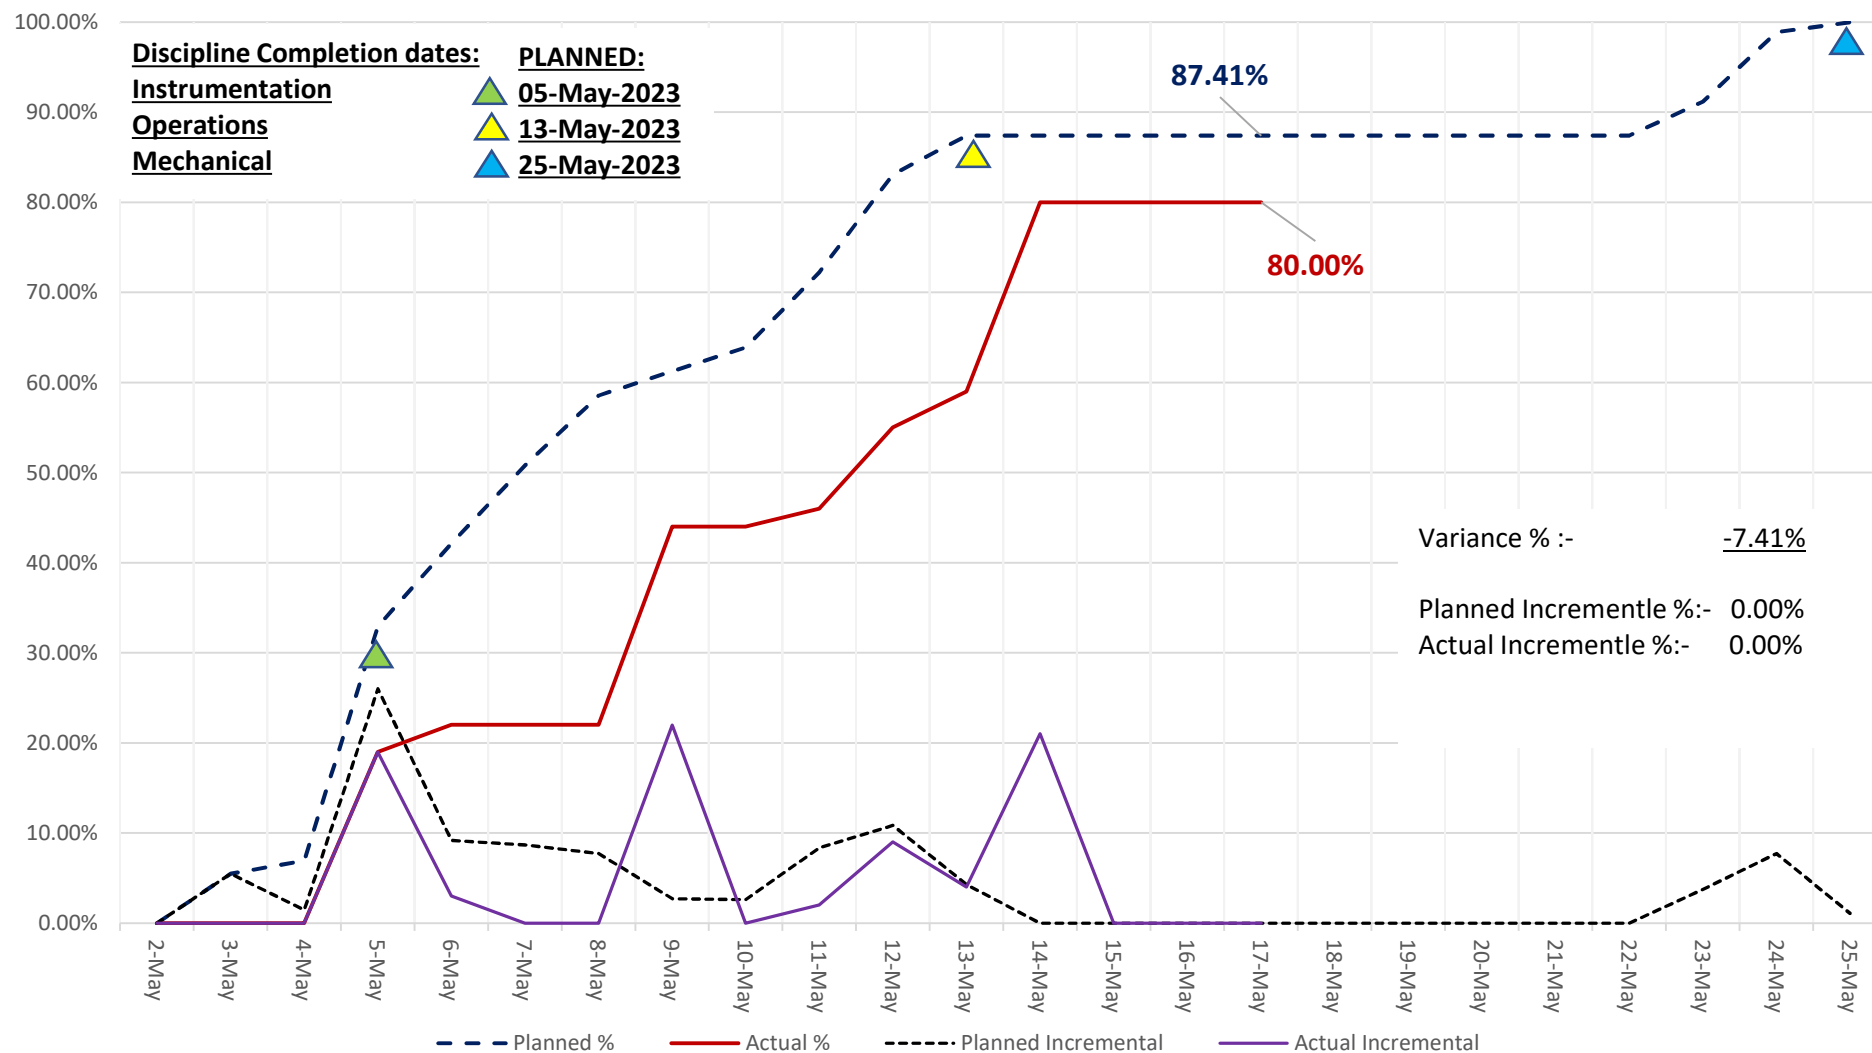





COMPACTION - A LINE:- Update 17 May 2023 - Rev 02

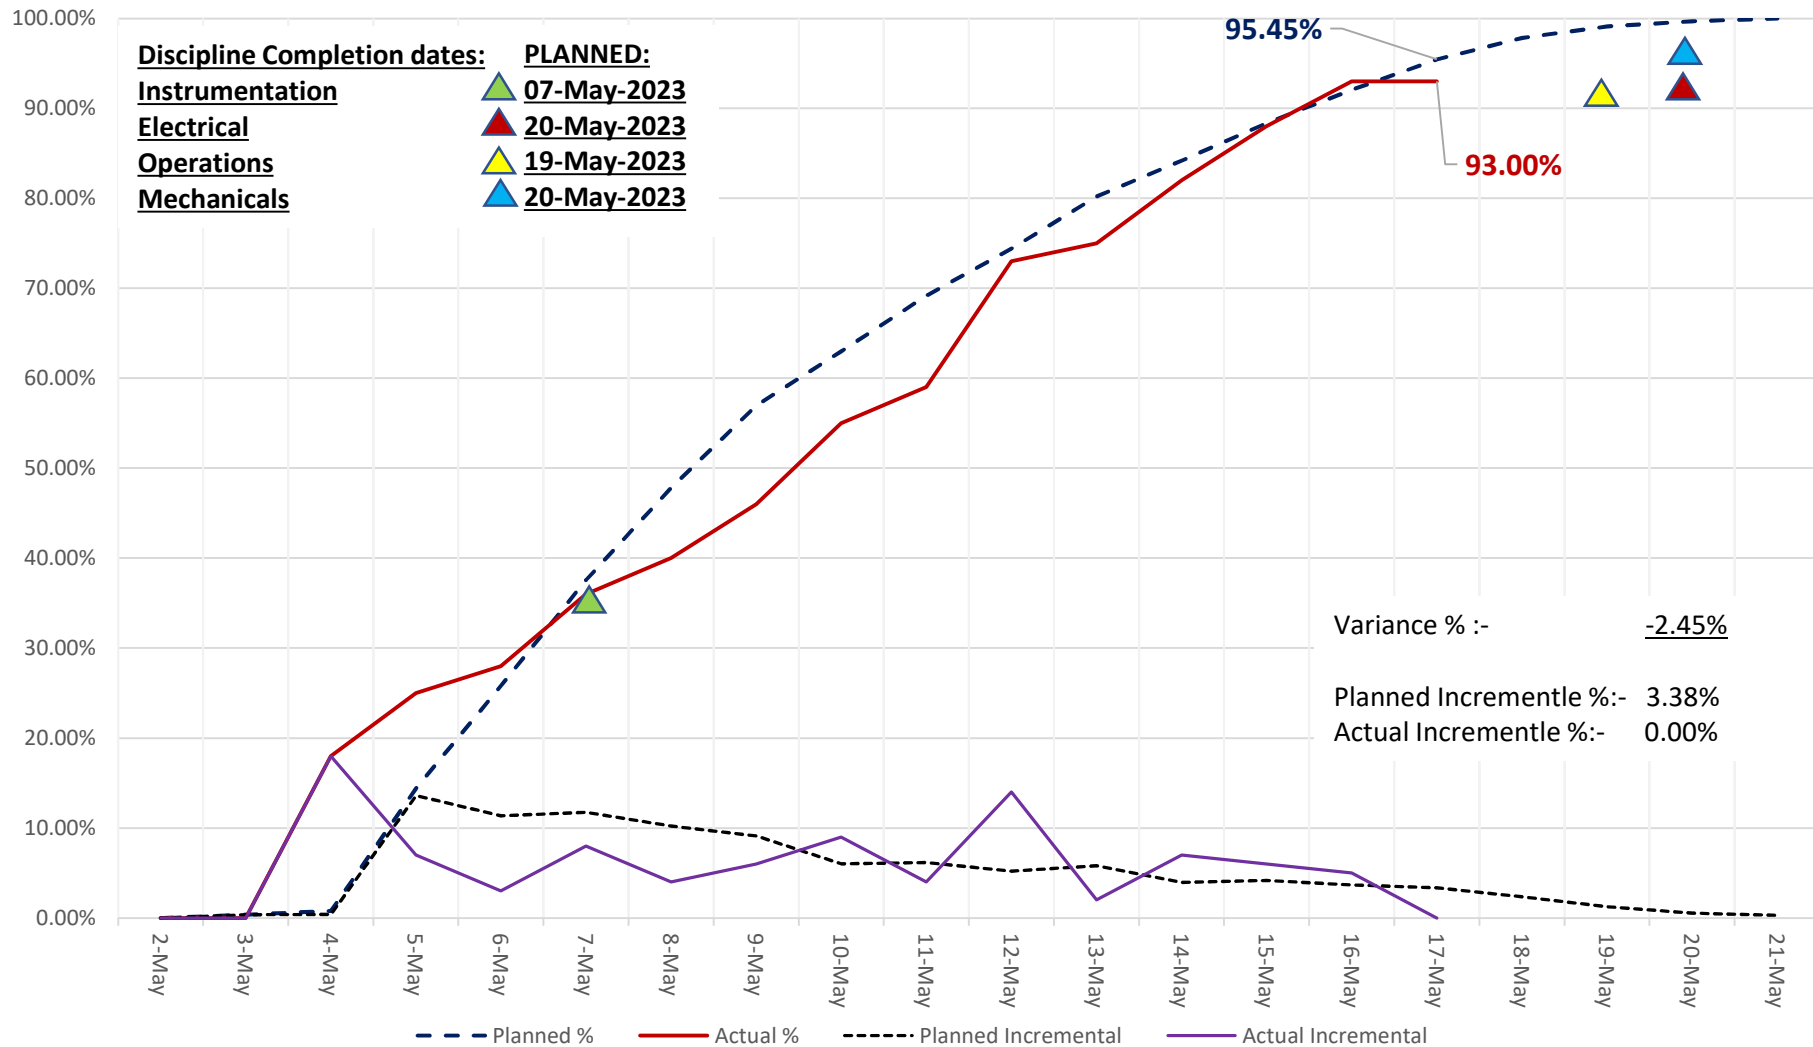

Progress			Incremental	
Planned	Actual	Variance	Planned	Actual
97.84%	0.00%	-97.84%	2.38%	0.00%




COMPACTION - B LINE:- Update 17 May 2023 - Rev 02

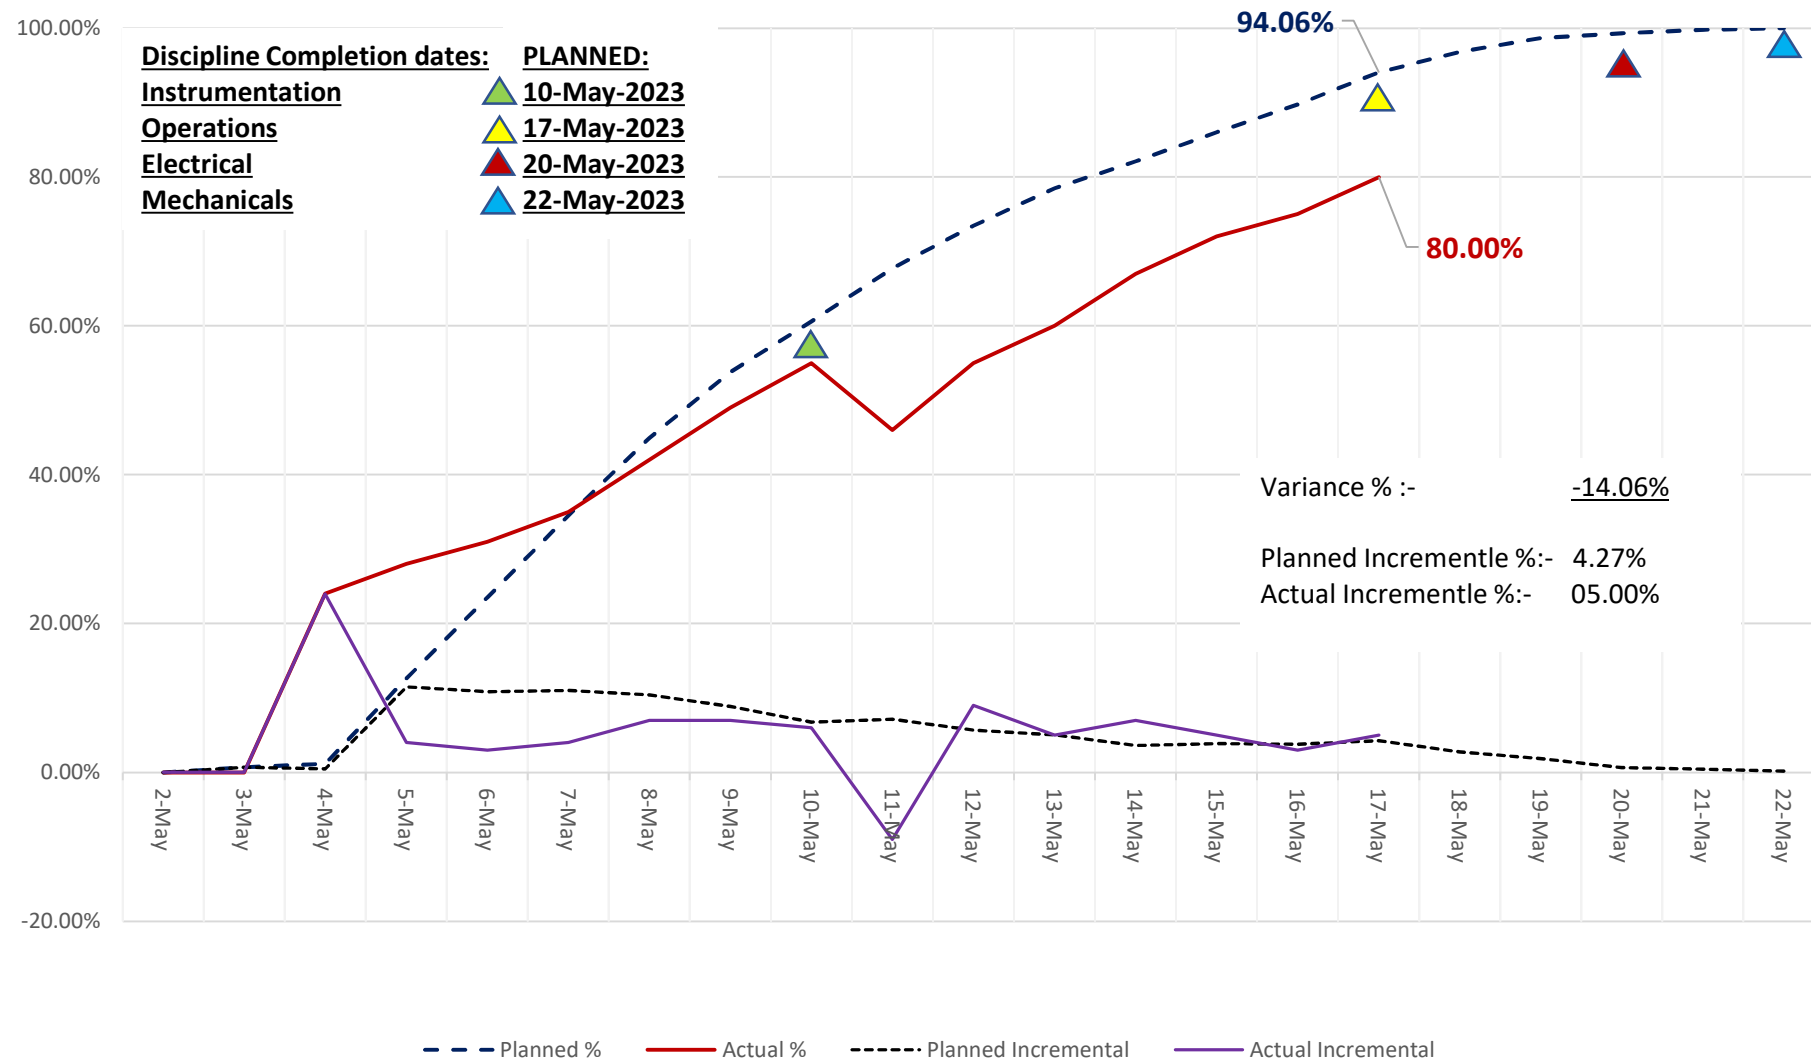




DENSE SODA ASH STORAGE:- Update 17 May 2023 - Rev 02

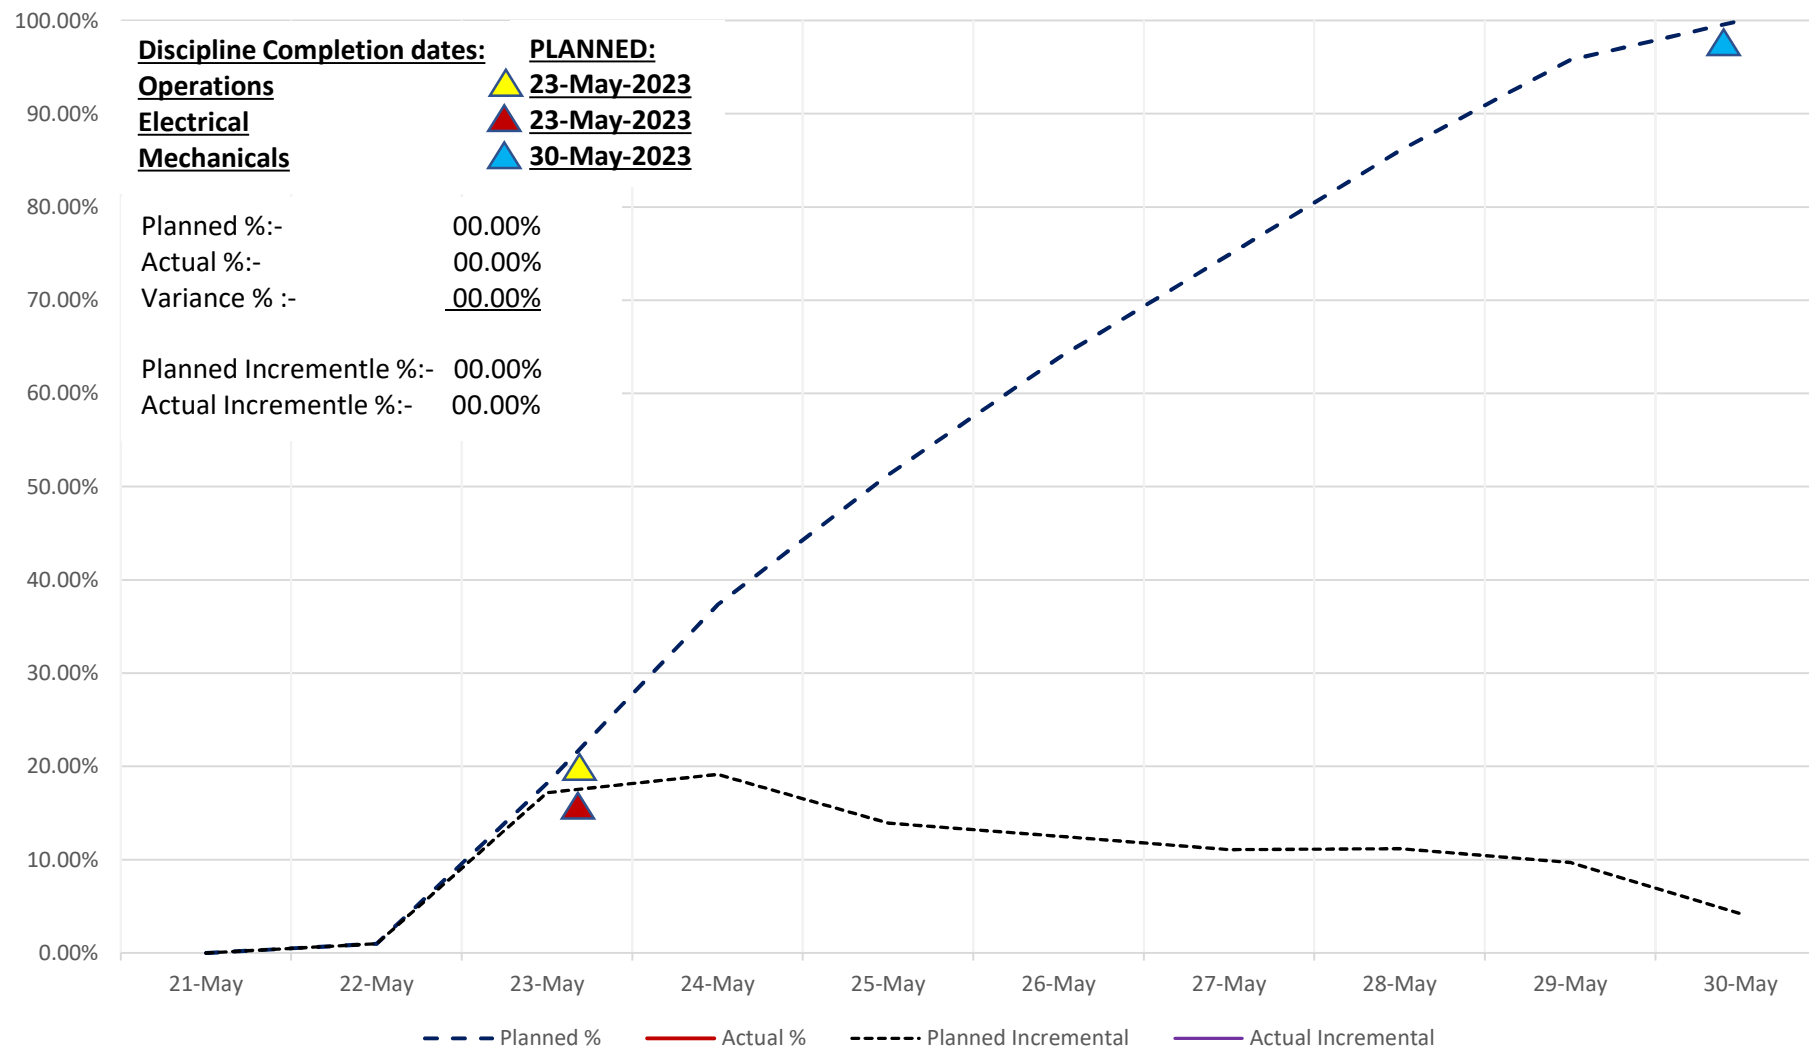

Progress			Incremental	
Planned	Actual	Variance	Planned	Actual



DENSE SODA ASH BAGGING:- Update 17 May 2023 - Rev 02

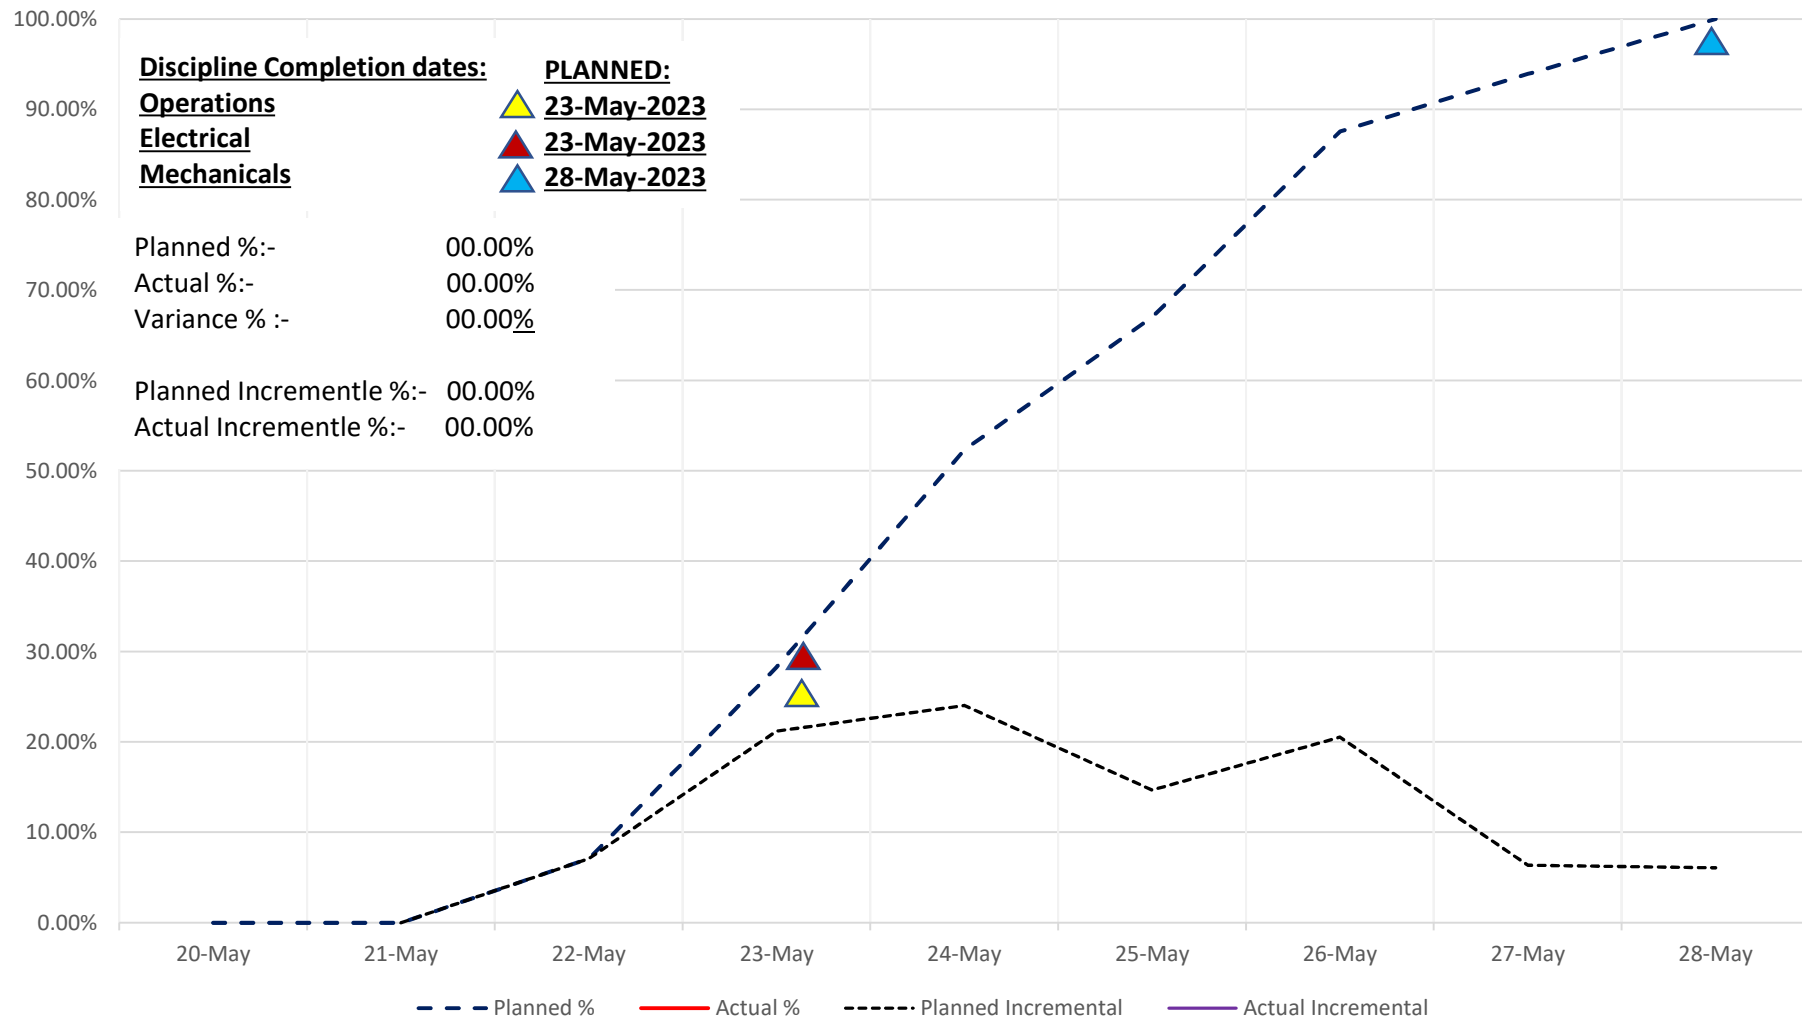

Progress			Incremental	
Planned	Actual	Variance	Planned	Actual
