
SALT PLANT DAS

SALT PLANT DASHBOARD

Drafted by: Slingsho	ot Consultancy
STATUS DATE:	9-May-23

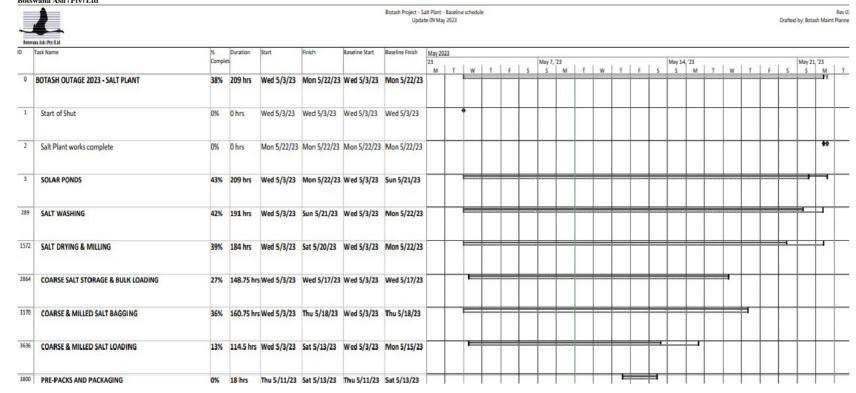

lotswana As	sh (Pty) Lti	1							Up	dat	e:-	09 I	May	20	<u>23</u>										
00.00%	KEY	MILEST	ONE	<u>S:</u>				PLA	NNE	<u>):</u>				- 525							e) - 105,40 e - 1	Δ	<u>^</u>		
90.00%	Dryin	ning Sa	Milli	ng Pla		_	- 4	24-	May-	2023			,,,												
80.00%	Coars	lemen se Salt Salt Ba	Bagg	ing -	er Sta	rt up	Z	241	May-2 May 2 May-2	023		'													
70.00%			30		-				,	,															
60.00%								,	,'																
50.00%							,	,																	
40.00%						,	′																		
30.00%					,	1													nned 9				52.90%		
20.00%				1	/													200	ual %: iance				38.009 -14.90		
10.00%		/	6	~				••••										the state of the			nentle entle %		07.339 04.009		
0.00%		-5		in.	0	-	00	(0)	Le.			10	bet .	het.							2	- 2	2	- 2	
	2-May	з-Мау	4-May	5-May	6-May	7-May	8-May	9-May	10-May	11-May	12-May	13-May	14-May	15-May	16-May	17-May	18-May	19-May	20-Ma)	21-Ma)	22-May	23-May	24-May	25-May	

SALT PLANT KEY MILESTONES	PLANNED	FORECAST	Variance	DAY	'S TO TO	P 5 RISKS				
Solar Ponds ready	21-May-23	24-May-23	-3	СОМР	LETION					
Salt Drying & Milling ready	22-May-23	23-May-23	-1		1)	T-Brine				
Salt Washing ready	22-May-23	21-May-23	1		2)	Solar Pond excavation				
Coarse Salt storage & bulk loading	17-May-23	13-May-23	4		3)	Cooling Water tie in				
Coarse & Milled salt bagging	20-May-23	22-May-23	-2		4)	Quality				
Coarse & Milled salt Loading	21-May-23	26-May-23	-5		5) Feeders & Screens					
Drying & Milling start up	22-May-23	26-May-23	-4							
					Planned %	Actual %				
PLANT SUB-AREA:		Planned	Actual	Variance	Increment	Increment	Risk			
SALT PLANT (Total)		45.57%	38.00%	-7.57%	8.17%	4.00%				
Solar Ponds		68.66%	43.00%	-25.66%	8.88%	5.00%				
Salt Washing		32.68%	42.00%	9.32%	8.80%	5.00%				
Salt Drying & Milling		43.87%	39.00%	-4.87%	11.18%	3.00%				
Coarse Salt Storage & Bulk Loading		3.58%	27.00%	23.42%	0.00%	5.00%				
Coarse & Milled Salt Bagging		53.27%	36.00%	-17.27%	8.45%	6.00%				
Coarse & Milled Salt Loading		74.91%	13.00%	-61.91%	8.60%	0.00%				
Pre-Packs & Packaging		0.00%	0.00%	0.00%	0.00%	0.00%				

LOOK AHEAD SCOPE OF WORKS	POSSIBLE RISKS	MITIGATIONS ON RISKS
Solar Ponds cleaning	Excavations	Close monitoring
PS7, ST1 & 2 Insp flush line		
T-Brine Line Valves	Critical	Close monitoring
ST1 & 2(N&S) Remove & Overhaul		
pumps		
Road hopper pump & Pipes lines		
Vibrating feeders & Scalping screen	Repairs	Prioritise
Discharge belt & Yard feed conveyors		
Single Boom stackers		
Side Arm reclaimer		
Wash Tanks		
T-Brine heat exchanger pipes	Critical	Close monitoring
Bucket elevator		
#1, 2 & 3 Wash Tanks - Rubber linings		
Electrical maint - Cyclone Pumps		
Coal handling conveyors structures	Sandblasting	Proper interface with others
Salt & Drying - cleaning silos 1, 2, 3		
Salt screens		
Feed conveyors		
Vibrator Distributors		
Coarse & Milles Salt Plant cleaning		
Civils - Raod hopper works		
